APPENDIX A
BORING AND WELL CONSTRUCTION LOGS

REVISED DRAFT
REMEDIAL INVESTIGATION REPORT
Capital Industries, Inc.
5801 3rd Avenue South
Seattle, Washington

Farallon PN: 457-004

FARALLON CONSULTING
975 5th Avenue Northwest
Issaquah, WA 98027

USCS Classification and Graphic Legend

Major Divisions			USCS Graphic Symbol	USCS Letter Symbol	Lithologic Description
Coarse-Grained Soil (More than 50% of material is larger than No. 200 sieve size)	GRAVEL AND GRAVELLY SOIL (More than 50% of coarse fraction retained on No. 4 sieve)	CLEAN GRAVEL (Little or no fines)		GW	Well graded GRAVEL, well graded GRAVEL with sand
				GP	Poorly graded GRAVEL, GRAVEL with sand
		GRAVEL WITH FINES (Appreciable amount of fines)		GP-GM	Poorly graded GRAVEL - GRAVEL with sand and silt
				GM	Silty GRAVEL
				GC	Clayey GRAVEL
	SAND AND SANDY SOIL (More than 50% of coarse fraction passed through No. 4 sieve)	CLEAN SAND (Little or no fines)		SW	Well graded SAND
				SP	Poorly graded SAND
		SAND WITH FINES (Appreciable amount of fines)		SP-SM	Poorly graded SAND - silty SAND
				SM	Silty SAND
				SC	Clayey SAND
				SM-ML	SILT - Silty SAND
Fine-Grained Soil (More than 50% of material is smaller than No. 200 sieve size)	SILT AND CLAY (Liquid limit less than 50)			ML	SILT
				CL	CLAY
				OL	Organic SILT
	SILT AND CLAY (Liquid limit greater than 50)			MH	Inorganic SILT
				CH	Inorganic CLAY
				OH	Organic CLAY
		Highly Organic Soil		PT	Peat
OTHER MATERIALS	PAVEMENT			AC	Asphalt concrete
				CO	Concrete
	OTHER			RK	Bedrock
				WD	Wood Debris
				DB	Debris (Miscellaneous)
				PC	Portland cement

Legend

- Sample Interval
- G — Grab Sample Interval
- Water level at time of drilling
- Water level at time of sampling
- Blank Casing
- Screened Casing
- Cement Grout
- Bentonite
- Sand Pack
- Well Cap
- _____ Solid line indicates sharp contact between units well defined.
- - - - - - Dashed line indicates gradational contact between units.

feet bgs = feet below ground surface
NE = Not Encountered
NA = Not Applicable
PID = Photoionization Detector
PN = Project Number
*ppm = parts per million total organic vapors in isobutylene equivalents using a 10.6 electron volt lamp
USCS = Unified Soil Classification System

PARALLON CONSULTING
320 3rd Avenue NE
Issaquah, WA 98027

Log of Boring: B-1

ient: Capital Industries
oject: Capital Industries
cation: Seattle, Washington
rallon PN: 457-001
gged By: T. Mulhern

Date/Time Started:	1/16/06 0900	**Sampler Type:**	Geoprobe
Date/Time Completed:	1/16/06 1115	**Drive Hammer (lbs.):**	N/A
Equipment:	Geoprobe	**Depth of Water ATD (ft bgs):**	8
Drilling Company:	Cascade Drilling	**Total Boring Depth (ft bgs):**	34
Drilling Foreman:	Kasey	**Total Well Depth (ft bgs):**	N/A
Drilling Method:	Direct Push		

Sample Interval	Lithologic Description	USCS	USGS Graphic	% Recovery	Blow Counts 8/8/8	PID (ppm)	Sample ID	Sample Analyzed	Well Construction Details
	Clear for utilities using vac-truck to 5.5'-6'								
	6'-8.5' Sandy SILT, fine grained, medium brown, wet to saturated, stiff, no odor.	ML							
	SAND, minor silt, fine grained, dark gray, saturated, dense, no odor.	SP		100		10.9	B1-9.5-10	X	▽
	Collect reconnaissance groundwater sample from 10'-14', water is cloudy, light brown.						B1-10	X	
				100		12.2	B1-13.5-14		Temporary Well Screen
	Becomes fine to medium grained sand, trace wood at 17'-18', 2" layer of silt at 16'. Collect reconnaissance groundwater sample from 14'-18', water is cloudy, light gray.						B1-14	X	
				100		7.2	B1-16.5-17		
							B1-17		
	Becomes fine grained, minor wood at 18'-18.5'. Collect reconnaissance groundwater sample from 18'-22', water is cloudy, light gray.						B1-18	X	

nent Type: N/A
l Diameter (inches): N/A
l Slot Size (inches): N/A
ed Interval (ft bgs): N/A

Well Construction Information

Filter Pack: N/A
Surface Seal: N/A
Annular Seal: N/A

Ground Surface Elevation (ft): N/A
Top of Casing Elevation (ft): N/A
Boring Abandonment: Bentonite
Surveyed Location: X: N/A Y: N/A

FARALLON CONSULTING
320 3rd Avenue NE
Issaquah, WA 98027

Log of Boring: B-1

Sample Interval	Lithologic Description	USCS	USGS Graphic	% Recovery	Blow Counts 8/8/8	PID (ppm)	Sample ID	Sample Analyzed	Well Construction Details
	No wood. Collect reconnaissance groundwater sample from 22'-26', water is cloudy, light gray.			100		10.2	B1-21.5-22		
							B1-22	X	
	Becomes very fine grained.			100		34.2	B1-25.5-26		
	Sandy SILT, fine grained, medium gray, saturated, stiff, no odor, becomes SILT, trace fine sand at 27'. Collect reconnaissance groundwater sample from 26'-30', water is slightly cloudy, light gray.	ML					B1-26	X	
				100		174	B1-29.5-30		
	Collect reconnaissance groundwater sample from 30'-34', water is cloudy, light gray.						B1-30	X	
	Silty SAND, fine grained, minor woor, dark gray, saturated, dense, no odor.	SP		100		210	B1-33.5-34	X	

Well Construction Information

nent Type:	N/A	Filter Pack:	N/A	Ground Surface Elevation (ft):	N/A
l Diameter (inches):	N/A	Surface Seal:	N/A	Top of Casing Elevation (ft):	N/A
Slot Size (inches):	N/A	Annular Seal:	N/A	Boring Abandonment:	Bentonite
ed Interval (ft bgs):	N/A			Surveyed Location: X: N/A	Y: N/A

FARALLON CONSULTING
320 3rd Avenue NE
Issaquah, WA 98027

Log of Boring: B-2

ent: Capital Industries
oject: Capital Industries
cation: Seattle, Washington
rallon PN: 457-001
gged By: T. Mulhern

Date/Time Started:	1/17/06 0830	**Sampler Type:**	Geoprobe
Date/Time Completed:	1/17/06 1115	**Drive Hammer (lbs.):**	N/A
Equipment:	Geoprobe	**Depth of Water ATD (ft bgs):**	7.5
Drilling Company:	Cascade Drilling	**Total Boring Depth (ft bgs):**	34
Drilling Foreman:	Kasey	**Total Well Depth (ft bgs):**	N/A
Drilling Method:	Direct Push		

Sample Interval	Lithologic Description	USCS	USGS Graphic	% Recovery	Blow Counts 8/8/8	PID (ppm)	Sample ID	Sample Analyzed	Well Construction Details
	CONCRETE	CO							
	SAND, trace silt, fine grained, yellow-brown, moist, loose, no odor. Becomes dark brown, trace wood.	SP		100		18.4	B2-2.5-3	X	
	SILT, trace fine sand, medium gray, moist to wet, stiff, no odor.	ML		100		18.7	B2-5.5-6	X	
	SAND, minor silt, fine grained, dark gray, saturated, moderately dense, no odor, becomes trace silt at 8'.	SP							▽
	Collect reconnaissance groundwater sample from 10'-14', water is cloudy, light brown.			100		28.5	B2-10 B2-11.5-12	X	Temporary Well Screen
	Collect reconnaissance groundwater sample from 14'-18', water is cloudy, light gray.			100		22.4	– B2-14	X	
	Collect reconnaissance groundwater sample from 18'-22', water is cloudy, light gray.			75		35.1	B2-17.5-18 B2-18	X	

nent Type: N/A
Diameter (inches): N/A
Slot Size (inches): N/A
ed Interval (ft bgs): N/A

Well Construction Information

Filter Pack: N/A
Surface Seal: N/A
Annular Seal: N/A

Ground Surface Elevation (ft): N/A
Top of Casing Elevation (ft): N/A
Boring Abandonment: Bentonite
Surveyed Location: X: N/A Y: N/A

FARALLON CONSULTING
320 3rd Avenue NE
Issaquah, WA 98027

Log of Boring: B-2

Sample Interval	Lithologic Description	USCS	USGS Graphic	% Recovery	Blow Counts 8/8/8	PID (ppm)	Sample ID	Sample Analyzed	Well Construction Details
	Collect reconnaissance groundwater sample from 22'-26', water is cloudy, light gray.			80		76.1	B2-21.5-22		
							B2-22	X	
				90		76.8	B2-25.5-26		
	Collect reconnaissance groundwater sample from 26'-30', water is cloudy, light gray.						B2-26	X	
				100		320	B2-29.5-30		
	Collect reconnaissance groundwater sample from 30'-34', water is cloudy, light gray.						B2-30	X	
				100		310	B2-32.5-33	X	
	Silty SAND, very fine grained, dark to medium gray, wet, dense, no odor.	SM				997	B2-33.5-34	X	

Well Construction Information

nent Type:	N/A	Filter Pack:	N/A	Ground Surface Elevation (ft):	N/A
) Diameter (inches):	N/A	Surface Seal:	N/A	Top of Casing Elevation (ft):	N/A
ı Slot Size (inches):	N/A	Annular Seal:	N/A	Boring Abandonment:	Bentonite
ed Interval (ft bgs):	N/A			Surveyed Location: X: N/A	Y: N/A

PARALLON CONSULTING
320 3rd Avenue NE
Issaquah, WA 98027

Log of Boring: B-3

ient: Capital Industries
oject: Capital Industries
cation: Seattle, Washington
rallon PN: 457-001
gged By: T. Mulhern

Date/Time Started:	1/17/06 1130	**Sampler Type:**	Geoprobe
Date/Time Completed:	1/17/06 1350	**Drive Hammer (lbs.):**	N/A
Equipment:	Geoprobe	**Depth of Water ATD (ft bgs):**	8
Drilling Company:	Cascade Drilling	**Total Boring Depth (ft bgs):**	34
Drilling Foreman:	Kasey	**Total Well Depth (ft bgs):**	N/A
Drilling Method:	Direct Push		

Sample Interval	Lithologic Description	USCS	USGS Graphic	% Recovery	Blow Counts 8/8/8	PID (ppm)	Sample ID	Sample Analyzed	Well Construction Details
	Clear utilities using vac-truck to 5.5'-6'. Standing water in hole from vac-turck due to rain overnight.								
	SILT, minor fine grained sand, light brown with orange mottling, moist to wet, stiff, no odor.	ML		90		14.6	B3-8.5-9	X	▽
	SAND, minor silt, fine grained, medium to dark brown with rust mottling, saturated, no odor, becomes trace wood at 10'. Collect reconnaissance groundwater sample from 10'-14', water is cloudy, light brown.	SP					B3-10	X	
				90		96.1	B3-13.5-14		Temporary Well Screen
	Becomes trace silt, dark gray, no rust mottling, no wood. Collect reconnaissance groundwater sample from 14'-18', water is cloudy, light gray.						B3-14	X	
				80		99.9	B3-17.5-18	X	
	Becomes trace wood. Collect reconnaissance groundwater sample from 18'-22', water is cloudy, light gray.						B3-18	X	

nent Type: N/A
Diameter (inches): N/A
Slot Size (inches): N/A
ed Interval (ft bgs): N/A

Well Construction Information

Filter Pack: N/A
Surface Seal: N/A
Annular Seal: N/A

Ground Surface Elevation (ft): N/A
Top of Casing Elevation (ft): N/A
Boring Abandonment: Bentonite
Surveyed Location: X: N/A Y: N/A

FARALLON CONSULTING
320 3rd Avenue NE
Issaquah, WA 98027

Log of Boring: B-3

Sample Interval	Lithologic Description	USCS	USGS Graphic	% Recovery	Blow Counts 8/8/8	PID (ppm)	Sample ID	Sample Analyzed	Well Construction Details
	Collect reconnaissance groundwater sample from 22'-26', water is cloudy, light gray.			85		112	B3-21.5-22		
							B3-22	X	
				85		468	B3-25.5-26	X	
	Becomes minor silt. Collect reconnaissance groundwater sample from 26'-30', water is cloudy, light gray.						B3-26	X	
				90		413	B3-29.5-30		
	Becomes with wood. Collect reconnaissance groundwater sample from 30'-34', water is clear to slightly cloudy.						B3-30	X	
				90		98.0	B3-32-32.5	X	

Well Construction Information

nent Type: N/A
l Diameter (inches): N/A
l Slot Size (inches): N/A
ed Interval (ft bgs): N/A

Filter Pack: N/A
Surface Seal: N/A
Annular Seal: N/A

Ground Surface Elevation (ft): N/A
Top of Casing Elevation (ft): N/A
Boring Abandonment: Bentonite
Surveyed Location: X: N/A Y: N/A

PARALLON CONSULTING
320 3rd Avenue NE
Issaquah, WA 98027

Log of Boring: B-4

ent: Capital Industries
oject: Capital Industries
cation: Seattle, Washington
rallon PN: 457-001
gged By: T. Mulhern

Date/Time Started:	1/16/06 1130	**Sampler Type:**	Geoprobe
Date/Time Completed:	1/17/06 1355	**Drive Hammer (lbs.):**	N/A
Equipment:	Geoprobe	**Depth of Water ATD (ft bgs):**	7.5
Drilling Company:	Cascade Drilling	**Total Boring Depth (ft bgs):**	34
Drilling Foreman:	Kasey	**Total Well Depth (ft bgs):**	N/A
Drilling Method:	Direct Push		

Sample Interval	Lithologic Description	USCS	USGS Graphic	% Recovery	Blow Counts 8/8/8	PID (ppm)	Sample ID	Sample Analyzed	Well Construction Details
	Clear for utilities using vac-truck to 5.5'-6'.								
	SILT, with fine grained sand, light to medium brown with rust mottling, wet, medium stiff, no odor.	ML							
	SAND, minor silt, fine grained, dark gray to red-brown, saturated, dense, no odor. Becomes trace silt at 8.5'.	SP		100		>2000	B4-9.5-10	X	▽
	Collect reconnaissance groundwater sample from 10'-14', water is cloudy, light brown.						B4-10	X	
				100		>2000	B4-13.5-14	X	Temporary Well Screen
	Becomes dark gray. Collect reconnaissance groundwater sample from 14'-18', water is cloudy, light to medium gray.						B4-14	X	
				100		47.2	B4-17.5-18	X	
	Collect reconnaissance groundwater sample from 18'-22', water is slightly cloudy, light gray.						B4-18	X	

Well Construction Information

ıent Type:	N/A	**Filter Pack:**	N/A	**Ground Surface Elevation (ft):**	N/A
Diameter (inches):	N/A	**Surface Seal:**	N/A	**Top of Casing Elevation (ft):**	N/A
Slot Size (inches):	N/A	**Annular Seal:**	N/A	**Boring Abandonment:**	Bentonite
ed Interval (ft bgs):	N/A			**Surveyed Location:** X: N/A	Y: N/A

FARALLON CONSULTING
320 3rd Avenue NE
Issaquah, WA 98027

Log of Boring: B-4

Sample Interval	Lithologic Description	USCS	USGS Graphic	% Recovery	Blow Counts 8/8/8	PID (ppm)	Sample ID	Sample Analyzed	Well Construction Details
	Collect reconnaissance groundwater sample from 22'-26', water is cloudy, medium gray.			95		34.0	B4-21.5-22		
							B4-22	X	
				90		11.8	B4-25.5-26		
	Becomes with silt. Collect reconnaissance groundwater sample from 26'-30', water is cloudy, medium gray.						B4-26	X	
				95		0.0	B4-29.5-30		
	Collect reconnaissance groundwater sample from 30'-34', water is cloudy, medium gray.						B4-30	X	
				95		0.0	B4-33.5-34		

Well Construction Information

nent Type:	N/A	Filter Pack:	N/A	Ground Surface Elevation (ft):	N/A
) Diameter (inches):	N/A	Surface Seal:	N/A	Top of Casing Elevation (ft):	N/A
) Slot Size (inches):	N/A	Annular Seal:	N/A	Boring Abandonment:	Bentonite
ied Interval (ft bgs):	N/A			Surveyed Location: X: N/A	Y: N/A

PARALLON CONSULTING
320 3rd Avenue NE
Issaquah, WA 98027

Log of Boring: B-5

ient: Capital Industries
oject: Capital Industries
cation: Seattle, Washington
rallon PN: 457-001
gged By: T. Mulhern

Date/Time Started:	1/16/06 1400	**Sampler Type:**	Geoprobe
Date/Time Completed:	1/16/06 1600	**Drive Hammer (lbs.):**	N/A
Equipment:	Geoprobe	**Depth of Water ATD (ft bgs):**	7
Drilling Company:	Cascade Drilling	**Total Boring Depth (ft bgs):**	38
Drilling Foreman:	Kasey	**Total Well Depth (ft bgs):**	N/A
Drilling Method:	Direct Push		

Sample Interval	Lithologic Description	USCS	USGS Graphic	% Recovery	Blow Counts 8/8/8	PID (ppm)	Sample ID	Sample Analyzed	Well Construction Details
	Clear for utilities using vac-truck to 5.5'-6'.								
	SILT, trace fine sand, light gray-brown, wet to saturated, stiff, no odor.	ML							▽
	SAND, with silt, fine grained, medium gray brown with rust moffling at 9.5'.	SP		95		0.0	B5-7.5-8	X	
	Becomes trace silt, dark gray brown, dense.			85		0.0	B5-13.5-14	X	
				85		0.0	B5-17.5-18	X	

nent Type: N/A
l Diameter (inches): N/A
l Slot Size (inches): N/A
ed Interval (ft bgs): N/A

Well Construction Information

Filter Pack: N/A
Surface Seal: N/A
Annular Seal: N/A

Ground Surface Elevation (ft): N/A
Top of Casing Elevation (ft): N/A
Boring Abandonment: Bentonite
Surveyed Location: X: N/A Y: N/A

FARALLON CONSULTING
320 3rd Avenue NE
Issaquah, WA 98027

Log of Boring: B-5

Sample Interval	Lithologic Description	USCS	USGS Graphic	% Recovery	Blow Counts 8/8/8	PID (ppm)	Sample ID	Sample Analyzed	Well Construction Details
	Trace wood from 21'-22'.			85		0.0	B5-21.5-22		
				90		0.0	B5-25.5-26		
	Collect reconnaissance groundwater sample from 26'-30', water is cloudy, light gay.						B5-26	X	
				90		0.0	B5-29.5-30		Temporary Well Screen
	Collect reconnaissance groundwater sample from 30'-34', water is cloudy, light gray.						B5-30	X	
				80		0.0	B5-33.5-34	X	
	Saturated sample caused poor recovery. Collect reconnaissance groundwater sample from 34'-38', water is cloudy, light gray.						B5-34	X	
				50		0.0	B5-37.5-38		

Well Construction Information

nent Type:	N/A	Filter Pack:	N/A	Ground Surface Elevation (ft):	N/A
Diameter (inches):	N/A	Surface Seal:	N/A	Top of Casing Elevation (ft):	N/A
Slot Size (inches):	N/A	Annular Seal:	N/A	Boring Abandonment:	Bentonite
ed Interval (ft bgs):	N/A			Surveyed Location: X: N/A	Y: N/A

FARALLON consulting
975 5th Avenue Northwest
Issaquah, Washington 98027

Log of Boring: B6

Client: Capital Industries Inc.
Project: Capital Industries Inc.
Location: Seattle, WA

Farallon PN: 457-004

Logged By: Ken Scott

Date/Time Started:	11/24/2008 7:50	**Sampler Type:**	Macrocore 60-inch
Date/Time Completed:	11/25/2008 9:30	**Drive Hammer (lbs.):**	NA
Equipment:	Geoprobe 6600	**Depth of Water ATD (ft bgs):**	10.5' bgs
Drilling Company:	Cascade Drilling	**Total Boring Depth (ft bgs):**	70' bgs
Drilling Foreman:	Kasey Goble	**Total Well Depth (ft bgs):**	NA
Drilling Method:	Direct-push		

Depth (feet bgs.)	Sample Interval	Lithologic Description	USCS	USGS Graphic	% Recovery	Blow Counts 8/8/8	PID (ppm*)	Sample ID	Sample Analyzed	Boring/Well Construction Details
0		0-6": Asphalt, black, dry, odor and sheen.	AC							Asphalt cap
		6"-1.5': Poorly-graded fine SAND (95% sand, 5% silt), gray, moist, no odor or sheen.	SP		100	N/A	0.0			
5		1.5'-2.1': SILT (100% silt), dark-brown, moist, no odor or sheen.	ML							Bentonite
		2.1'-6.1': Silty SAND (65% sand, 35% silt), fine sand, light-brown, moist, no odor or sheen. Observed red-oxides b/w 4.0' to 6.0' bgs.	SM							
		6.1'-10.0': Poorly-graded fine SAND (95% sand, 5% silt), black, moist, no odor or sheen. Observed red-oxides b/w 6.1' to 10.0' bgs.	SP		100	N/A	0.0			
10		10.0-10.5': Sandy SILT (60% silt, 40% sand), fine sand, light-brown, moist to wet, no odor or sheen. Observed water at 10.5' bgs, and red-oxides b/w 10.0' to 10.5' bgs.	ML					B6-112408-10	X	Initial water level
		10.5'-16.8': Poorly-graded fine SAND (95% sand, 5% silt), black, wet, no odor or sheen. Observed red-oxides b/w 6.1'-10.0' bgs.	SP		100	N/A	0.0			
15								B6-112408-14	X	
								B6-112408-15-15.5	X	
		16.8'-17.0': SILT with sand (80% silt, 20% sand), fine sand, light-brown, wet, no odor or sheen.	ML		100	N/A	0.0			
		17.0'-23.0': Poorly-graded fine SAND (95% sand, 5% silt), black, wet, no odor or sheen.	SP					B6-112408-18	X	
20								Dup-B6-112408-18	X	
								B6-112408-22	X	
		23.0'-23.4': SILT (100% silt), gray, wet, no odor or sheen.	ML		100	N/A	0.0			
25		23.4'-24.5': Poorly-graded fine SAND (95% sand, 5% silt), black, wet, no odor or sheen.	SP							
		24.5'-25.0': SILT with sand (80% silt, 20% sand), fine sand, light-brown, wet, no odor or sheen.	ML					B6-112408-26	X	
			ML		100	N/A	0.0			
30		25.0'-29.0': SILT (90% silt, 10% sand), fine sand, light-brown, wet, no odor or sheen.	SP					B6-112408-30	X	
								B6-112408-30-30.5	X	
		29.0'-30.2': Poorly-graded fine SAND (95% sand, 5% silt), brown, wet, no odor or sheen.	ML							
			SP		100	N/A	0.0			Bentonite
35		30.2'-31.8': SILT with sand (80% silt, 20% sand), fine sand, brown, wet, no odor or sheen.	ML					B6-112408-34	X	
		31.8'-32.5': Poorly-graded fine SAND (95% sand, 5% silt), brown, wet, no odor or sheen.	SP		100	N/A	0.0	B6-112408-38	X	
40										

Well Construction Information

Monument Type:	NA	**Filter Pack:**	NA	**Ground Surface Elevation (ft):**	NA
Casing Diameter (inches):	2-inch	**Surface Seal:**	Asphalt	**Top of Casing Elevation (ft):**	NA
Screen Slot Size (inches):	0.004	**Annular Seal:**	NA	**Boring Abandonment:**	Bentonite
Screened Interval (ft bgs):	4' intervals			**Surveyed Location:**	X: 47.330154402 Y: -122.200081190

FARALLON consulting
975 5th Avenue Northwest
Issaquah, Washington 98027

Log of Boring: B6

Depth (feet bgs.)	Sample Interval	Lithologic Description	USCS	USGS Graphic	% Recovery	Blow Counts 8/8/8	PID (ppm)	Sample ID	Sample Analyzed	Well Construction Details
40		32.5'-34.0': SILT (90% silt, 10% sand), fine sand, brown, wet, no odor or sheen.								
		34.0'-48.5': Poorly-graded fine SAND (95% sand, 5% silt), brown, wet, no odor or sheen.			100	N/A	0.0	B6-112408-42	X	
45								B6-112408-46	X	
					95	N/A	0.0			
		48.5'-50.0': Silty SAND (80% sand, 20% silt), fine sand, brown, wet, no odor or sheen.	SM							
50			SP					B6-112408-50	X	
		50.0'-58.3': Poorly-graded fine SAND (95% sand, 5% silt), brown, wet, no odor or sheen.			100	N/A	0.0			
55								B6-112408-54	X	
								Dup-B6-112408-54	X	
					100	N/A	0.0			
		58.3'-62.5': Silty SAND (65% sand, 35% silt), fine sand, brown, wet, no odor or sheen.	SM					B6-112408-58	X	Bentonite
60								B6-112408-60-60.5	X	
		62.5'-70.0': Poorly-graded fine SAND (95% sand, 5% silt), brown, wet, no odor or sheen.	SP		100	N/A	0.0	B6-112508-62	X	
65								B6-112508-66	X	
					100	N/A	0.0			
70										Bentonite
75										
80										

Well Construction Information

Monument Type:	NA	**Filter Pack:**	NA	**Ground Surface Elevation (ft):**	NA
Casing Diameter (inches):	2-inch	**Surface Seal:**	Asphalt	**Top of Casing Elevation (ft):**	NA
Screen Slot Size (inches):	0.004	**Annular Seal:**	NA	**Boring Abandonment:**	Bentonite
Screened Interval (ft bgs):	4' intervals			**Surveyed Location:**	X: 47.330154402 Y: -122.200081190

FARALLON consulting
975 5th Avenue Northwest
Issaquah, Washington 98027

Log of Boring: B7

Client: Capital Industries Inc.
Project: Capital Industries Inc.
Location: Seattle, WA
Farallon PN: 457-004
Logged By: Ken Scott

Date/Time Started:	11/13/2008 7:45	**Sampler Type:**	Macrocore 60-inch
Date/Time Completed:	11/14/2008 10.10	**Drive Hammer (lbs.):**	NA
Equipment:	Geoprobe 6600	**Depth of Water ATD (ft bgs):**	8.0' bgs
Drilling Company:	Cascade Drilling	**Total Boring Depth (ft bgs):**	70' bgs
Drilling Foreman:	Kasey Goble	**Total Well Depth (ft bgs):**	NA
Drilling Method:	Direct-push		

Depth (feet bgs.)	Sample Interval	Lithologic Description	USCS	USGS Graphic	% Recovery	Blow Counts 8/8/8	PID (ppm*)	Sample ID	Sample Analyzed	Boring/Well Construction Details
0		0-5": Asphalt, black, dry, odor and sheen.	AC							Asphalt cap
		5"-1.2': Silty SAND (65% sand, 35% silt), fine sand, brown, moist, no odor or sheen.	SM		100	N/A	0.2			
5		1.2'-1.6': SILT (100% silt), dark-brown, moist, no odor or sheen.	ML							Bentonite
		1.6'-1.9': Sandy SILT (65% silt, 35% sand), fine sand, light-brown, moist, no odor or sheen.	ML							
		1.9'-7.0': SILT with sand (80% silt, 20% sand), fine sand, light-brown, moist, no odor or sheen.	ML		100	N/A	0.0	B7-111308-8	X	▽ Initial water level
10		7.0'-10.0': Poorly-graded fine SAND (95% sand, 5% silt), black, moist to wet, no odor or sheen. Observed water, and red-oxides at 8.0' bgs.	SP							
		10.0'-10.8': Silty SAND (60% sand, 40% silt), fine sand, brown, wet, no odor or sheen.	SM		100	N/A	0.0	B7-111308-12	X	
15		10.8'-28.0': Poorly-graded fine SAND (95% sand, 5% silt), black, wet, no odor or sheen.	SP					B7-111308-16	X	
					100	N/A	0.0			
20								B7-111308-20	X	
					70	N/A	0.0			
25								B7-111308-24	X	
		28.0'-28.2': SILT with sand (80% silt, 20% sand), fine sand, brown, wet, no odor or sheen.	ML		60	N/A	0.2	B7-111308-28	X	
30		28.2'-29.0': Poorly-graded fine SAND (95% sand, 5% silt), brown, wet, no odor or sheen.	SP					Dup-B7-111308-28	X	
		29.0'-29.5': SILT with sand (80% silt, 20% sand), fine sand, brown, wet, no odor or sheen.	ML							
			SP		100	N/A	0.0	B7-111308-32	X	Bentonite
35		29.5'-34.0': Poorly-graded fine SAND (95% sand, 5% silt), brown, wet, no odor or sheen.	ML							
								B7-111308-36	X	
		34.0'-37.5': Sandy SILT (65% silt, 35% sand), fine sand, brown, wet, no odor or sheen.	ML		80	N/A	0.0			
40			SP							

Well Construction Information

Monument Type: NA
Casing Diameter (inches): 2-inch
Screen Slot Size (inches): 0.004
Screened Interval (ft bgs): 4' intervals
Filter Pack: NA
Surface Seal: Asphalt
Annular Seal: NA
Ground Surface Elevation (ft): NA
Top of Casing Elevation (ft): NA
Boring Abandonment: Bentonite
Surveyed Location: X: 47.330133674 Y: -122.195790324

FARALLON consulting
975 5th Avenue Northwest
Issaquah, Washington 98027

Log of Boring: B7

Depth (feet bgs.)	Sample Interval	Lithologic Description	USCS	USGS Graphic	% Recovery	Blow Counts 8/8/8	PID (ppm)	Sample ID	Sample Analyzed	Well Construction Details
40		37.5'-37.9': Sandy SILT (60% silt, 40% sand), fine sand, brown, wet, slight decomposition-like odor, no sheen.	ML					B7-111308-40	X	
45		37.9'-41.0': Poorly-graded fine SAND (95% sand, 5% silt), brown, wet, no odor or sheen.	SM		70	N/A	0.0	B7-111308-44	X	
		41.0'-43.5': Sandy SILT (60% silt, 40% sand), fine sand, brown, wet, no odor or sheen.	SP							
50		43.5'-46.0': Silty SAND (65% sand, 35% silt), fine sand, brown, wet, no odor or sheen.			100	N/A	0.0	B7-111308-48	X	
		46.0'-58.0': Poorly-graded fine SAND (95% sand, 5% silt), brown, wet, slight decomposition-like odor, no sheen.			100	N/A	0.0	B7-111308-52	X	
55								B7-111308-56	X	
		58.0'-62.0': Sandy SILT (60% silt, 40% sand), fine sand, brown, wet, no odor or sheen.	ML		100	N/A	0.0			Bentonite
60								B7-111308-60	X	
		62.0'-70.0': Poorly-graded fine SAND (95% sand, 5% silt), brown, wet, no odor or sheen.	SP		100	N/A	0.0	B7-111308-64	X	
65								Dup-B7-111308-64	X	
					100	N/A	0.0			
70										Bentonite
75										
80										

Well Construction Information

Monument Type:	NA	**Filter Pack:**	NA	**Ground Surface Elevation (ft):**	NA
Casing Diameter (inches):	2-inch	**Surface Seal:**	Asphalt	**Top of Casing Elevation (ft):**	NA
Screen Slot Size (inches):	0.004	**Annular Seal:**	NA	**Boring Abandonment:**	Bentonite
Screened Interval (ft bgs):	4' intervals			**Surveyed Location:**	X: 47.330133674 Y: -122.195790324

FARALLON consulting
975 5th Avenue Northwest
Issaquah, Washington 98027

Log of Boring: B8

Client: Capital Industries Inc.
Project: Capital Industries Inc.
Location: Seattle, WA

Farallon PN: 457-004

Logged By: Ken Scott & Jen Baptist

Date/Time Started:	11/25/2008 9:45	**Sampler Type:**	Macrocore 60-inch
Date/Time Completed:	11/26/2008 14:15	**Drive Hammer (lbs.):**	NA
Equipment:	Geoprobe 6600	**Depth of Water ATD (ft bgs):**	6.0' bgs
Drilling Company:	Cascade Drilling	**Total Boring Depth (ft bgs):**	70' bgs
Drilling Foreman:	Kasey Goble	**Total Well Depth (ft bgs):**	NA
Drilling Method:	Direct-push		

Depth (feet bgs.)	Sample Interval	Lithologic Description	USCS	USGS Graphic	% Recovery	Blow Counts 8/8/8	PID (ppm*)	Sample ID	Sample Analyzed	Boring/Well Construction Details
0		0-8": Asphalt, black, dry, odor and sheen.	AC							Asphalt cap
		8"-2.0': Poorly-graded fine SAND with silt and gravel (70% sand, 20% gravel, 10% silt), fine gravel, gray, moist, no odor or sheen. Observed rounded gravel..	SP-SM		80	N/A	0.0			
5		2.0'-4.0': Poorly-graded fine SAND with silt (90% sand, 10% silt), tan, moist, no odor or sheen.	SP-SM / ML							Bentonite
		4.0'-5.0': SILT (100% silt), gray and tan layers, moist, stiff, no odor or sheen.	SP / ML		100	N/A	0.0	B8-112508-8	X	Initial water level
10		5.0'-6.0': Poorly-graded fine SAND (85% sand, 10% gravel, 5% silt), fine gravel, tan to brown, moist to wet, no odor or sheen. Observed water at 6.0' bgs.	SP / ML							
		6.0'-8.3': SILT (100% silt), gray, wet, soft, no odor or sheen.	ML / SP		100	N/A	0.0	B8-112508-12	X	
15		8.3'-10.0': Poorly-graded fine SAND (95% sand, 5% silt), black, wet, no odor or sheen.	SP					B8-112508-16	X	
		10.0'-11.0': SILT, trace gravel (95% silt, 5% gravel), brown, wet, no odor or sheen.	SP		80	N/A	0.0			
20		11.0'-18.0': Poorly-graded fine SAND (95% sand, 5% silt), black, wet, no odor or sheen.	SP					B8-112508-20	X	
		18.0'-23.0': Silty SAND (80% sand, 20% silt), black, wet, no odor or sheen. Observed wood-debris in sampler.	ML / SP		80	N/A	0.0			
25		23.0'-25.0': SILT (100% silt), tan, wet, no odor or sheen. Observed wood-debris in sampler.	SP					B8-112508-24	X	
		25.0'-27.2': Silty SAND (80% sand, 20% silt), black, wet, no odor or sheen.	ML		85	N/A	0.0	B8-112508-28	X	
30		27.2'-30.0': SILT (100% silt), tan, wet, no odor or sheen. Observed wood-debris in sampler.	ML							
		30.0'-34.0': SILT (90% silt, 10% sand), fine sand, gray, wet, no odor or sheen. Observed wood-debris in sampler.	ML		95	N/A	0.0	B8-112508-32	X	Bentonite
35		34.0'-37.4': Poorly-graded fine SAND with silt (90% sand, 10% silt), black, wet, no odor, no sheen. Observed wood-debris throughout sampler.	SP-SM					B8-112508-36	X	
		37.4'-37.7': SILT (95% silt, 5% sand), fine sand, gray, wet, no odor or sheen.	ML / SP		95	N/A	0.0			
40										

Well Construction Information

Monument Type: NA
Casing Diameter (inches): 2-inch
Screen Slot Size (inches): 0.004
Screened Interval (ft bgs): 4' intervals

Filter Pack: NA
Surface Seal: Asphalt
Annular Seal: NA

Ground Surface Elevation (ft): NA
Top of Casing Elevation (ft): NA
Boring Abandonment: Bentonite
Surveyed Location: X: 47.35882410 Y: -122.200041452

FARALLON consulting
975 5th Avenue Northwest
Issaquah, Washington 98027

Log of Boring: B8

Depth (feet bgs.)	Sample Interval	Lithologic Description	USCS	USGS Graphic	% Recovery	Blow Counts 8/8/8	PID (ppm)	Sample ID	Sample Analyzed	Well Construction Details
40		37.7'-45.0': Poorly-graded fine SAND with silt (90% sand, 10% silt), black, wet, no odor, no sheen. Observed wood-debris b/w 37.7 to 40.0' bgs.			100	N/A	0.0	B8-112508-40 Dup-B8-112508-40	X X	
45		55.0'-70.0': Poorly-graded fine SAND (95% sand, 5% silt), brown, wet, no odor, no sheen.	SP		100	N/A	0.0	B8-112508-44	X	
50					100	N/A	0.0	B8-112608-48	X	
55					100	N/A	0.0	B8-112608-52	X	
60					100	N/A	0.0	B8-112608-56	X	Bentonite
65					100	N/A	0.0	B8-112608-60	X	
70					100	N/A	0.0	B8-112608-64	X	Bentonite
75										
80										

Well Construction Information

Monument Type:	NA	Filter Pack:	NA	Ground Surface Elevation (ft):	NA
Casing Diameter (inches):	2-inch	Surface Seal:	Asphalt	Top of Casing Elevation (ft):	NA
Screen Slot Size (inches):	0.004	Annular Seal:	NA	Boring Abandonment:	Bentonite
Screened Interval (ft bgs):	4' intervals			Surveyed Location:	X: 47.35882410 Y: -122.200041452

FARALLON consulting
975 5th Avenue Northwest
Issaquah, Washington 98027

Log of Boring: B9

Client: Capital Industries Inc.
Project: Capital Industries Inc.
Location: Seattle, WA
Farallon PN: 457-004
Logged By: Ken Scott

Date/Time Started:	11/14/2008 10:30	**Sampler Type:**	Macrocore 60-inch
Date/Time Completed:	11/18/2008 13:45	**Drive Hammer (lbs.):**	NA
Equipment:	Geoprobe 6600	**Depth of Water ATD (ft bgs):**	10.0
Drilling Company:	Cascade Drilling	**Total Boring Depth (ft bgs):**	70' bgs
Drilling Foreman:	Kasey Goble	**Total Well Depth (ft bgs):**	NA
Drilling Method:	Direct-push		


Depth (feet bgs.)	Sample Interval	Lithologic Description	USCS	USGS Graphic	% Recovery	Blow Counts 8/8/8	PID (ppm*)	Sample ID	Sample Analyzed	Boring/Well Construction Details
0		0-6": Asphalt, black, dry, odor and sheen.	AC							Asphalt cap
		6"-4.0': Silty SAND (60% sand, 35% silt, 5% gravel), fine sand and gravel, dark-brown, moist, no odor or sheen. Observed red-oxides b/w 4 to 6' bgs.	SM		100	N/A	0.0			
5		4.0'-7.4':Silty SAND (80% sand, 20% silt), fine sand, brown, moist, no odor or sheen. Observed laminated wood-debris in sampler.	SM							Bentonite
		7.4'-11.5': Poorly-graded fine SAND with silt (90% sand, 10% silt), brown, moist to wet, no odor or sheen.	SP		100	N/A	0.0			
10		Observed red-oxides and water at 10.0' bgs.						B9-111408-10	X	Initial water level
		11.5'-23.0': Poorly-graded fine SAND (95% sand, 5% silt), black, wet, no odor or sheen.	SP		100	N/A	0.0			
15								B9-111408-14	X	
								B9-111408-15-15.5	X	
					100	N/A	0.0			
20								B9-111408-18	X	
								B9-111408-22	X	
		23.0'-25.0': Sandy SILT (65% silt, 35% sand), fine sand, brown, wet, no odor or sheen.	ML		100	N/A	0.0			
25		25.0'-26.0': Poorly-graded fine SAND (95% sand, 5% silt), brown, wet, no odor or sheen.	SP							
		26.0'-30.5': Sandy SILT (60% silt, 40% sand), fine sand, brown, wet, no odor or sheen.	ML		100	N/A	0.0	B9-111408-26	X	
30								B9-111408-30	X	
		30.5'-31.0': SILT(100% silt), brown, wet, no odor or sheen.	ML					B9-111408-30-30.5	X	
		31.0'-32.2': Poorly-graded fine SAND (95% sand, 5% silt), brown, wet, no odor or sheen.	SP		100	N/A	0.0			Bentonite
35		32.2'-32.6': SILT(100% silt), brown, wet, no odor or sheen.	ML					B9-111408-34	X	
		32.6'-33.5': Poorly-graded fine SAND (95% sand, 5% silt), brown, wet, no odor or sheen.	SP							
			SM		100	N/A	0.0			
40		33.5'-34.0': Silty SAND (60% sand, 40% silt), fine sand, brown, wet, no	SP					B9-111408-38	X	

Well Construction Information

Monument Type:	NA	**Filter Pack:**	NA	**Ground Surface Elevation (ft):**	NA
Casing Diameter (inches):	2-inch	**Surface Seal:**	Asphalt	**Top of Casing Elevation (ft):**	NA
Screen Slot Size (inches):	0.004	**Annular Seal:**	NA	**Boring Abandonment:**	Bentonite
Screened Interval (ft bgs):	4' intervals			**Surveyed Location:**	X: 47.325889364 Y: -122.195861273

FARALLON consulting
975 5th Avenue Northwest
Issaquah, Washington 98027

Log of Boring: B9

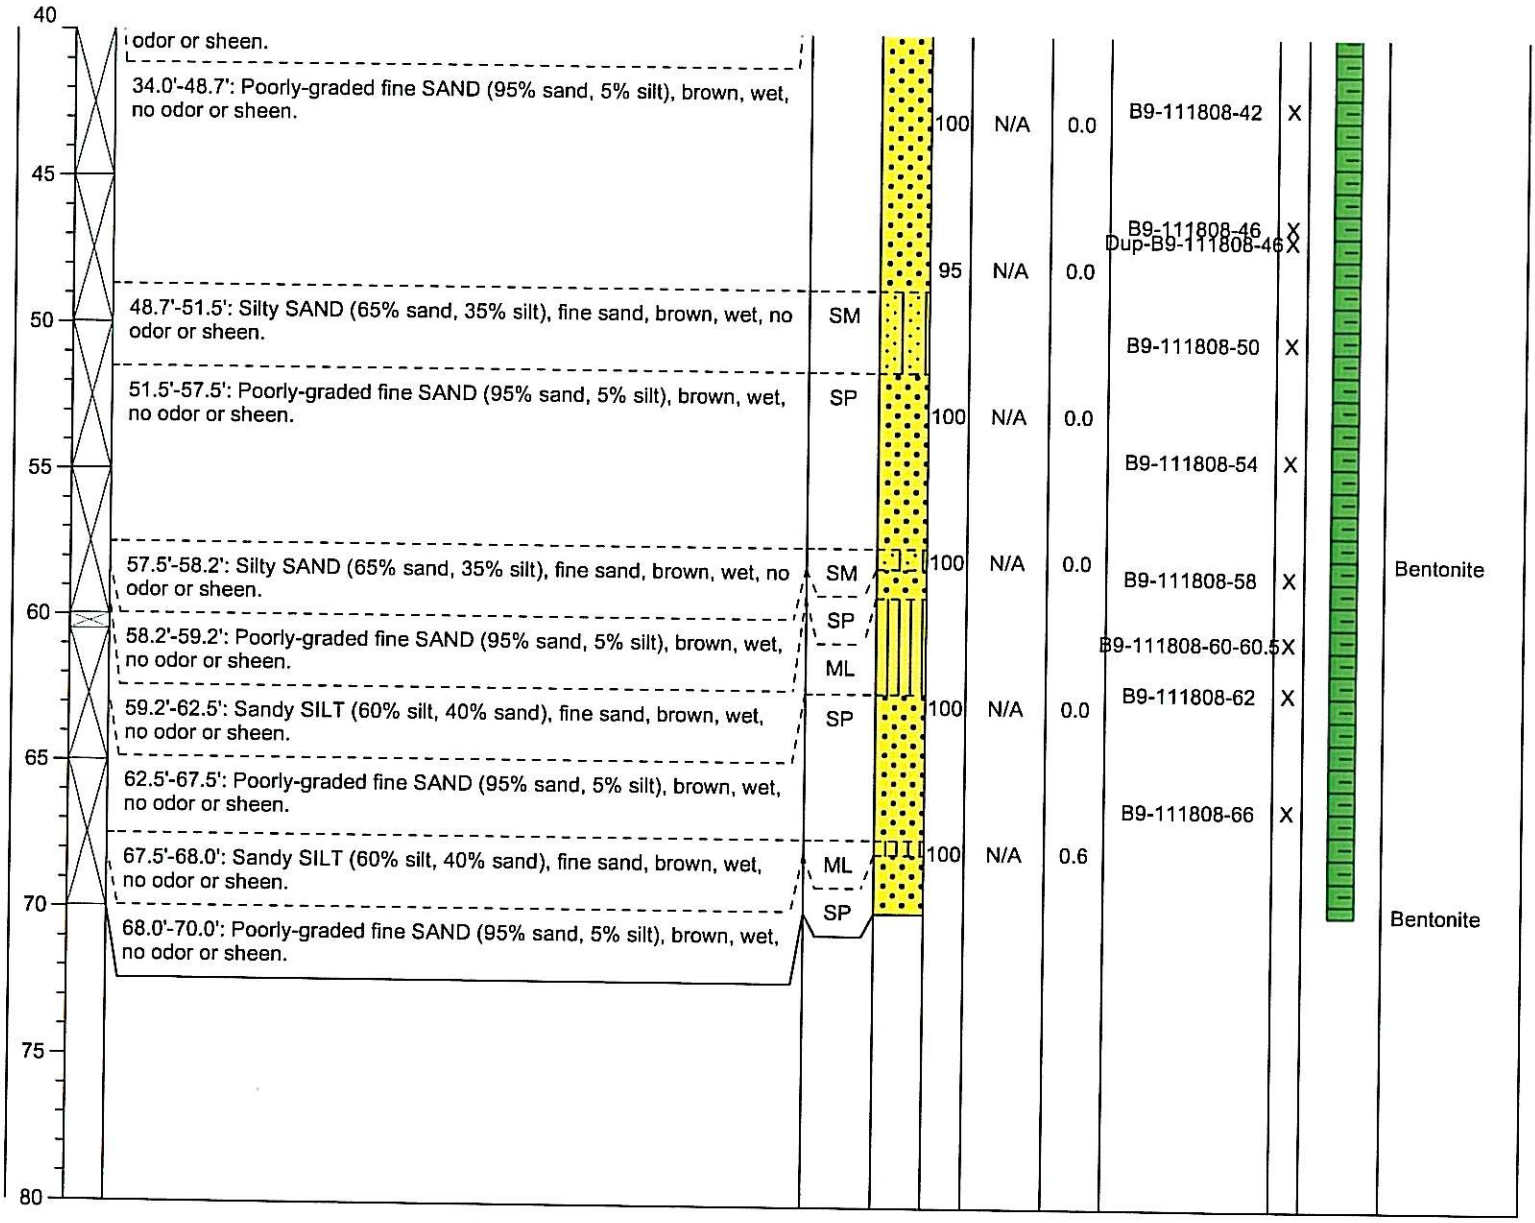

Well Construction Information

Monument Type:	NA	**Filter Pack:**	NA	**Ground Surface Elevation (ft):**	NA
Casing Diameter (inches):	2-inch	**Surface Seal:**	Asphalt	**Top of Casing Elevation (ft):**	NA
Screen Slot Size (inches):	0.004	**Annular Seal:**	NA	**Boring Abandonment:**	Bentonite
Screened Interval (ft bgs):	4' intervals			**Surveyed Location:**	X: 47.325889364 Y: -122.195861273

FARALLON consulting
975 5th Avenue Northwest
Issaquah, Washington 98027

Log of Boring: B10

Client: Capital Industries Inc.
Project: Capital Industries Inc.
Location: Seattle, WA

Farallon PN: 457-004

Logged By: Ken Scott

Date/Time Started:	11/20/2008 11:50	**Sampler Type:**	Macrocore 60-inch
Date/Time Completed:	11/21/2008 14:05	**Drive Hammer (lbs.):**	NA
Equipment:	Geoprobe 6600	**Depth of Water ATD (ft bgs):**	8.0
Drilling Company:	Cascade Drilling	**Total Boring Depth (ft bgs):**	70' bgs
Drilling Foreman:	Kasey Goble	**Total Well Depth (ft bgs):**	NA
Drilling Method:	Direct-push		

Depth (feet bgs.)	Sample Interval	Lithologic Description	USCS	USGS Graphic	% Recovery	Blow Counts 8/8/8	PID (ppm*)	Sample ID	Sample Analyzed	Boring/Well Construction Details
0		0-4": Organic, grass, Sandy SILT (65% silt, 35% sand), fine sand, brown, moist, no odor, slight monochromatic (white) sheen.	OL							Grass plug
		4"-2.5': Poorly-graded fine SAND (95% sand, 5% silt), fine sand, light-brown, moist, no odor or sheen.	SP		100	N/A	0.0			
5		2.5'-3.0': Sandy SILT (60% silt, 40% sand), fine sand, brown, moist, no odor or sheen. Observed red-oxides b/w 2.5 to 3.0' bgs.	ML							Bentonite
		3.0'-6.0': Poorly-graded fine SAND (95% sand, 5% silt), fine sand, brown, moist, no odor or sheen.	SP							
10		6.0'-9.5': Sandy SILT (60% silt, 40% sand), fine sand, light-brown, moist to wet, no odor or sheen. Observed water at 8.0' bgs..	ML		100	N/A	0.0	B10-112008-8	X	Initial water level
		9.5'-41.0': Poorly-graded fine SAND (95% sand, 5% silt), fine sand, brown, wet, no odor or sheen.	SP							
					100	N/A	0.0	B10-112008-12	X	
15										
					100	N/A	0.0	B10-112008-16	X	
20										
					100	N/A	0.0	B10-112008-20	X	
25										
					100	N/A	0.0	B10-112008-24	X	
30										
					100	N/A	0.0	B10-112008-28	X	
35										
					100	N/A	0.0	B10-112108-32	X	Bentonite
								B10-112108-36	X	
40					100	N/A	0.0	Dup-B10-112108-36	X	

Well Construction Information


Monument Type: NA
Casing Diameter (inches): 2-inch
Screen Slot Size (inches): 0.004
Screened Interval (ft bgs): 4' intervals

Filter Pack: NA
Surface Seal: Asphalt
Annular Seal: NA

Ground Surface Elevation (ft): NA
Top of Casing Elevation (ft): NA
Boring Abandonment: Bentonite
Surveyed Location: X: 47.330236411 Y: -122.200257281

FARALLON consulting
975 5th Avenue Northwest
Issaquah, Washington 98027

Log of Boring: B10

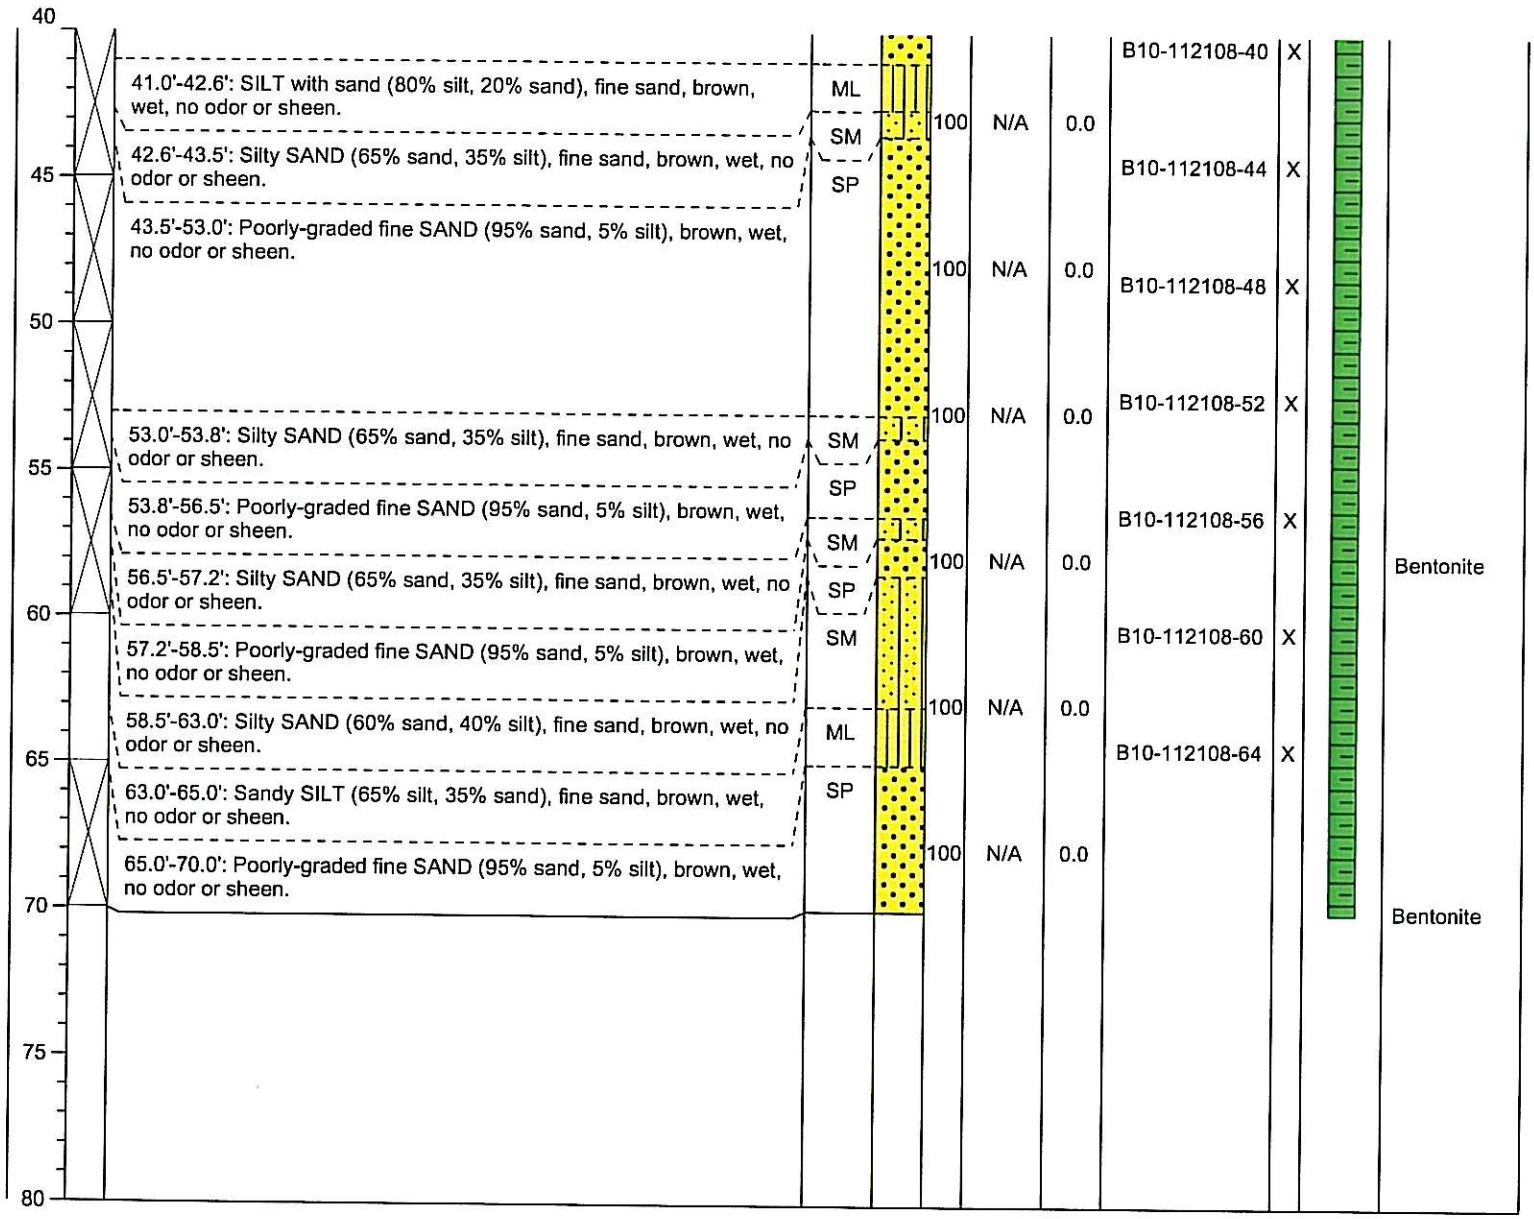

Well Construction Information

Monument Type:	NA	**Filter Pack:**	NA	**Ground Surface Elevation (ft):**	NA
Casing Diameter (inches):	2-inch	**Surface Seal:**	Asphalt	**Top of Casing Elevation (ft):**	NA
Screen Slot Size (inches):	0.004	**Annular Seal:**	NA	**Boring Abandonment:**	Bentonite
Screened Interval (ft bgs):	4' intervals			**Surveyed Location:**	X: 47.330236411 Y: -122.200257281

FARALLON consulting
975 5th Avenue Northwest
Issaquah, Washington 98027

Log of Boring: B11

Client: Capital Industries Inc.
Project: Capital Industries Inc.
Location: Seattle, WA
Farallon PN: 457-004
Logged By: Ken Scott

Date/Time Started:	11/19/2008 7:55	**Sampler Type:**	Macrocore 60-inch
Date/Time Completed:	11/20/2008 11:10	**Drive Hammer (lbs.):**	NA
Equipment:	Geoprobe 6600	**Depth of Water ATD (ft bgs):**	8.0' bgs
Drilling Company:	Cascade Drilling	**Total Boring Depth (ft bgs):**	70' bgs
Drilling Foreman:	Kasey Goble	**Total Well Depth (ft bgs):**	NA
Drilling Method:	Direct-push		

Depth (feet bgs.)	Sample Interval	Lithologic Description	USCS	USGS Graphic	% Recovery	Blow Counts 8/8/8	PID (ppm*)	Sample ID	Sample Analyzed	Boring/Well Construction Details
0		0-6": Asphalt, black, dry, odor and sheen.	AC							Asphalt cap
		6"-4.0': Silty SAND (70% sand, 20% silt, 10% gravel), fine sand and gravel, brown, moist, no odor or sheen.	SM		100	N/A	0.0			
5		4.0'-9.0': SILT with sand (80% silt, 20% sand), fine sand, light-brown, moist to wet, no odor or sheen. Observed water at 8.0' bgs, and red-oxides b/w 7 to 9' bgs.	ML		100	N/A	0.0	B11-111908-8	X	Bentonite Initial water level
10		9.0'-10.0': Poorly-graded fine SAND (95% sand, 5% silt), black, wet, no odor or sheen.	SP							
		10.0'-10.9': SILT, minor sand (90% silt, 10% sand), fine sand, light-brown, wet, no odor or sheen.	ML		100	N/A	0.0	B11-111908-12	X	
		10.9'-11.6': Silty SAND (65% sand, 35% silt), fine sand, brown, wet, no odor or sheen.	SM							
15		11.6'-29.0': Poorly-graded fine SAND (95% sand, 5% silt), black, wet, no odor or sheen.	SP					B11-111908-16	X	
					100	N/A	0.0			
20								B11-111908-20	X	
								Dup-B11-111908-20	X	
					100	N/A	0.0			
25								B11-111908-24	X	
					90	N/A	0.0			
								B11-111908-28	X	
30		29.0'-31.5': Silty SAND (65% sand, 35% silt), fine sand, brown, wet, no odor or sheen.	SM							
		31.5'-32.3': Poorly-graded fine SAND (95% sand, 5% silt), brown, wet, no odor or sheen.	SP		95	N/A	0.0	B11-111908-32	X	Bentonite
35		32.3'-33.2': SILT (90% silt, 10% sand), fine sand, brown, wet, no odor or sheen.	ML							
		33.2'-34.5': Silty SAND (65% sand, 35% silt), fine sand, brown, wet, no odor or sheen.	SM					B11-111908-36	X	
			SP		80	N/A	0.0			
40		34.5'-47.5': Poorly-graded fine SAND (95% sand, 5% silt), brown, wet,								

Well Construction Information

Monument Type:	NA	**Filter Pack:**	NA	**Ground Surface Elevation (ft):**	NA
Casing Diameter (inches):	2-inch	**Surface Seal:**	Asphalt	**Top of Casing Elevation (ft):**	NA
Screen Slot Size (inches):	0.004	**Annular Seal:**	NA	**Boring Abandonment:**	Bentonite
Screened Interval (ft bgs):	4' intervals			**Surveyed Location:**	X: 47.325981700 Y: -122.200244632

FARALLON consulting
975 5th Avenue Northwest
Issaquah, Washington 98027

Log of Boring: B11

Depth (feet bgs.)	Sample Interval	Lithologic Description	USCS	USGS Graphic	% Recovery	Blow Counts 8/8/8	PID (ppm)	Sample ID	Sample Analyzed	Well Construction Details
40		no odor or sheen.			100	N/A	0.0	B11-111908-40	X	
45		Observed a small chunk of wood debris at 38.5' bgs.						B11-111908-44	X	
		47.5'-47.9': Silty SAND (60% sand, 40% silt), fine sand, brown, wet, no odor or sheen.	SM		95	N/A	0.0	B11-111908-48	X	
50		47.9'-53.0': Poorly-graded fine SAND (95% sand, 5% silt), brown, wet, no odor or sheen.	SP					B11-112008-52	X	
		53.0'-54.2': Silty SAND (65% sand, 35% silt), fine sand, brown, wet, no odor or sheen.	SM		100	N/A	0.0			
55		54.2'-56.0': Sandy SILT (60% silt, 40% sand), fine sand, brown, wet, no odor or sheen.	ML					B11-112008-56	X	
		56.0'-56.8': Sandy SILT (60% silt, 40% sand), fine sand, brown, wet, no odor or sheen.	ML		100	N/A	0.0			Bentonite
60		56.8'-59.5': Silty SAND (65% sand, 35% silt), fine sand, brown, wet, no odor or sheen.	SM					B11-112008-60	X	
		59.5'-66.0': Poorly-graded fine SAND (95% sand, 5% silt), brown, wet, no odor, no sheen.	SP					Dup-B11-112008-60	X	
65					100	N/A	0.0	B11-112008-64	X	
		66.0'-66.7': Silty SAND (65% sand, 35% silt), fine sand, brown, wet, no odor or sheen.	SM							
		66.7'-70.0': Poorly-graded fine SAND (95% sand, 5% silt), brown, wet, no odor, no sheen.	SP		100	N/A	0.0			
70										Bentonite
75										
80										

Well Construction Information

Monument Type:	NA	**Filter Pack:**	NA	**Ground Surface Elevation (ft):**	NA
Casing Diameter (inches):	2-inch	**Surface Seal:**	Asphalt	**Top of Casing Elevation (ft):**	NA
Screen Slot Size (inches):	0.004	**Annular Seal:**	NA	**Boring Abandonment:**	Bentonite
Screened Interval (ft bgs):	4' intervals			**Surveyed Location:**	X: 47.325981700 Y: -122.200244632

FARALLON consulting
975 5th Avenue Northwest
Issaquah, Washington 98027

Log of Boring: B12

Client: Capital Industries Inc.
Project: Capital Industries Inc.
Location: Seattle, WA

Farallon PN: 457-004

Logged By: Ken Scott

Date/Time Started:	12/08/2008 9:05	**Sampler Type:**	Macrocore 60-inch
Date/Time Completed:	12/09/2008 10:15	**Drive Hammer (lbs.):**	NA
Equipment:	Geoprobe 6600	**Depth of Water ATD (ft bgs):**	7.25' bgs
Drilling Company:	Cascade Drilling	**Total Boring Depth (ft bgs):**	70' bgs
Drilling Foreman:	Kasey Goble	**Total Well Depth (ft bgs):**	NA
Drilling Method:	Direct-push		

Depth (feet bgs.)	Sample Interval	Lithologic Description	USCS	USGS Graphic	% Recovery	Blow Counts 8/8/8	PID (ppm*)	Sample ID	Sample Analyzed	Boring/Well Construction Details
0		0-11": Poorly-graded GRAVEL with sand (80% gravel, 15% sand, 5% silt), coarse gravel, fine to medium sand, gray gravel/brown soil, moist, no odor or sheen. Observed coarse angular granite gravel.	GP							Gravel cap
			ML		100	N/A	0.0			
5		11"-1.3': SILT (95% silt, 5% sand), fine sand, dark-brown, moist, no odor or sheen.	ML							Bentonite
		1.3'-6.0': SILT (100% silt), tan, moist, no odor or sheen. Observed red-oxides b/w 2.5' to 6.0' bgs.	SP							▽ Initial water level
			SP		100	N/A	0.0	B12-120808-8	X	
10		6.0'-7.5': Poorly-graded SAND with silt (90% sand, 10% silt), fine sand, black, moist to wet, no odor or sheen. Observed water at 7.25' bgs.	ML							
		7.5'-10.5': Poorly-graded fine SAND (95% sand, 5% silt), black, wet, no odor or sheen.	SP		100	N/A	0.0	B12-120808-12	X	
15		10.5'-11.5': SILT with sand (80% silt, 20% sand), fine sand, tan, wet, no odor or sheen.						B12-120808-16	X	
		11.5'-30.5': Poorly-graded fine SAND (95% sand, 5% silt), black, wet, no odor or sheen.			100	N/A	0.0			
20								B12-120808-20	X	
								Dup-B12-120808-20	X	
					90	N/A	0.0			
25								B12-120808-24	X	
					80	N/A	0.0	B12-120808-28	X	
30		30.5'-30.8': SILT (95% silt, 5% sand), fine sand, light-brown, wet, no odor or sheen.	ML							
		30.8'-31.5': Poorly-graded fine SAND (95% sand, 5% silt), brown, wet, no odor or sheen.	SP		90	N/A	0.0	B12-120808-32	X	Bentonite
35		31.5'-32.5': Silty SAND (80% sand, 20% silt), fine sand, brown, wet, no odor or sheen.	SP							
		32.5'-33.0': Silty SAND (65% sand, 35% silt), fine sand, brown, wet, no odor or sheen.	SM					B12-120808-36	X	
40			SP		100	N/A	0.0			
			SM							

Well Construction Information

Monument Type:	NA	**Filter Pack:**	NA	**Ground Surface Elevation (ft):**	NA
Casing Diameter (inches):	2-inch	**Surface Seal:**	N/A	**Top of Casing Elevation (ft):**	NA
Screen Slot Size (inches):	0.004	**Annular Seal:**	NA	**Boring Abandonment:**	Bentonite
Screened Interval (ft bgs):	4' intervals			**Surveyed Location:**	X: 47.330087036 Y: -122.195593404

FARALLON consulting
975 5th Avenue Northwest
Issaquah, Washington 98027

Log of Boring: B12

Depth (feet bgs.)	Sample Interval	Lithologic Description	USCS	USGS Graphic	% Recovery	Blow Counts 8/8/8	PID (ppm)	Sample ID	Sample Analyzed	Well Construction Details
40		33.0'-35.0': Poorly-graded fine SAND with silt (95% sand, 5% silt), brown, wet, no odor or sheen.	ML					B12-120808-40	X	
		35.0'-37.0': Silty SAND (65% sand, 35% silt), fine sand, brown, wet, no odor or sheen.	SP		100	N/A	0.0			
45		37.0'-37.7': SILT (95% silt, 5% sand), fine sand, brown, wet, no odor or sheen.	ML					B12-120808-44	X	
		33.7'-38.5': Poorly-graded fine SAND (95% sand, 5% silt), brown, wet, no odor or sheen.	SM		100	N/A	0.0	B12-120808-48	X	
50		38.5'-41.0': SILT with sand (75% silt, 25% sand), fine sand, brown, wet, no odor or sheen.	ML							
		41.0'-49.5': Silty SAND (65% sand, 35% silt), fine sand, brown, wet, no odor or sheen.	SM					B12-120808-52	X	
55		49.5'-50.5': SILT (95% silt, 5% sand), fine sand, brown, wet, no odor or sheen.	SP		100	N/A	0.0			
		50.5'-51.7': Silty SAND (65% sand, 35% silt), fine sand, brown, wet, no odor or sheen.	ML					B12-120908-56	X	
60		51.7'-52.4': Poorly-graded fine SAND (95% sand, 5% silt), brown, wet, no odor or sheen.	SP					Dup-B12-120908-56	X	
		52.4'-53.5': Sandy SILT (60% silt, 40% sand), fine sand, brown, wet, no odor or sheen.	SM		100	N/A	0.0			Bentonite
65		53.5'-56.0': Poorly-graded fine SAND (95% sand, 5% silt), brown, wet, no odor or sheen.	SP					B12-120908-60	X	
		56.0'-57.5': Silty SAND (65% sand, 35% silt), fine sand, brown, wet, no odor or sheen.	ML							
70		57.5'-62.5': Poorly-graded fine SAND (95% sand, 5% silt), brown, wet, no odor or sheen.	SP		100	N/A	0.0	B12-120908-64	X	
		62.5'-63.5': Silty SAND (65% sand, 35% silt), fine sand, brown, wet, no odor or sheen.								
75		63.5.'-64.5': SILT (90% silt, 10% sand), fine sand, brown, wet, no odor or sheen.								
		64.5'-69.5': Poorly-graded fine SAND (95% sand, 5% silt), brown, wet, no odor or sheen.			100	N/A	0.0			
80		69.5'-70.0': SILT (100% silt), brown, wet, no odor or sheen.	ML							Bentonite

Well Construction Information

Monument Type:	NA	**Filter Pack:**	NA	**Ground Surface Elevation (ft):**	NA
Casing Diameter (inches):	2-inch	**Surface Seal:**	N/A	**Top of Casing Elevation (ft):**	NA
Screen Slot Size (inches):	0.004	**Annular Seal:**	NA	**Boring Abandonment:**	Bentonite
Screened Interval (ft bgs):	4' intervals			**Surveyed Location:**	X: 47.330087036 Y: -122.195593404

FARALLON consulting
975 5th Avenue Northwest
Issaquah, Washington 98027

Log of Boring: B13

Client: Capital Industries Inc.
Project: Capital Industries Inc.
Location: Seattle, WA

Farallon PN: 457-004

Logged By: Ken Scott

Date/Time Started:	12/01/2008 8:00	**Sampler Type:**	Macrocore 60-inch
Date/Time Completed:	12/02/2008 12:20	**Drive Hammer (lbs.):**	NA
Equipment:	Geoprobe 6600	**Depth of Water ATD (ft bgs):**	11.0' bgs
Drilling Company:	Cascade Drilling	**Total Boring Depth (ft bgs):**	70' bgs
Drilling Foreman:	Kasey Goble	**Total Well Depth (ft bgs):**	NA
Drilling Method:	Direct-push		


Depth (feet bgs.)	Sample Interval	Lithologic Description	USCS	USGS Graphic	% Recovery	Blow Counts 8/8/8	PID (ppm*)	Sample ID	Sample Analyzed	Boring/Well Construction Details
0		0-6": Asphalt, black, dry, odor and sheen.	SP							Asphalt cap
		6"-2.8': Poorly-graded fine SAND (95% sand, 5% silt), tan, moist, no odor or sheen.	SP-SM		100	N/A	0.0			
5		2.8'-6.0': Poorly-graded SAND with silt and gravel (60% sand, 30% gravel, 10% silt), fine gravel and sand, dark-brown, moist, no odor or sheen.	SP							Bentonite
		6.0'-7.0': Poorly-graded fine SAND (95% sand, 5% silt), light-brown, moist, no odor or sheen.	ML		100	N/A	0.0			
10		7.0'-10.5': SILT (95% silt, 5% sand), fine sand, light brown, moist, no odor or sheen.	SP					B13-120108-10	X	Initial water level
		10.5'-11.5': Poorly-graded fine SAND (95% sand, 5% silt), tan, moist to wet, no odor or sheen. Observed water at 11.0' bgs.	SM		100	N/A	0.0			
15		11.5'-12.8': Silty SAND (80% sand, 20% silt), fine sand, tan, wet, no odor or sheen. Observed red-oxides b/w 12.6' to 12.8' bgs.	SP					B13-120108-14	X	
			SP					B13-120108-15-15.5	X	
		12.8'-13.2': Silty SAND (80% sand, 20% silt), brown, wet, no odor or sheen.	ML		90	N/A	0.0	B13-120108-18	X	
20		13.2'-16.0': Poorly-graded fine SAND (95% sand, 5% silt), black, wet, no odor or sheen.	SP							
		16.0'-16.5': SILT (100% silt), light-brown, wet, no odor or sheen.			95	N/A	0.0	B13-120108-22	X	
								Dup-B13-120108-22	X	
25		16.5'-25.0': Poorly-graded fine SAND (95% sand, 5% silt), black, wet, no odor or sheen.	SP							
		25.0'-32.5': Poorly-graded fine SAND (95% sand, 5% silt), brown, wet, no odor or sheen.			100	N/A	0.0	B13-120108-26	X	
30								B13-120108-30	X	
								B13-120108-30-30.5	X	
		32.5'-33.7': SILT (100% silt), light-brown, wet, no odor or sheen.	ML		100	N/A	0.0			Bentonite
35		33.7'-34.7': Poorly-graded fine SAND (95% sand, 5% silt), brown, wet, no odor or sheen.	SP					B13-120108-34	X	
		34.7'-35.3': SILT (95% silt, 5% sand), fine sand, light brown, wet, no odor or sheen.	ML							
			SP		100	N/A	0.0	B13-120108-38	X	
40		35.3'-41.5': Poorly-graded fine SAND (95% sand, 5% silt), brown, wet,								

Well Construction Information

Monument Type:	NA	**Filter Pack:**	NA	**Ground Surface Elevation (ft):**	NA
Casing Diameter (inches):	2-inch	**Surface Seal:**	Asphalt	**Top of Casing Elevation (ft):**	NA
Screen Slot Size (inches):	0.004	**Annular Seal:**	NA	**Boring Abandonment:**	Bentonite
Screened Interval (ft bgs):	4' intervals			**Surveyed Location:**	X: 47.330060754 Y: -122.195112269

FARALLON consulting
975 5th Avenue Northwest
Issaquah, Washington 98027

Log of Boring: B13

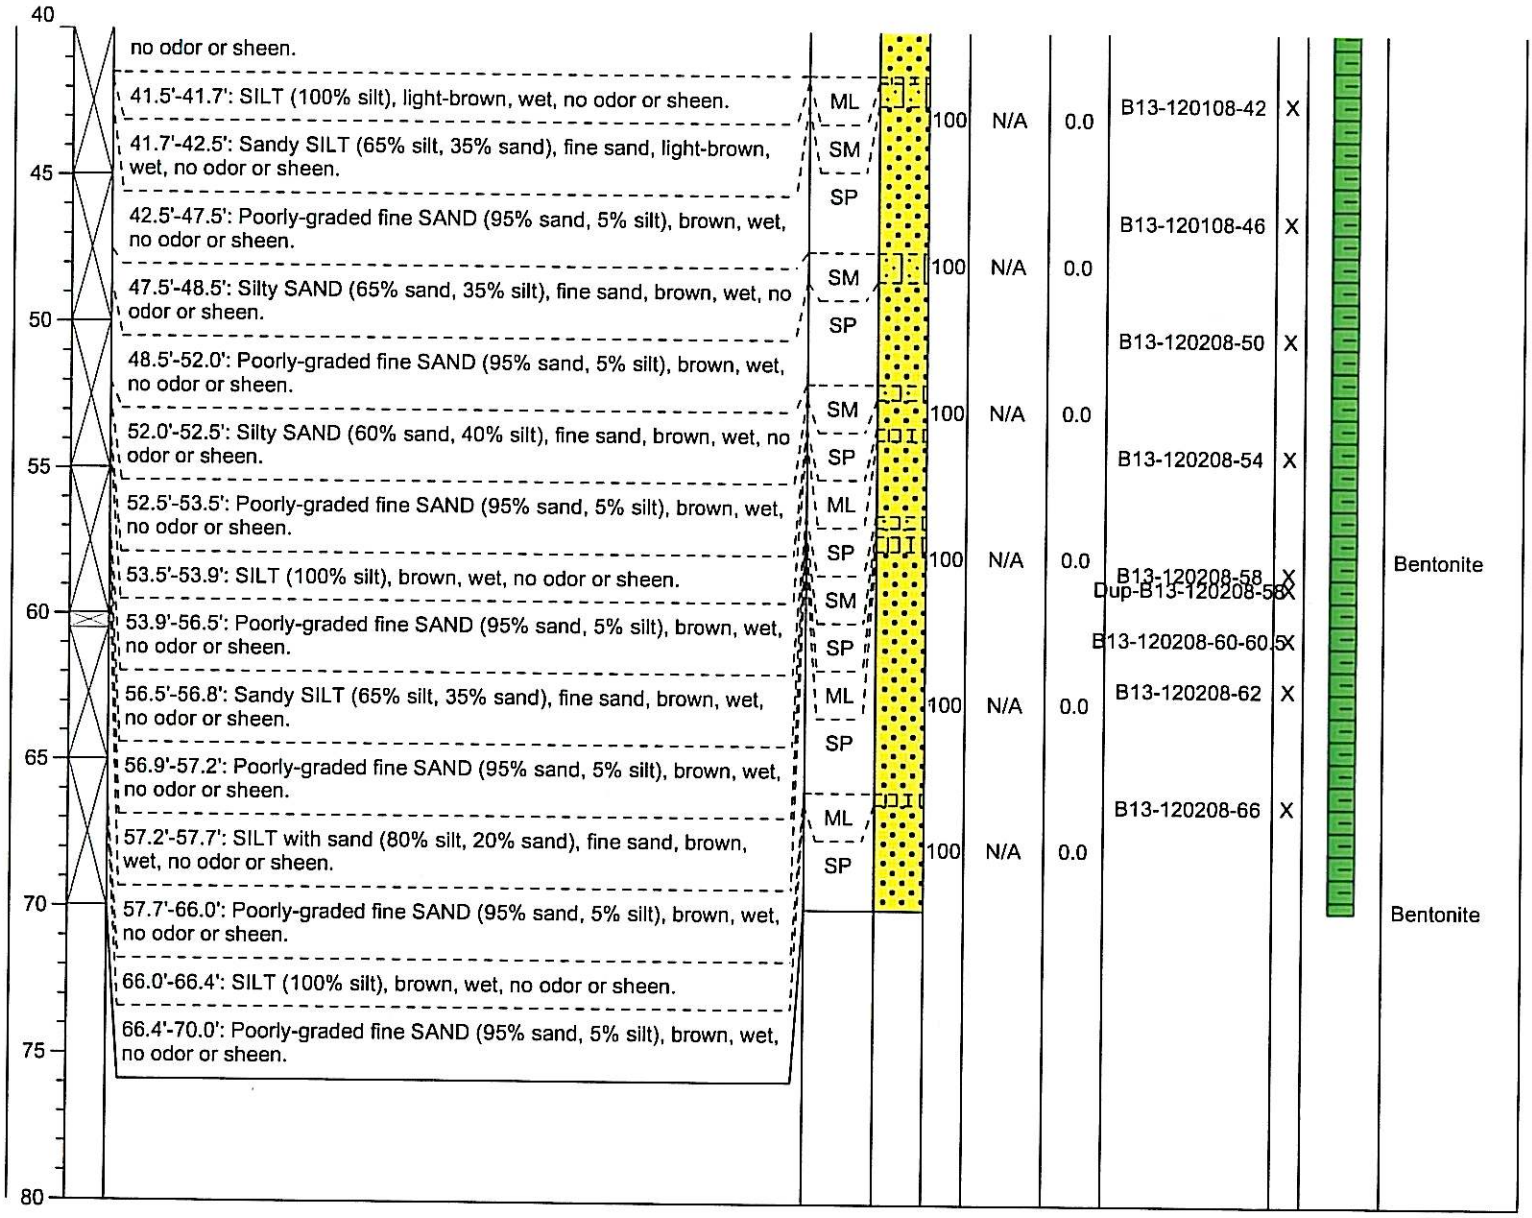

Well Construction Information

Monument Type:	NA	**Filter Pack:**	NA	**Ground Surface Elevation (ft):**	NA
Casing Diameter (inches):	2-inch	**Surface Seal:**	Asphalt	**Top of Casing Elevation (ft):**	NA
Screen Slot Size (inches):	0.004	**Annular Seal:**	NA	**Boring Abandonment:**	Bentonite
Screened Interval (ft bgs):	4' intervals			**Surveyed Location:**	**X:** 47.330060754 **Y:** -122.195112269

FARALLON consulting
975 5th Avenue Northwest
Issaquah, Washington 98027

Log of Boring: B14

Client: Capital Industries Inc.
Project: Capital Industries Inc.
Location: Seattle, WA

Farallon PN: 457-004

Logged By: Ken Scott

Date/Time Started:	12/04/2008 12:05	**Sampler Type:**	Macrocore 60-inch
Date/Time Completed:	12/05/2008 14:30	**Drive Hammer (lbs.):**	NA
Equipment:	Geoprobe 6600	**Depth of Water ATD (ft bgs):**	7.25' bgs
Drilling Company:	Cascade Drilling	**Total Boring Depth (ft bgs):**	70' bgs
Drilling Foreman:	Kasey Goble	**Total Well Depth (ft bgs):**	NA
Drilling Method:	Direct-push		

Depth (feet bgs.)	Sample Interval	Lithologic Description	USCS	USGS Graphic	% Recovery	Blow Counts 8/8/8	PID (ppm*)	Sample ID	Sample Analyzed	Boring/Well Construction Details
0		0-6": Asphalt, black, dry, odor and sheen.	AC							Asphalt cap
		6"-1.0': Silty SAND (60% sand, 40% silt), fine sand, dark-brown, moist, no odor or sheen.	SM		100	N/A	0.0	B14-120408-2	X	
5		1.0'-6.5': SILT (90% silt, 10% sand), fine sand, light-brown, moist, no odor or sheen.	ML					B14-120408-5	X	Bentonite
		6.5'-8.5': Silty SAND (65% sand, 35% silt), fine sand, tan, moist to wet, no odor or sheen. Observed red-oxides b/w 6.8' to 7.5' bgs.	SM		100	N/A	0.0	B14-120408-7	X	▽ Initial water level
		8.5'-10.5': Poorly-graded fine SAND (95% sand, 5% silt), fine sand, black, wet, no odor or sheen.	SP					B14-120408-8	X	
10		10.5'-11.0': Silty SAND (60% sand, 40% silt), fine sand, brown, wet, no odor or sheen.	SM							
		11.0'-33.0': Poorly-graded fine SAND (95% sand, 5% silt), black, wet, no odor or sheen. Observed red-oxides b/w 12.5' to 12.75' bgs. Observed wood-debris in sampler.	SP		100	N/A	0.0	B14-120408-12	X	
15								B14-120408-16	X	
					100	N/A	0.0			
20								B14-120408-20	X	
					100	N/A	0.0			
25								B14-120408-24	X	
					100	N/A	0.0			
30								B14-120508-28	X	
		33.0'-42.5': Sandy SILT (60% silt, 40% sand), fine sand, brown, wet, no odor or sheen.	ML		100	N/A	0.0	B14-120508-32	X	Bentonite
35								B14-120508-36	X	
					100	N/A	0.0			
40										

Well Construction Information


Monument Type: NA
Casing Diameter (inches): 2-inch
Screen Slot Size (inches): 0.004
Screened Interval (ft bgs): 4' intervals

Filter Pack: NA
Surface Seal: Asphalt
Annular Seal: NA

Ground Surface Elevation (ft): NA
Top of Casing Elevation (ft): NA
Boring Abandonment: Bentonite
Surveyed Location: X: 47.330146258 Y: -122.194828214

FARALLON consulting
975 5th Avenue Northwest
Issaquah, Washington 98027

Log of Boring: B14

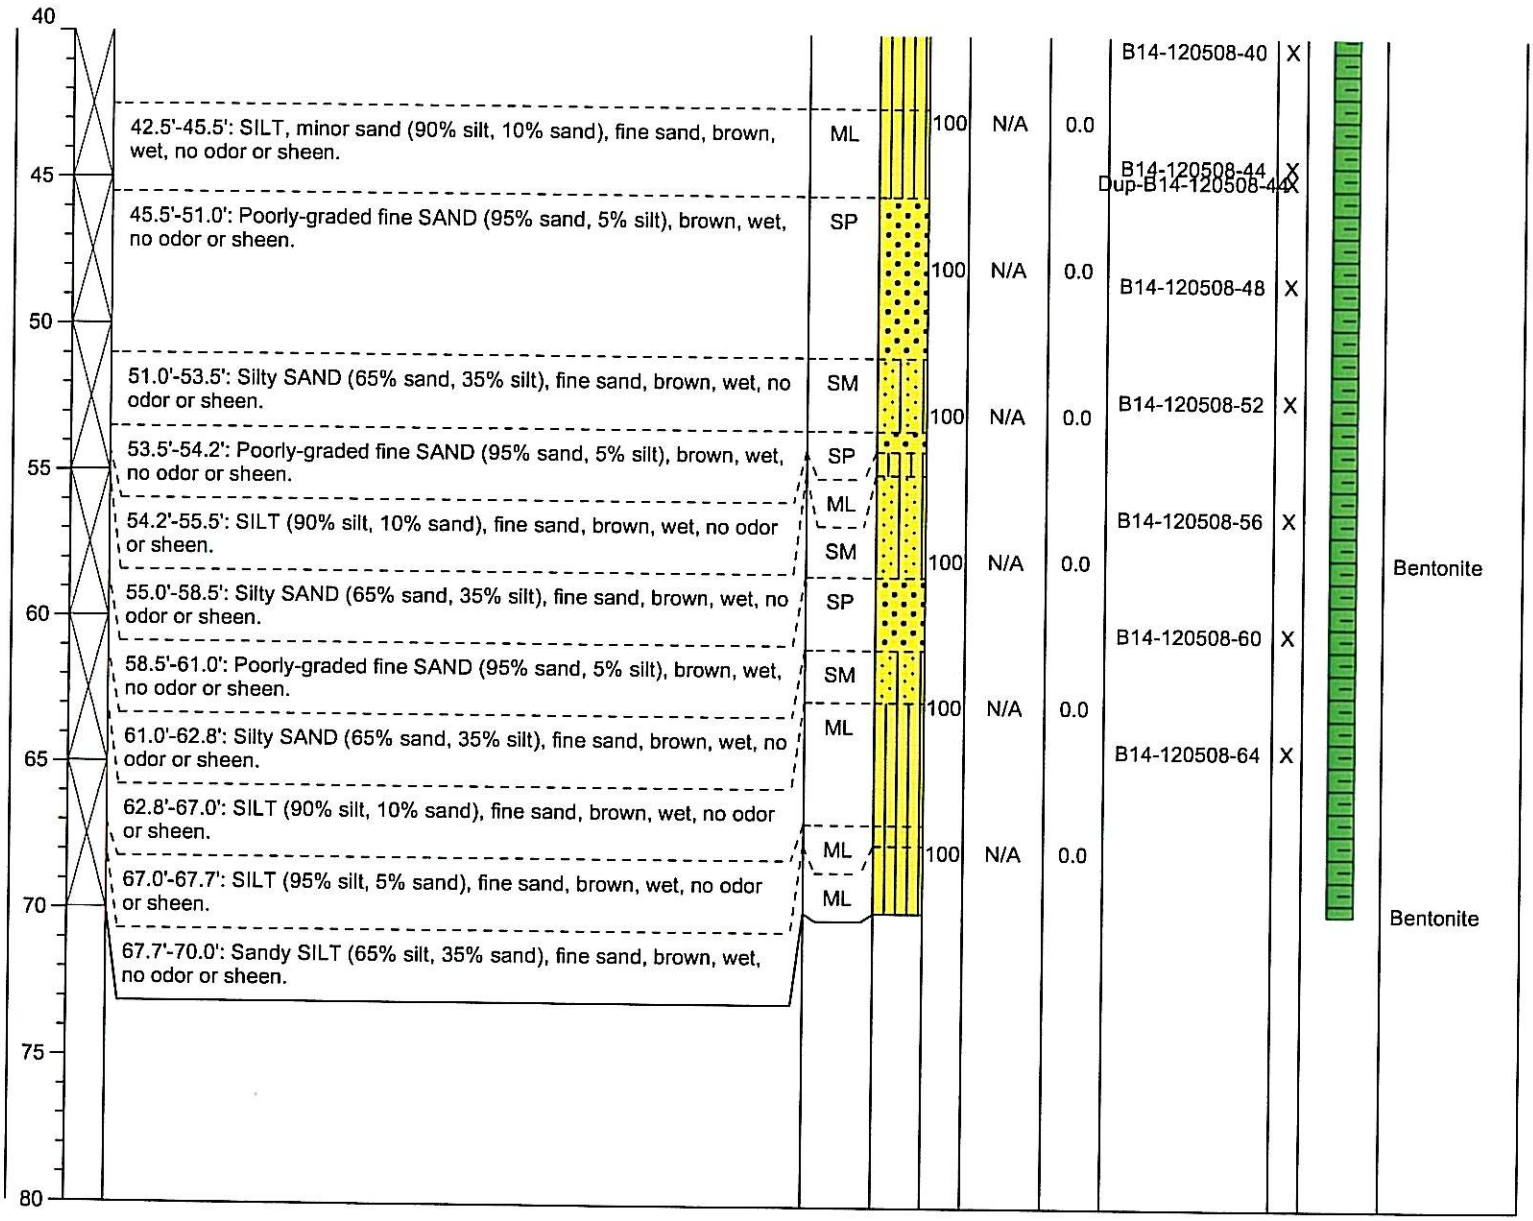

Well Construction Information

Monument Type:	NA	**Filter Pack:**	NA	**Ground Surface Elevation (ft):**	NA
Casing Diameter (inches):	2-inch	**Surface Seal:**	Asphalt	**Top of Casing Elevation (ft):**	NA
Screen Slot Size (inches):	0.004	**Annular Seal:**	NA	**Boring Abandonment:**	Bentonite
Screened Interval (ft bgs):	4' intervals			**Surveyed Location:**	X: 47.330146258 Y: -122.194828214

FARALLON consulting
975 5th Avenue Northwest
Issaquah, Washington 98027

Log of Boring: B15

Client: Capital Industries Inc.
Project: Capital Industries Inc.
Location: Seattle, WA
Farallon PN: 457-004
Logged By: Ken Scott

Date/Time Started:	12/02/2008 13:30	**Sampler Type:**	Macrocore 60-inch
Date/Time Completed:	12/04/2008 11:40	**Drive Hammer (lbs.):**	NA
Equipment:	Geoprobe 6600	**Depth of Water ATD (ft bgs):**	7.5' bgs
Drilling Company:	Cascade Drilling	**Total Boring Depth (ft bgs):**	70' bgs
Drilling Foreman:	Kasey Goble	**Total Well Depth (ft bgs):**	NA
Drilling Method:	Direct-push		


Depth (feet bgs.)	Sample Interval	Lithologic Description	USCS	USGS Graphic	% Recovery	Blow Counts 8/8/8	PID (ppm*)	Sample ID	Sample Analyzed	Boring/Well Construction Details
0		0-6": Asphalt, black, dry, odor and sheen.	AC							Asphalt cap
		6"-1.2': Poorly-graded fine SAND (95% sand, 5% silt), fine sand, tan, moist, no odor, slight monochromatic (white) sheen.	SP		100	N/A	0.0	B15-120208-2	X	
5		1.2'-1.8': Sandy SILT (65% silt, 35% sand), fine sand, dark-brown, moist, no odor or sheen.	ML							Bentonite
			SP					B15-120208-5	X	
		1.8'-4.0': Silty SAND (80% sand, 20% silt), light-brown, moist, no odor or sheen.	ML		100	N/A	0.0	B15-120208-7	X	▽ Initial water level
10		4.0'-5.5': SILT (90% silt, 10% sand), fine sand, light-brown, moist, no odor or sheen.	SM					B15-120208-8	X	
			ML							
		5.5'-6.5': Silty SAND (60% sand, 40% silt), fine sand, brown, moist, no odor or sheen.	SP		100	N/A	0.0	B15-120208-12	X	
15		6.5'-7.5': SILT with sand (75% silt, 25% sand), fine sand, light-brown, moist to slightly wet, no odor, slight monochromatic (white) sheen. Observed water at 7.5' bgs, and red-oxides b/w 6.5' to 7.5' bgs.						B15-120308-16	X	
		7.5'-17.5': Poorly-graded fine SAND (95% sand, 5% silt), black, wet, no odor or sheen. Observed red-oxides b/w 7.5 to 8.5' bgs.	SM		90	N/A	0.0			
20		17.5'-17.9': Silty SAND (65% sand, 35% silt), fine sand, brown, wet, no odor or sheen.	SP					B15-120308-20	X	
		17.9'-19.2': Poorly-graded fine SAND (95% sand, 5% silt), black, wet, no odor or sheen.	ML							
			SP		100	N/A	0.0			
25		19.2'-19.4': SILT (100% silt), light-brown, wet, no odor or sheen.						B15-120308-24	X	
		19.4'-26.5': Poorly-graded fine SAND (95% sand, 5% silt), black, wet, no odor or sheen.	ML		100	N/A	0.0			
		26.5'-27.0': SILT (100% silt), light-brown, wet, no odor or sheen.	SP					B15-120308-28	X	
30		27.0'-31.8': Poorly-graded fine SAND (95% sand, 5% silt), black, wet, no odor or sheen.								
		31.8'-32.0': SILT with sand (80% silt, 20% sand), fine sand, light-brown, wet, no odor or sheen.	ML		100	N/A	0.0	B15-120308-32	X	Bentonite
35		32.0'-37.0': Poorly-graded fine SAND (95% sand, 5% silt), black, wet, no odor or sheen.	SP					Dup-B15-120308-32	X	
								B15-120308-36	X	
		37.0'-37.4': SILT (95% silt, 5% sand), fine sand, light-brown, wet, no odor or sheen.	ML		100	N/A	0.0			
40			SP							

Well Construction Information

Monument Type:	NA	**Filter Pack:**	NA	**Ground Surface Elevation (ft):**	NA
Casing Diameter (inches):	2-inch	**Surface Seal:**	Asphalt	**Top of Casing Elevation (ft):**	NA
Screen Slot Size (inches):	0.004	**Annular Seal:**	NA	**Boring Abandonment:**	Bentonite
Screened Interval (ft bgs):	4' intervals			**Surveyed Location:**	X: 47.330150272 Y: -122.195017256

FARALLON consulting
975 5th Avenue Northwest
Issaquah, Washington 98027

Log of Boring: B15

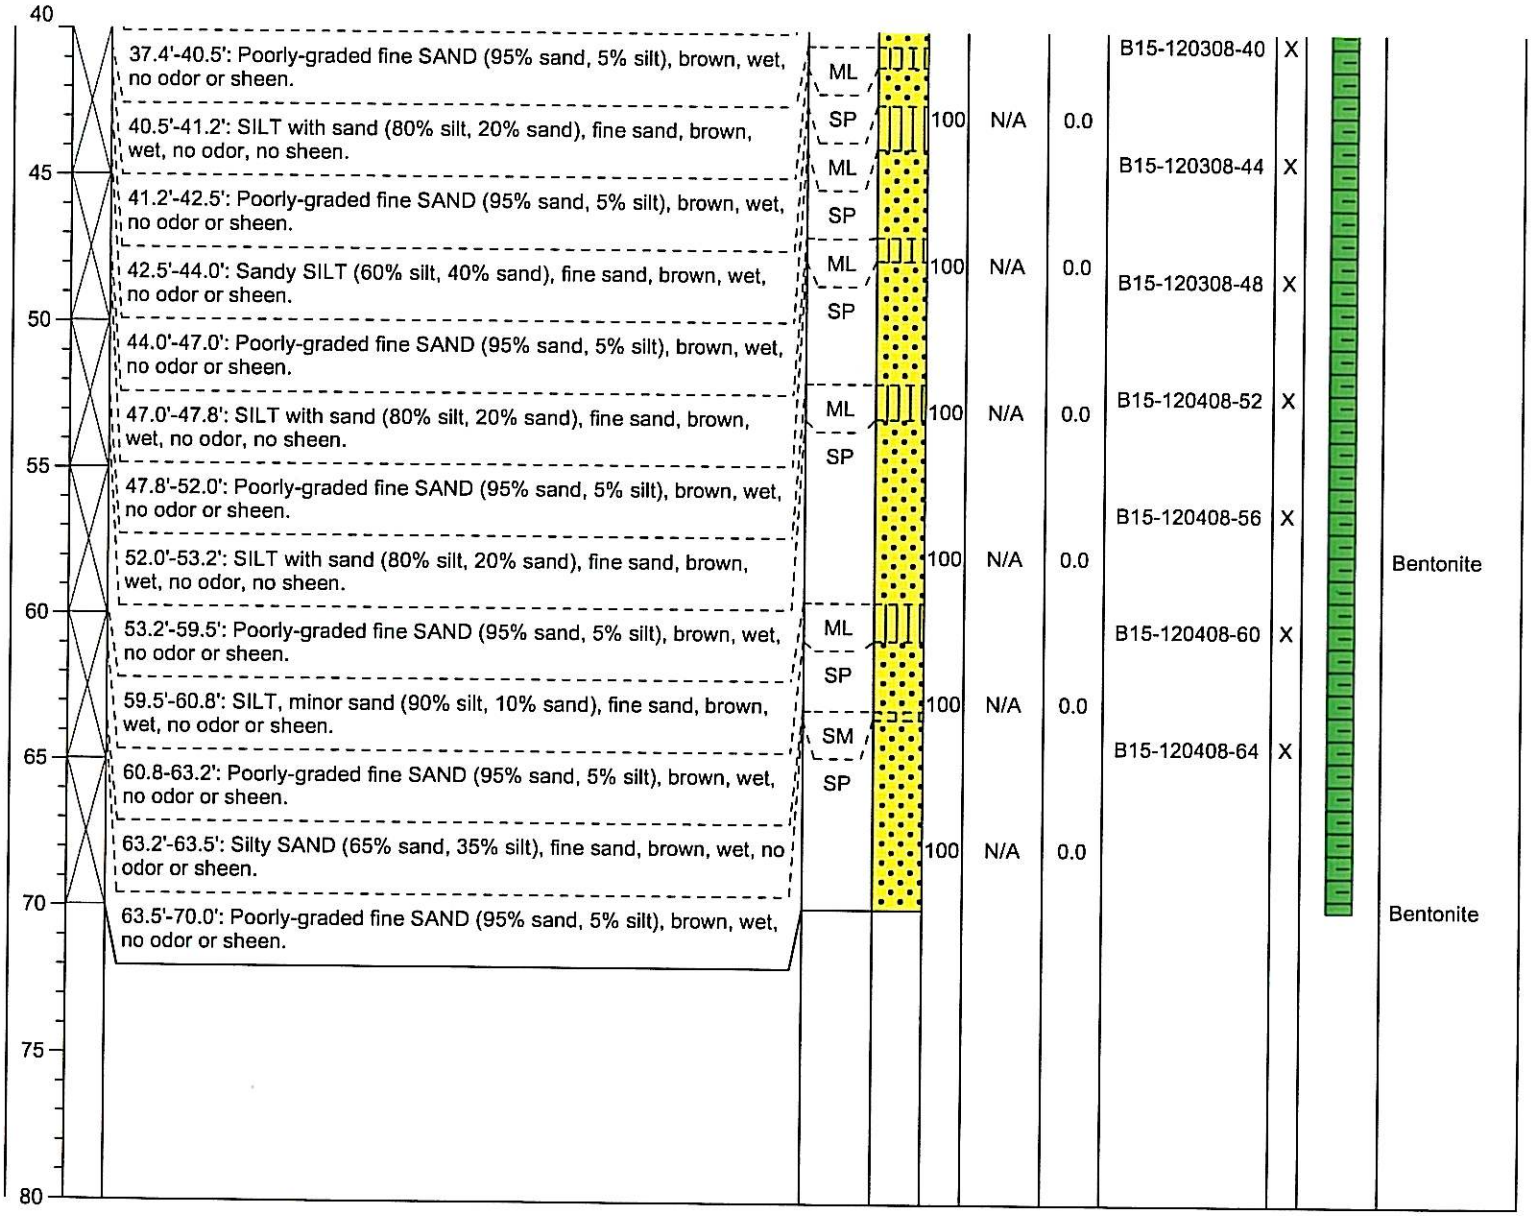

Well Construction Information

Monument Type:	NA	**Filter Pack:**	NA	**Ground Surface Elevation (ft):**	NA
Casing Diameter (inches):	2-inch	**Surface Seal:**	Asphalt	**Top of Casing Elevation (ft):**	NA
Screen Slot Size (inches):	0.004	**Annular Seal:**	NA	**Boring Abandonment:**	Bentonite
Screened Interval (ft bgs):	4' intervals			**Surveyed Location:**	**X:** 47.330150272 **Y:** -122.195017256

FARALLON consulting
975 5th Avenue Northwest
Issaquah, Washington 98027

Log of Boring: B16

Client: Capital Industries Inc.
Project: Capital Industries Inc.
Location: Seattle, WA

Farallon PN: 457-004

Logged By: Ken Scott

Date/Time Started:	11/11/2008 12:00	**Sampler Type:**	Macrocore 60-inch
Date/Time Completed:	11/12/2008 13:30	**Drive Hammer (lbs.):**	NA
Equipment:	Geoprobe 6600	**Depth of Water ATD (ft bgs):**	7.5' bgs
Drilling Company:	Cascade Drilling	**Total Boring Depth (ft bgs):**	70' bgs
Drilling Foreman:	Kasey Goble	**Total Well Depth (ft bgs):**	NA
Drilling Method:	Direct-push		


Depth (feet bgs.)	Sample Interval	Lithologic Description	USCS	USGS Graphic	% Recovery	Blow Counts 8/8/8	PID (ppm*)	Sample ID	Sample Analyzed	Boring/Well Construction Details
0		0.0-4": Asphalt, black, dry, odor and sheen.	AC							Asphalt cap
		4"-1.5': Poorly-graded fine SAND (95% sand, 5% silt), gray, moist, no odor or sheen.	SP		100	N/A	0.0			
5		1.5'-2.5': SILT (100% silt), dark-brown, moist, no odor or sheen.	ML							Bentonite
		2.5'-3.4': Poorly-graded fine SAND (95% sand, 5% silt), brown, moist, no odor or sheen.	SP							
		3.4'-7.5': Sandy SILT (65% silt, 35% sand), fine sand, light-brown, moist to wet, no odor or sheen. Observed water at 7.5' bgs, and red-oxides b/w 6.5 to 7.5' bgs.	ML		100	N/A	0.0	B16-111108-8	X	▽ Initial water level
10		7.5'-8.5': SILT with sand (80% silt, 20% sand), fine sand, gray, wet, no odor or sheen.	ML							
		8.5'-26.5': Poorly-graded fine SAND (95% sand, 5% silt), black, wet, no odor or sheen.	SP		100	N/A	0.0	B16-111108-12	X	
15								B16-111108-16	X	
					100	N/A	0.0	Dup-B16-111108-16	X	
20								B16-111108-20	X	
					100	N/A	0.0			
25								B16-111108-24	X	
		26.5'-27.4': Silty SAND (60% sand, 40% silt), fine sand, brown, wet, no odor or sheen.	SM		100	N/A	0.0	B16-111108-28	X	
		27.4'-45.5': Poorly-graded fine SAND (95% sand, 5% silt), black, wet, no odor or sheen.	SP							
30					100	N/A	0.0	B16-111208-32	X	Bentonite
35								B16-111208-36	X	
					100	N/A	0.0			
40										

Well Construction Information

Monument Type:	NA	**Filter Pack:**	NA	**Ground Surface Elevation (ft):**	NA
Casing Diameter (inches):	2-inch	**Surface Seal:**	Asphalt	**Top of Casing Elevation (ft):**	NA
Screen Slot Size (inches):	0.004	**Annular Seal:**	NA	**Boring Abandonment:**	Bentonite
Screened Interval (ft bgs):	4' intervals			**Surveyed Location:**	X: 47.330353867 Y: -122.194840773

FARALLON consulting
975 5th Avenue Northwest
Issaquah, Washington 98027

Log of Boring: B16

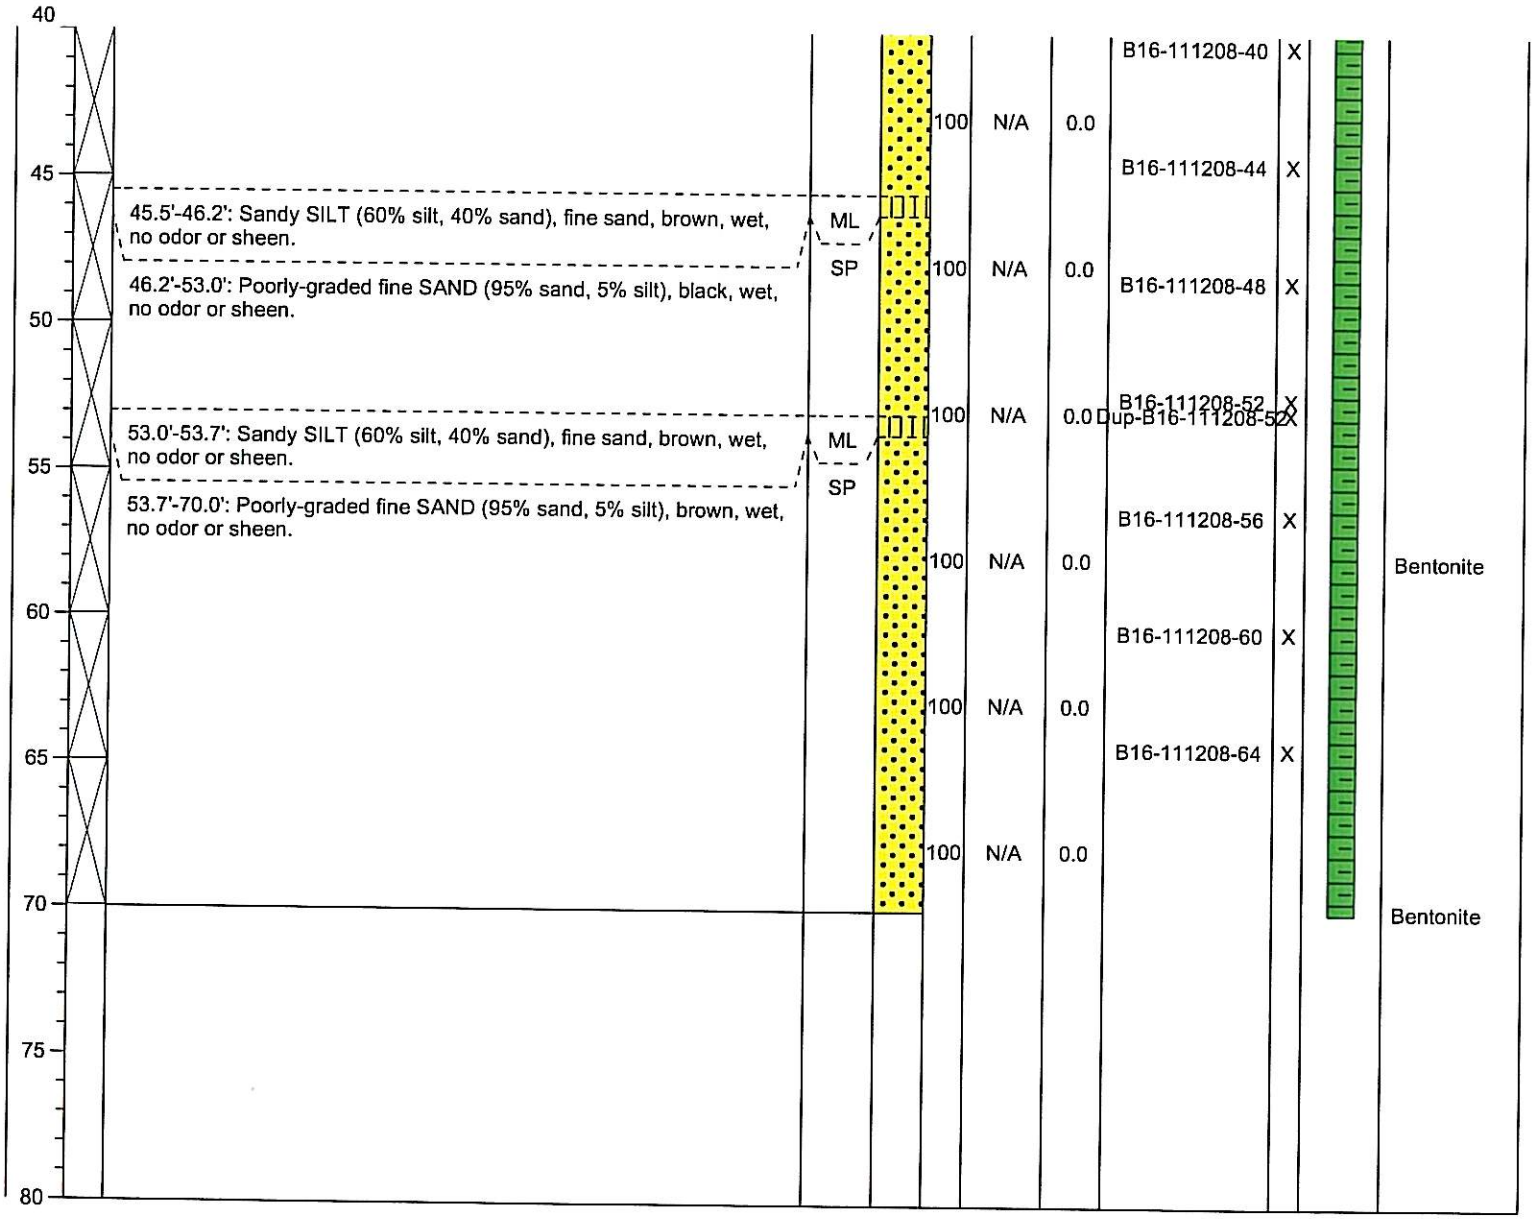

Well Construction Information

Monument Type:	NA	**Filter Pack:**	NA	**Ground Surface Elevation (ft):**	NA
Casing Diameter (inches):	2-inch	**Surface Seal:**	Asphalt	**Top of Casing Elevation (ft):**	NA
Screen Slot Size (inches):	0.004	**Annular Seal:**	NA	**Boring Abandonment:**	Bentonite
Screened Interval (ft bgs):	4' intervals			**Surveyed Location:**	X: 47.330353867 Y: -122.194840773

FARALLON consulting
975 5th Avenue Northwest
Issaquah, Washington 98027

Log of Boring: B17

Client: Capital Industries Inc.
Project: Capital Industries Inc.
Location: Seattle, WA
Farallon PN: 457-004
Logged By: Ken Scott

Date/Time Started:	11/10/2008 8:20	**Sampler Type:**	Macrocore 60-inch
Date/Time Completed:	11/11/2008 11:30	**Drive Hammer (lbs.):**	NA
Equipment:	Geoprobe 6600	**Depth of Water ATD (ft bgs):**	8.0' bgs
Drilling Company:	Cascade Drilling	**Total Boring Depth (ft bgs):**	70' bgs
Drilling Foreman:	Kasey Goble	**Total Well Depth (ft bgs):**	NA
Drilling Method:	Direct-push		


Depth (feet bgs.)	Sample Interval	Lithologic Description	USCS	USGS Graphic	% Recovery	Blow Counts 8/8/8	PID (ppm*)	Sample ID	Sample Analyzed	Boring/Well Construction Details
0		0-4": Asphalt, black, dry, odor and sheen.	AC							Asphalt cap
		4"-1.0': Poorly-graded fine SAND (95% sand, 5% silt), tan, moist, no odor or sheen.	SP		100	N/A	0.2			
5		1.0'-1.8': SILT (100% silt), dark brown, moist, no odor or sheen.	ML							Bentonite
		1.8'-7.5': SILT with sand (80% silt, 20% sand), fine sand, tan, moist, no odor or sheen.	ML							
		7.5'-24.0': Poorly-graded fine SAND (95% sand, 5% silt), black, moist to wet, no odor or sheen. Observed water at 8.0' bgs.	SP		100	N/A	4.5	B17-111008-8	X	Initial water level
10					100	N/A	13.7	B17-111008-12	X	
15								B17-111008-15-15.5	X	
					100	N/A	66.3	B17-111008-16	X	
20								B17-111008-20	X	
					100	N/A	116			
25		24.0'-25.0': Sandy SILT (65% silt, 35% sand), fine sand, brown, wet, sweet odor, no sheen.	ML					B17-111008-24	X	
		25.0'-26.5': Poorly-graded fine SAND (95% sand, 5% silt), black, wet, slight sweet odor, no sheen.	SP							
		26.5'-28.2': Sandy SILT (65% silt, 35% sand), fine sand, brown, wet, sweet odor, no sheen.	ML		100	N/A	306	B17-111008-28	X	
30			SP					B17-111008-30-30.5	X	
		28.2'-51.0': Poorly-graded fine SAND (95% sand, 5% silt), black, wet, sweet odor, no sheen.			100	N/A	218	B17-111008-32	X	Bentonite
35								B17-111008-36	X	
					100	N/A	191			
40										

Well Construction Information

Monument Type:	NA	**Filter Pack:**	NA	**Ground Surface Elevation (ft):**	NA
Casing Diameter (inches):	2-inch	**Surface Seal:**	Asphalt	**Top of Casing Elevation (ft):**	NA
Screen Slot Size (inches):	0.004	**Annular Seal:**	NA	**Boring Abandonment:**	Bentonite
Screened Interval (ft bgs):	4' intervals			**Surveyed Location:**	X: 47.330430687 Y: -122.194902296

FARALLON consulting
975 5th Avenue Northwest
Issaquah, Washington 98027

Log of Boring: B17

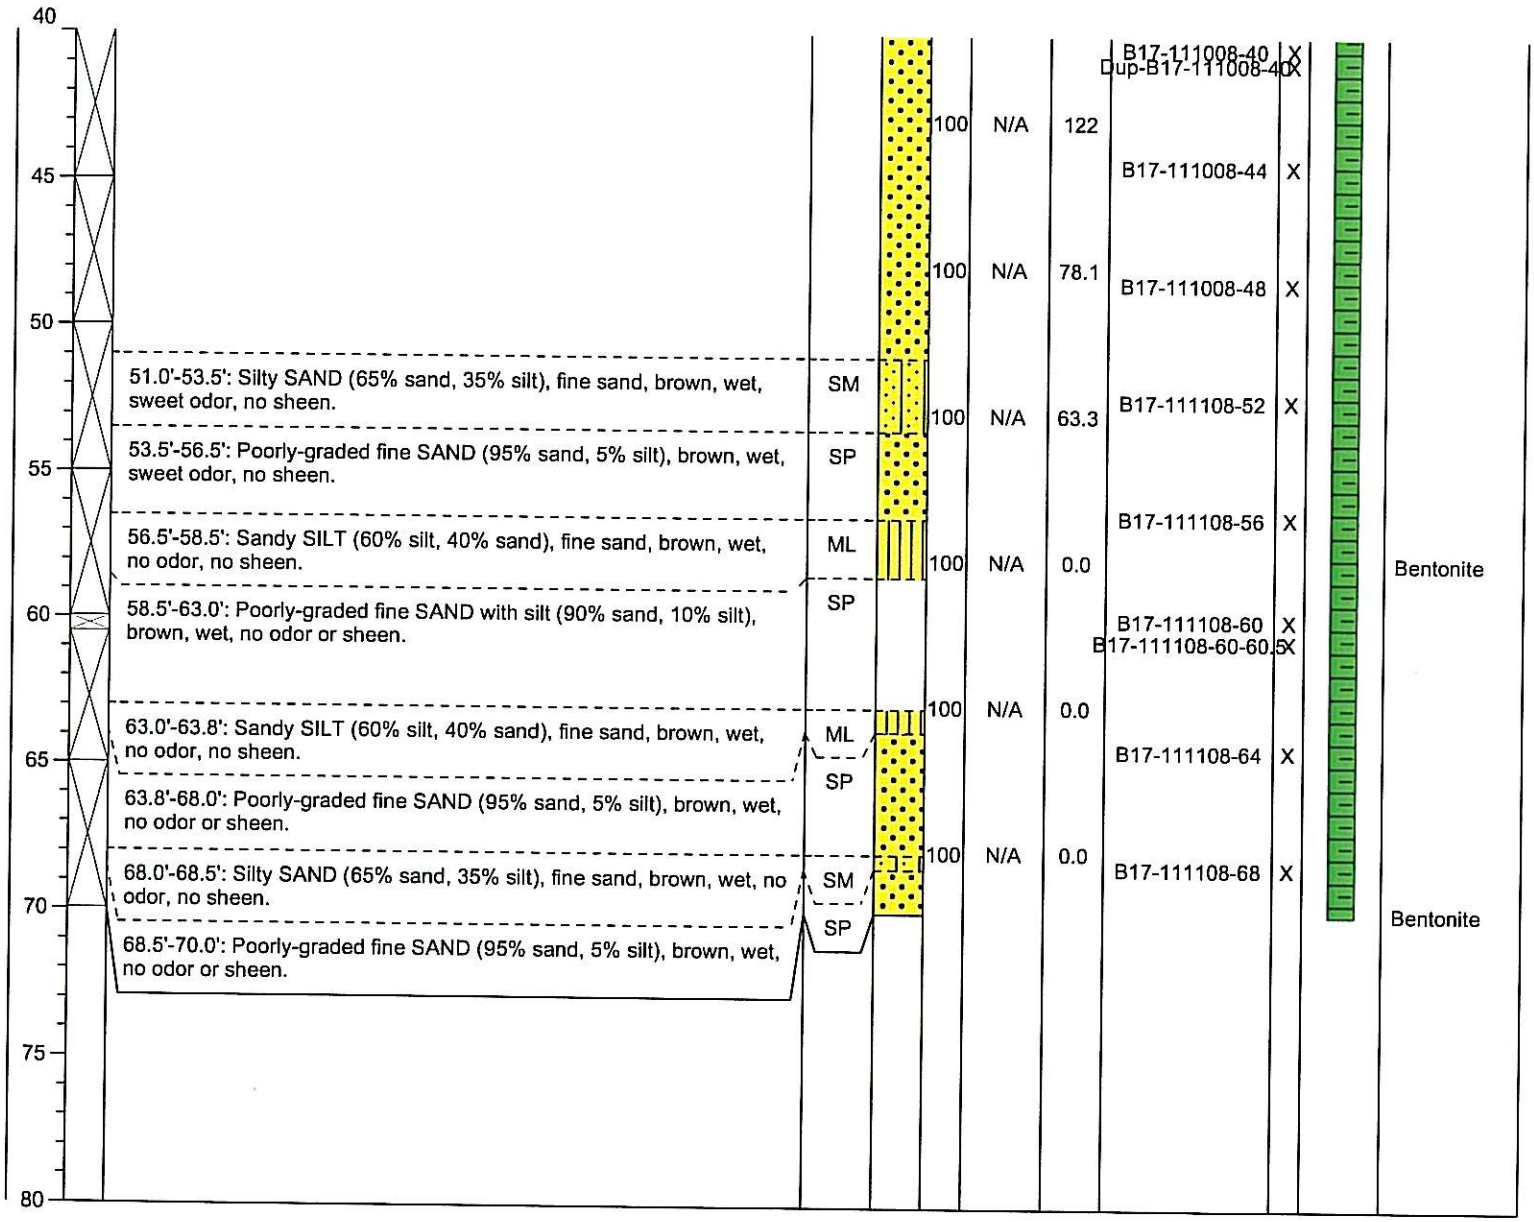

Well Construction Information

Monument Type:	NA	**Filter Pack:**	NA	**Ground Surface Elevation (ft):**	NA
Casing Diameter (inches):	2-inch	**Surface Seal:**	Asphalt	**Top of Casing Elevation (ft):**	NA
Screen Slot Size (inches):	0.004	**Annular Seal:**	NA	**Boring Abandonment:**	Bentonite
Screened Interval (ft bgs):	4' intervals			**Surveyed Location:**	X: 47.330430687 Y: -122.194902296

FARALLON consulting
975 5th Avenue Northwest
Issaquah, Washington 98027

Log of Boring: B18

Client: Capital Industries Inc.
Project: Capital Industries Inc.
Location: Seattle, WA
Farallon PN: 457-004
Logged By: Ken Scott

Date/Time Started:	12/09/2008 10:45	**Sampler Type:**	Macrocore 60-inch
Date/Time Completed:	12/09/2008 12:30	**Drive Hammer (lbs.):**	NA
Equipment:	Geoprobe 6600	**Depth of Water ATD (ft bgs):**	7.75' bgs
Drilling Company:	Cascade Drilling	**Total Boring Depth (ft bgs):**	15' bgs
Drilling Foreman:	Kasey Goble	**Total Well Depth (ft bgs):**	NA
Drilling Method:	Direct-push		

Depth (feet bgs.)	Sample Interval	Lithologic Description	USCS	USGS Graphic	% Recovery	Blow Counts 8/8/8	PID (ppm*)	Sample ID	Sample Analyzed	Boring/Well Construction Details
0		0-3": Concrete, white, dry, no odor or sheen.	CO							Concrete cap
		3"-2.5: Poorly-graded fine SAND with gravel (70% sand, 20% gravel, 5% silt), fine to medium sand, fine gravel, tan, moist, no odor, no sheen. Observed subangular to subrounded granite gravel.	SP					B18-120908-2	X	
		2.5-3.2': Poorly-graded fine SAND (95% sand, 5% silt), tan, moist, no odor or sheen.	SP		100	N/A	0.0			
		3.2-3.7': SILT (95% silt, 5% sand), fine sand, dark-brown, moist, no odor or sheen.	ML							Bentonite
		3.7'-5.5': SILT (100% silt), light-brown, moist, no odor or sheen. Observed red-oxides b/w 4.5' to 7.0' bgs.	ML							
5								B18-120908-5	X	
		5.5'-5.8': Silty SAND (80% sand, 20% silt), gray, moist, no odor or sheen.	SP							
		5.8'-9.0': SILT (95% silt, 5% sand), fine sand, light-brown, moist to wet, no odor or sheen.	ML							
								B18-120908-7	X	
					100	N/A	0.0	Dup-B18-120908-7	X	Initial water level
								B18-120908-8	X	
		9.0'-11.0': Poorly-graded fine SAND (95% sand, 5% silt), black, wet, no odor or sheen.	SP							
10		11.0'-11.4': GRAVEL with sand (80% gravel, 15% sand, 5% silt), fine gravel and sand, gray, wet, no odor or sheen.	GP							
		11.4'-15.0': Poorly-graded fine SAND (95% sand, 5% silt), black, wet, no odor or sheen.	SP		100	N/A	0.0			Bentonite
15										

Well Construction Information

Monument Type:	NA	**Filter Pack:**	NA	**Ground Surface Elevation (ft):**	NA
Casing Diameter (inches):	2-inch	**Surface Seal:**	Concrete	**Top of Casing Elevation (ft):**	NA
Screen Slot Size (inches):	0.004	**Annular Seal:**	NA	**Boring Abandonment:**	Bentonite
Screened Interval (ft bgs):	4' intervals			**Surveyed Location:**	X: 47.330234151 Y: -122.194731409

FARALLON consulting
975 5th Avenue Northwest
Issaquah, Washington 98027

Log of Boring: B19

Client: Capital Industries Inc.
Project: Capital Industries Inc.
Location: Seattle, WA
Farallon PN: 457-004
Logged By: Ken Scott

Date/Time Started:	6/30/09 0845	**Sampler Type:**	Macrocore 60-inch
Date/Time Completed:	6/30/09 1415	**Drive Hammer (lbs.):**	NA
Equipment:	Geoprobe 6600	**Depth of Water ATD (ft bgs):**	13' bgs
Drilling Company:	Cascade Drilling	**Total Boring Depth (ft bgs):**	78' bgs
Drilling Foreman:	Kasey Goble	**Total Well Depth (ft bgs):**	NA
Drilling Method:	Direct-push		


Depth (feet bgs.)	Sample Interval	Lithologic Description	USCS	% Recovery	Blow Counts 8/8/8	PID (ppm*)	Sample ID	Sample Analyzed	Boring/Well Construction Details
0		0-2": Asphalt, black, dry, odor and sheen.	AC						Asphalt cap
		2"-5': Silty SAND with gravel (70% sand, 15% silt, 15% gravel), fine grained sand, fine to coarse gravel, dark brown, moist, no odor, no sheen.	SM	100	N/A	0.4			Bentonite
5		5'-33': Poorly-graded SAND (95% sand, 5% silt), fine grained sand, black, moist to wet, no odor, no sheen.	SP	100	N/A	0.1			
10				100	N/A	0.0	B19-063009-10		▽ Initial water level
15							B19-063009-16		
20									
25				100	N/A	0.0	B19-063009-26		
30				100	N/A	0.0			Bentonite
35		33'-35': Poorly-graded SAND with silt (90% sand, 10% silt), fine grained sand, brown, wet, no odor, no sheen.	SP-SM						
		35'-42': Poorly-graded SAND (95% sand, 5% silt), fine grained sand, brown, wet, no odor, no sheen.	SP	100	N/A	0.0	B19-063009-38		
40									

Well Construction Information

Monument Type:	NA	**Filter Pack:**	NA	**Ground Surface Elevation (ft):**	NA
Casing Diameter (inches):	2-inch	**Surface Seal:**	Asphalt	**Top of Casing Elevation (ft):**	NA
Screen Slot Size (inches):	0.004	**Annular Seal:**	NA	**Boring Abandonment:**	Bentonite
Screened Interval (ft bgs):	4' intervals			**Surveyed Location:** X: NA	Y: NA

FARALLON consulting
975 5th Avenue Northwest
Issaquah, Washington 98027

Log of Boring: B19

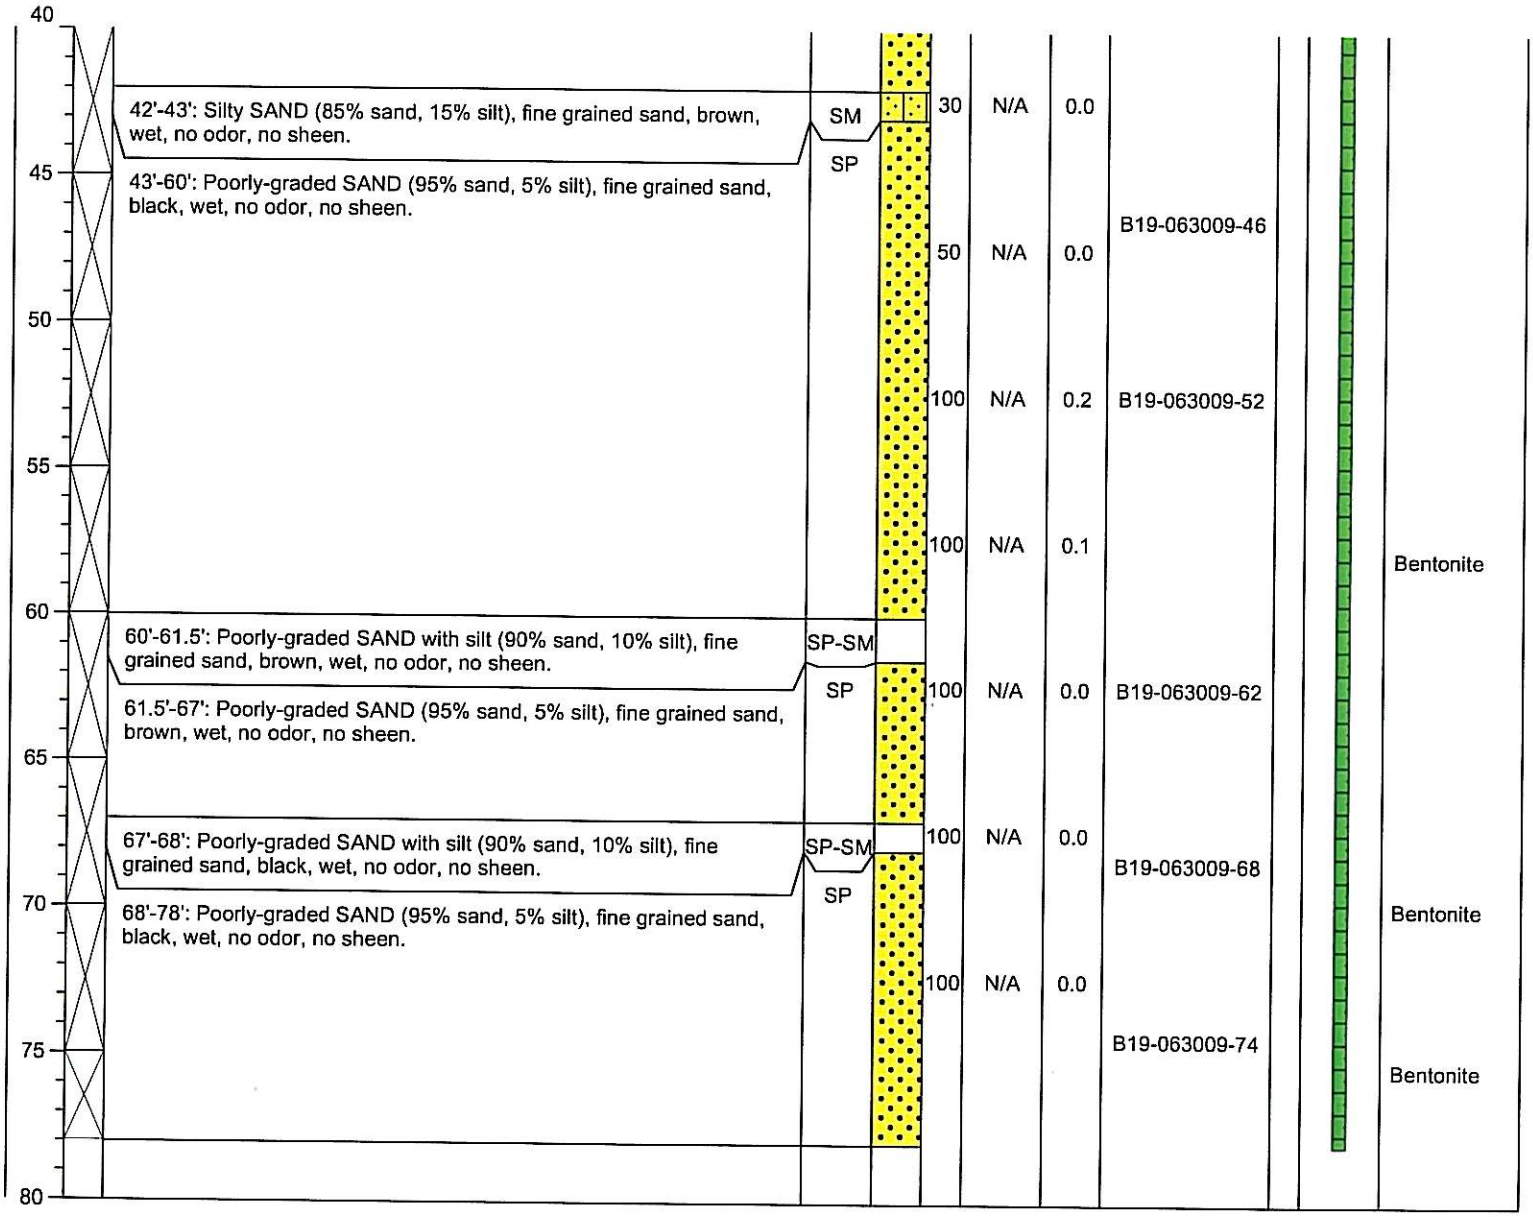

Well Construction Information

Monument Type:	NA	**Filter Pack:**	NA	**Ground Surface Elevation (ft):**	NA
Casing Diameter (inches):	2-inch	**Surface Seal:**	Asphalt	**Top of Casing Elevation (ft):**	NA
Screen Slot Size (inches):	0.004	**Annular Seal:**	NA	**Boring Abandonment:**	Bentonite
Screened Interval (ft bgs):	4' intervals			**Surveyed Location:** X: NA	Y: NA

FARALLON consulting
975 5th Avenue Northwest
Issaquah, Washington 98027

Log of Boring: B20

Client: Capital Industries Inc.
Project: Capital Industries Inc.
Location: Seattle, WA
Farallon PN: 457-004
Logged By: Ken Scott

Date/Time Started:	7/7/09 0845	**Sampler Type:**	Macrocore 60-inch
Date/Time Completed:	7/7/09 1350	**Drive Hammer (lbs.):**	NA
Equipment:	Geoprobe 6600	**Depth of Water ATD (ft bgs):**	12' bgs
Drilling Company:	Cascade Drilling	**Total Boring Depth (ft bgs):**	70' bgs
Drilling Foreman:	Kasey Goble	**Total Well Depth (ft bgs):**	NA
Drilling Method:	Direct-push		


Depth (feet bgs.)	Lithologic Description	USCS	% Recovery	Blow Counts 8/8/8	PID (ppm*)	Sample ID	Boring/Well Construction Details
0	0-2": Asphalt, black, dry, odor and sheen.	AC					Asphalt cap
	2"-7": Poorly-graded SAND with silt and gravel (70% sand, 20% gravel, 10% silt), fine grained sand, fine to coarse gravel, brown, moist, no odor, no sheen.	SP-SM	100	N/A	0.0		
5							Bentonite
	7'-8': Poorly-graded SAND (95% sand, 5% silt), fine grained sand, brown, moist, no odor, no sheen.	SP	100	N/A	0.0		
	8'-8.3': SILT (100% silt), tan, moist, no odor, no sheen.	ML					
10	8.3'-14.5': Poorly-graded SAND (95% sand, 5% silit), fine grained sand, brown, moist to wet, no odor, no sheen.	SP				B20-070709-10	Initial water level
	14.5'-14.8': SILT (100% silt), tan, wet, no odor, no sheen.	ML	100	N/A	0.0		
15	14.8'-20': Poorly-graded SAND (95% sand, 5% silt), fine grained sand, brown, wet, no odor, no sheen.	SP				B20-070709-16	
20	20'-34': Poorly-graded SAND (95% sand, 5% silt), fine grained sand, black, wet, no odor, no sheen.	SP	100	N/A	0.0		
25						B20-070709-24	
30			100	N/A	0.0	B20-070709-30	Bentonite
35	34'-34.3': SILT (90% silt, 10% sand), fine grained sand, tan, wet, no odor, no sheen.	ML					
	34.3'-41': Poorly-graded SAND (95% sand, 5% silt), fine grained sand, black, wet, no odor, no sheen.	SP	100	N/A	0.0	B20-070709-36	
40							

Well Construction Information

Monument Type: NA
Casing Diameter (inches): 2-inch
Screen Slot Size (inches): 0.004
Screened Interval (ft bgs): 4' intervals
Filter Pack: NA
Surface Seal: Asphalt
Annular Seal: NA
Ground Surface Elevation (ft): NA
Top of Casing Elevation (ft): NA
Boring Abandonment: Bentonite
Surveyed Location: X: NA Y: NA

FARALLON consulting
975 5th Avenue Northwest
Issaquah, Washington 98027

Log of Boring: B20

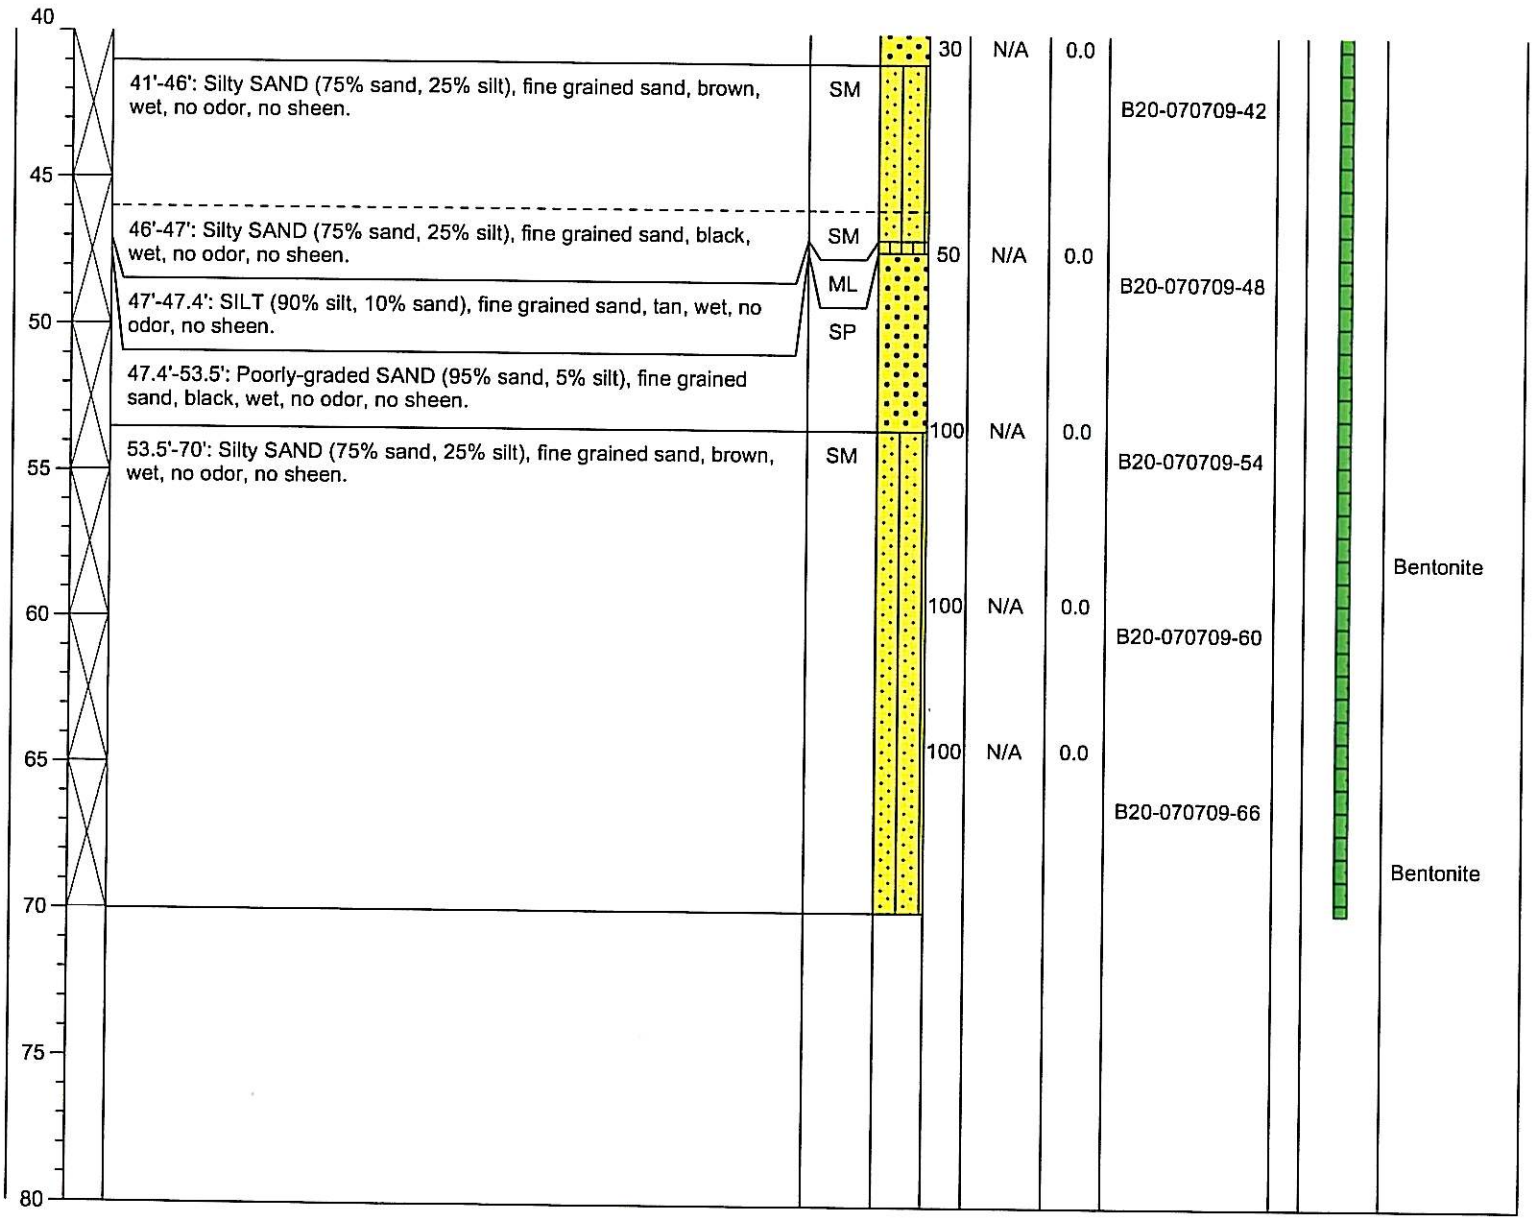

Well Construction Information

Monument Type:	NA	**Filter Pack:**	NA	**Ground Surface Elevation (ft):**	NA
Casing Diameter (inches):	2-inch	**Surface Seal:**	Asphalt	**Top of Casing Elevation (ft):**	NA
Screen Slot Size (inches):	0.004	**Annular Seal:**	NA	**Boring Abandonment:**	Bentonite
Screened Interval (ft bgs):	4' intervals			**Surveyed Location:** X: NA	Y: NA

FARALLON consulting
975 5th Avenue Northwest
Issaquah, Washington 98027

Log of Boring: B21

Client: Capital Industries Inc.
Project: Capital Industries Inc.
Location: Seattle, WA

Farallon PN: 457-004

Logged By: Ken Scott

Date/Time Started:	7/6/09 0900	**Sampler Type:**	Macrocore 60-inch
Date/Time Completed:	7/6/09 1400	**Drive Hammer (lbs.):**	NA
Equipment:	Geoprobe 6600	**Depth of Water ATD (ft bgs):**	13' bgs
Drilling Company:	Cascade Drilling	**Total Boring Depth (ft bgs):**	78' bgs
Drilling Foreman:	Elijah Floyd	**Total Well Depth (ft bgs):**	NA
Drilling Method:	Direct-push		

Depth (feet bgs.)	Sample Interval	Lithologic Description	USCS	% Recovery	Blow Counts 8/8/8	PID (ppm*)	Sample ID	Sample Analyzed	Boring/Well Construction Details
0		0-5": Asphalt, black, dry, odor and sheen.	AC						Asphalt cap
		5"-1': Poorly-graded GRAVEL with sand (70% gravel, 25% sand, 5% silt), fine grained sand, fine to coarse gravel, brown, moist, no odor, no sheen.	GP / CO	100	N/A	0.0			
5		1'-1.5': Concrete, white, dry, no odor, no sheen.	SP						Bentonite
		1.5'-6': Poorly-graded SAND (95% sand, 5% silt), fine grained sand, brown, moist, no odor, no sheen.	SP-SM	100	N/A	0.0			
10		6'-6.5': Poorly-graded SAND with silt (90% sand, 10% silt), fine grained sand, brown, moist, no odor, no sheen.	SP				B21-070609-10		
		6.5'-15.5': Poorly-graded SAND (95% sand, 5% silt), fine grained sand, brown, moist to wet, no odor, no sheen.		100	N/A	0.0			▽ Initial water level
15		15.5'-20': Silty SAND (75% sand, 25% silt), fine grained sand, brown, wet, no odor, no sheen.	SM	100	N/A	0.0	B21-070609-16		
20		20'-36': Poorly-graded SAND (95% sand, 5% silt), fine grained sand, black, wet, no odor, no sheen.	SP						
25				100	N/A	0.0	B21-070609-26		
30									
				100	N/A	0.0			Bentonite
35		36'-36.2': Wood Debris (100% wood debris), brown, wet, no odor, no sheen.	DB						
		36.2'-43.3': Silty SAND (75% sand, 25% silt), fine grained sand,	SM	100	N/A	0.0	B21-070609-38		
40									

Well Construction Information

Monument Type:	NA	**Filter Pack:**	NA	**Ground Surface Elevation (ft):**	NA
Casing Diameter (inches):	2-inch	**Surface Seal:**	Asphalt	**Top of Casing Elevation (ft):**	NA
Screen Slot Size (inches):	0.004	**Annular Seal:**	NA	**Boring Abandonment:**	Bentonite
Screened Interval (ft bgs):	4' intervals			**Surveyed Location:** X: NA	Y: NA

FARALLON consulting
975 5th Avenue Northwest
Issaquah, Washington 98027

Log of Boring: B21

Depth (feet bgs.)	Sample Interval	Lithologic Description	USCS	USGS Graphic	% Recovery	Blow Counts 8/8/8	PID (ppm)	Sample ID	Sample Analyzed	Well Construction Details
40		brown, wet, no odor, no sheen.			100	N/A	0.0			
45		43.3'-43.5': SILT (100% silt), brown, wet, no odor, no sheen.	ML							
		43.5'-56': Poorly-graded SAND (95% sand, 5% silt), fine grained sand, black, wet, no odor, no sheen.	SP					B21-070609-46		
50					100	N/A	0.0			
								B21-070609-52		
55		56'-58': SILT with sand (80% silt, 20% sand), fine grained sand, brown, wet, no odor, no sheen.	ML							Bentonite
		58'-67': Poorly-graded SAND (95% sand, 5% silt), fine grained sand, black, wet, no odor, no sheen.	SP		100	N/A	0.0			
60					100	N/A	0.0			
								B21-070609-62		
65					100	N/A	0.0			
		67'-73': SILT with sand (80% silt, 20% sand), fine grained sand, brown, wet, no odor, no sheen.	ML					B21-070609-68		Bentonite
70										
		73'-78': Poorly-graded SAND (95% sand, 5% silt), fine grained sand, black, wet, no odor, no sheen.	SP		100	N/A	0.0	B21-070609-74		Bentonite
75										
80										

Well Construction Information

Monument Type:	NA	**Filter Pack:**	NA	**Ground Surface Elevation (ft):**	NA
Casing Diameter (inches):	2-inch	**Surface Seal:**	Asphalt	**Top of Casing Elevation (ft):**	NA
Screen Slot Size (inches):	0.004	**Annular Seal:**	NA	**Boring Abandonment:**	Bentonite
Screened Interval (ft bgs):	4' intervals			**Surveyed Location:** X: NA	Y: NA

FARALLON consulting
975 5th Avenue Northwest
Issaquah, Washington 98027

Log of Boring: B22

Client: Capital Industries Inc.
Project: Capital Industries Inc.
Location: Seattle, WA

Farallon PN: 457-004

Logged By: Ken Scott

Date/Time Started:	7/9/09 0840	**Sampler Type:**	Macrocore 60-inch
Date/Time Completed:	7/9/09 1320	**Drive Hammer (lbs.):**	NA
Equipment:	Geoprobe 6600	**Depth of Water ATD (ft bgs):**	13' bgs
Drilling Company:	Cascade Drilling	**Total Boring Depth (ft bgs):**	68' bgs
Drilling Foreman:	Kasey Goble	**Total Well Depth (ft bgs):**	NA
Drilling Method:	Direct-push		


Depth (feet bgs.)	Lithologic Description	USCS	% Recovery	Blow Counts 8/8/8	PID (ppm*)	Sample ID	Boring/Well Construction Details
0	0'-3': Sandy SILT (65% silt, 35% sand), fine grained sand, brown, moist, no odor, no sheen.	ML	100	N/A	0.2		Asphalt cap
5	3'-14': Poorly-graded SAND (95% sand, 5% silt), fine grained sand, brown, moist to wet, no odor, no sheen.	SP	100	N/A	0.1		Bentonite
10						B22-070909-10	
15	14'-15.5': Silty SAND (70% sand, 30% silt), fine grained sand, brown, wet, odor, no sheen.	SM	100	N/A	0.0		Initial water level
	15.5'-16': SILT (90% silt, 10% sand), fine grained sand, tan, wet, odor, no sheen.	ML					
20	16'-22': Poorly-graded SAND (95% sand, 5% silt), fine grained sand, brown, wet, odor, no sheen.	SP				B22-070909-18	
25	22'-30': Poorly-graded SAND (95% sand, 5% silt), fine grained sand, brown, wet, slight odor, no sheen.	SP	100	N/A	0.0		
			100	N/A	0.0	B22-070909-26	
30	30'-32': Silty SAND (70% sand, 30% silt), fine grained sand, brown, wet, slight odor, no sheen.	SM					
35	32'-38': SILT with sand (75% silt, 25% sand), fine grained sand, brown, wet, slight odor, no sheen.	ML	100	N/A	0.0	B22-070909-34	Bentonite
40	38'-39': SILT with sand (75% silt, 25% sand), fine grained sand, brown, wet, no odor, no sheen.	ML	100	N/A	0.0		

Well Construction Information

Monument Type:	NA	**Filter Pack:**	NA	**Ground Surface Elevation (ft):**	NA
Casing Diameter (inches):	2-inch	**Surface Seal:**	Asphalt	**Top of Casing Elevation (ft):**	NA
Screen Slot Size (inches):	0.004	**Annular Seal:**	NA	**Boring Abandonment:**	Bentonite
Screened Interval (ft bgs):	4' intervals			**Surveyed Location:** X: NA	Y: NA

FARALLON consulting
975 5th Avenue Northwest
Issaquah, Washington 98027

Log of Boring: B22

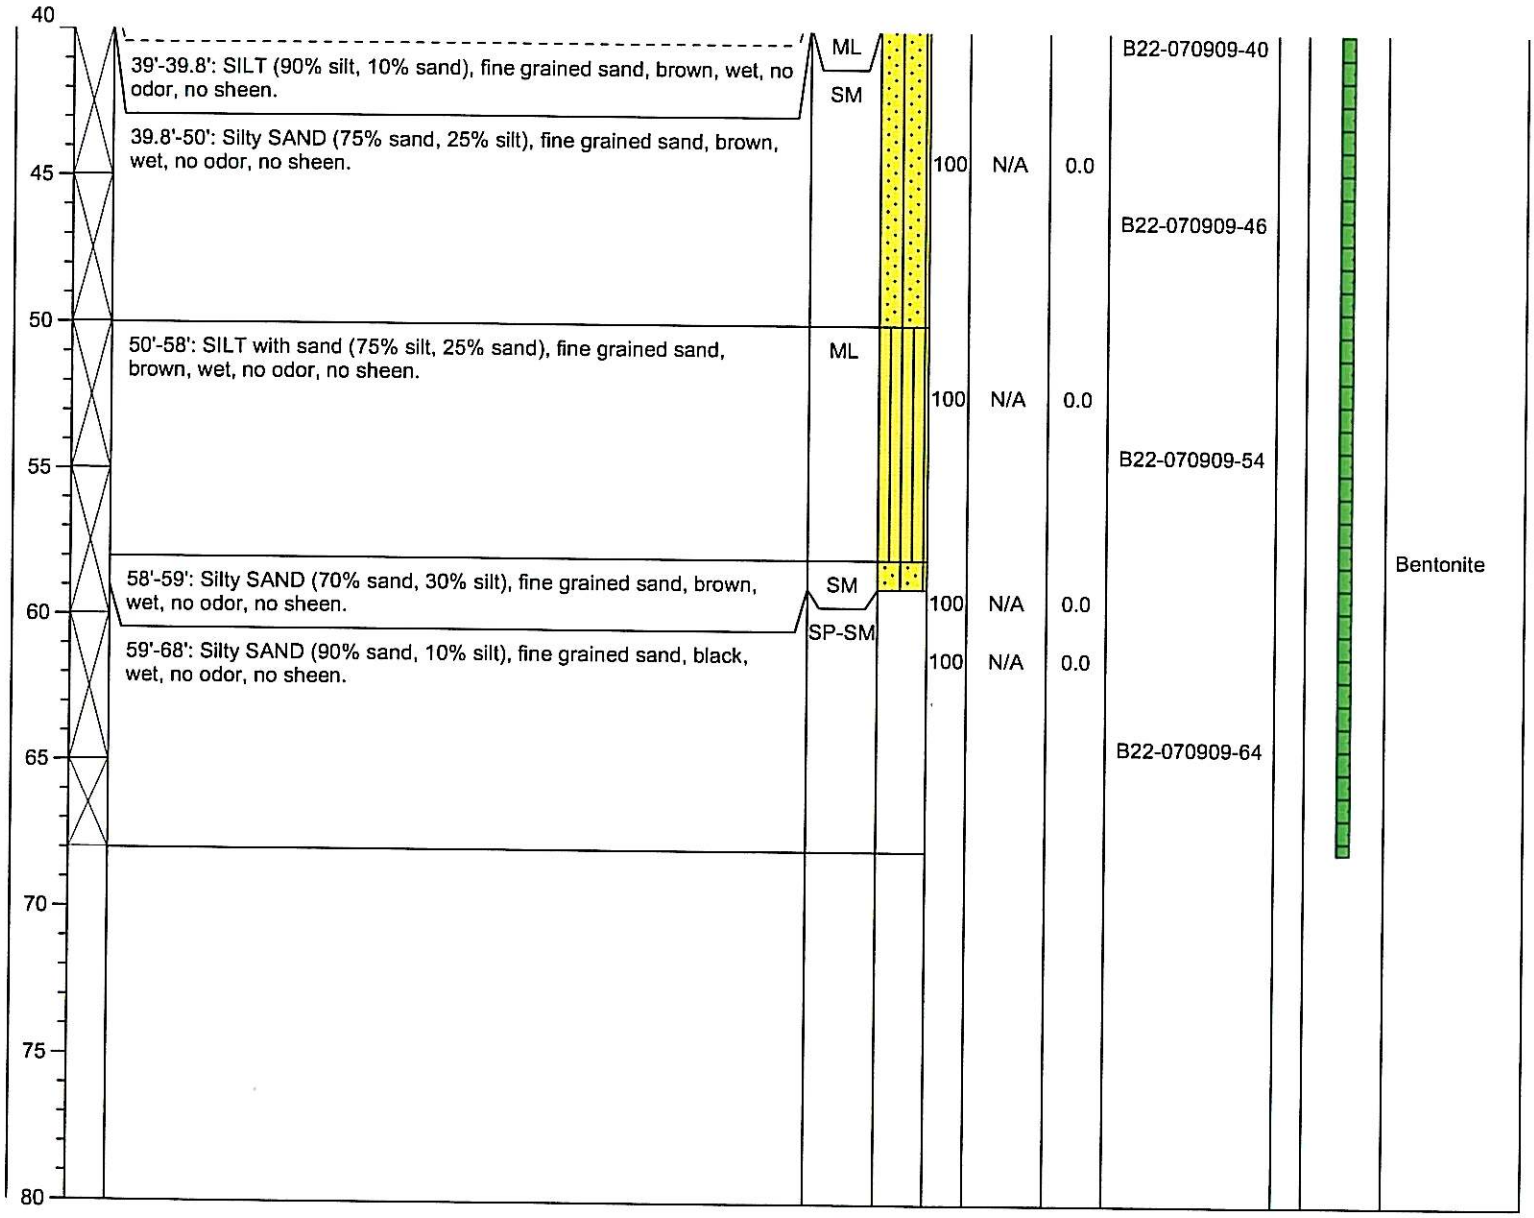

Well Construction Information

Monument Type:	NA	**Filter Pack:**	NA	**Ground Surface Elevation (ft):**	NA
Casing Diameter (inches):	2-inch	**Surface Seal:**	Asphalt	**Top of Casing Elevation (ft):**	NA
Screen Slot Size (inches):	0.004	**Annular Seal:**	NA	**Boring Abandonment:**	Bentonite
Screened Interval (ft bgs):	4' intervals			**Surveyed Location:** X: NA	Y: NA

FARALLON consulting
975 5th Avenue Northwest
Issaquah, Washington 98027

Log of Boring: B23

Client: Capital Industries Inc.
Project: Capital Industries Inc.
Location: Seattle, WA

Farallon PN: 457-004

Logged By: Ken Scott

Date/Time Started:	7/1/09 0825	**Sampler Type:**	Macrocore 60-inch
Date/Time Completed:	7/1/09 1445	**Drive Hammer (lbs.):**	NA
Equipment:	Geoprobe 6600	**Depth of Water ATD (ft bgs):**	12' bgs
Drilling Company:	Cascade Drilling	**Total Boring Depth (ft bgs):**	74' bgs
Drilling Foreman:	Kasey Goble	**Total Well Depth (ft bgs):**	NA
Drilling Method:	Direct-push		

Depth (feet bgs.)	Sample Interval	Lithologic Description	USCS	USGS Graphic	% Recovery	Blow Counts 8/8/8	PID (ppm*)	Sample ID	Sample Analyzed	Boring/Well Construction Details
0		0-2": Asphalt, black, dry, no odor, no sheen.	AC							Asphalt cap
		3"-5': Poorly-graded SAND (85% sand, 10% gravel, 5% silt), fine grained sand, fine to coarse gravel, brown, moist, no odor, no sheen.	SP-SM		100	N/A	0.1			
5		5'-14': Poorly-graded SAND (95% sand, 5% silt), fine grained sand, black, moist to wet, no odor, no sheen.	SP		100	N/A	0.4			Bentonite
10								B23-070109-10		Initial water level
15		14'-15': Poorly-graded SAND with silt (90% sand, 10% silt), fine grained sand, brown, wet, no odor, no sheen.	SP-SM							
		15'-38': Poorly-graded SAND (95% sand, 5% silt), fine grained sand, black, wet, no odor, no sheen.	SP		100	N/A	0.1	B23-070109-16		
20					100	N/A	0.0			
								B23-070109-22		
25					100	N/A	0.0			
								B23-070109-28		
30										Bentonite
35					100	N/A	0.0	B23-070109-34		
					100	N/A	0.0			
40		38'-38.5': Poorly-graded SAND with silt (90% sand, 10% silt), fine grained sand, brown, wet, no odor, no sheen.	SP-SM							

Well Construction Information

Monument Type: NA
Casing Diameter (inches): 2-inch
Screen Slot Size (inches): 0.004
Screened Interval (ft bgs): 4' intervals

Filter Pack: NA
Surface Seal: Asphalt
Annular Seal: NA

Ground Surface Elevation (ft): NA
Top of Casing Elevation (ft): NA
Boring Abandonment: Bentonite
Surveyed Location: X: NA Y: NA

FARALLON consulting
975 5th Avenue Northwest
Issaquah, Washington 98027

Log of Boring: B23

Depth (feet bgs.)	Sample Interval	Lithologic Description	USCS	USGS Graphic	% Recovery	Blow Counts 8/8/8	PID (ppm)	Sample ID	Sample Analyzed	Well Construction Details
40		38.5'-44.5': Poorly-graded SAND (95% sand, 5% silt), fine grained sand, black, wet, no odor, no sheen.	SP					B23-070109-40		
45		44.5'-45': SILT (100% silt), brown, wet, no odor, no sheen.	ML		100	N/A	0.0			
		45'-50.5': Silty SAND (75% sand, 25% silt), fine grained sand, brown, wet, no odor, no sheen.	SM					B23-070109-46		
50		50.5'-51': SILT (100% silt), brown, wet, no odor, no sheen.	ML		100	N/A	0.2			
		51'-56.5': Silty SAND (75% sand, 25% silt), fine grained sand, brown, wet, no odor, no sheen.	SM					B23-070109-52		
55					100	N/A	0.1			
		56.5'-63.5': Poorly-graded SAND (95% sand, 5% silt), fine grained sand, black, wet, no odor, no sheen.	SP					B23-070109-58		Bentonite
60										
65		63.5'-68.4': Poorly-graded SAND with silt (90% sand, 10% silt), fine grained sand, brown, wet, no odor, no sheen.	SP-SM		100	N/A	0.0	B23-070109-64		Bentonite
		68.4'-74': Poorly-graded SAND (95% sand, 5% silt), fine grained sand, black, wet, no odor, no sheen.	SP							
70					100	N/A	0.0	B23-070109-70		
										Bentonite
75										
80										

Well Construction Information

Monument Type:	NA	**Filter Pack:**	NA	**Ground Surface Elevation (ft):**	NA
Casing Diameter (inches):	2-inch			**Top of Casing Elevation (ft):**	NA
Screen Slot Size (inches):	0.004	**Surface Seal:**	Asphalt	**Boring Abandonment:**	Bentonite
Screened Interval (ft bgs):	4' intervals	**Annular Seal:**	NA	**Surveyed Location:** X: NA	Y: NA

FARALLON consulting
975 5th Avenue Northwest
Issaquah, Washington 98027

Log of Boring: B24

Client: Capital Industries Inc.
Project: Capital Industries Inc.
Location: Seattle, WA
Farallon PN: 457-004
Logged By: Ken Scott

Date/Time Started:	7/2/09 0830	**Sampler Type:**	Macrocore 60-inch
Date/Time Completed:	7/2/09 1330	**Drive Hammer (lbs.):**	NA
Equipment:	Geoprobe 6600	**Depth of Water ATD (ft bgs):**	11' bgs
Drilling Company:	Cascade Drilling	**Total Boring Depth (ft bgs):**	70' bgs
Drilling Foreman:	Kasey Goble, Frank Scott and Elijah Floyd	**Total Well Depth (ft bgs):**	NA
Drilling Method:	Direct-push		

Depth (feet bgs.)	Sample Interval	Lithologic Description	USCS	USGS Graphic	% Recovery	Blow Counts 8/8/8	PID (ppm*)	Sample ID	Sample Analyzed	Boring/Well Construction Details
0		0-3": Asphalt, black, dry, odor and sheen.	AC							Asphalt cap
		3"-15': Poorly-graded SAND (85% sand, 10% gravel, 5% silt), fine grained sand, fine to coarse gravel, brown, moist to wet, no odor, no sheen.	SP		100	N/A	0.0			
5					100	N/A	0.4			Bentonite
10								B24-070209-10		Initial water level
15		15'-15.4': SILT (100% silt), brown, wet, no odor, no sheen.	ML		100	N/A	0.0			
		15.4'-21': Poorly-graded SAND (95% sand, 5% silt), fine grained sand, brown, wet, no odor, no sheen.	SP					B24-070209-16		
20		21'-21.5': Poorly-graded SAND with silt (90% sand, 10% silt), fine grained sand, brown, wet, no odor, no sheen.	SP-SM		100	N/A	0.0			
		21.5'-40.8': Poorly-graded SAND (95% sand, 5% silt), fine grained sand, black, wet, no odor, no sheen.	SP					B24-070209-24		
25										
30					100	N/A	0.0	B24-070209-30		Bentonite
35					100	N/A	0.0			
								B24-070209-36		
40										

Well Construction Information

Monument Type: NA
Casing Diameter (inches): 2-inch
Screen Slot Size (inches): 0.004
Screened Interval (ft bgs): 4' intervals
Filter Pack: NA
Surface Seal: Asphalt
Annular Seal: NA
Ground Surface Elevation (ft): NA
Top of Casing Elevation (ft): NA
Boring Abandonment: Bentonite
Surveyed Location: X: NA Y: NA

FARALLON consulting
975 5th Avenue Northwest
Issaquah, Washington 98027

Log of Boring: B24

Depth (feet bgs.)	Sample Interval	Lithologic Description	USCS	USGS Graphic	% Recovery	Blow Counts 8/8/8	PID (ppm)	Sample ID	Sample Analyzed	Well Construction Details
40		40.8'-41.5': SILT (100% silt), brown, wet, no odor, no sheen.	ML		100	N/A	0.0			
		41.5'-46.5': Poorly-graded SAND (95% sand, 5% silt), fine grained sand, black, wet, no odor, no sheen.	SP					B24-070209-42		
45		46.5'-48': Poorly-graded SAND with silt (90% sand, 10% silt), fine grained sand, brown, wet, no odor, no sheen.	SP-SM		100	N/A	0.0			
		48'-55': Poorly-graded SAND (95% sand, 5% silt), fine grained sand, black, wet, no odor, no sheen.	SP					B24-070209-50		
50										
55		55'-55.5': Wood debris (100% wood debris), brown, wet, no odor, no sheen.	DB		30	N/A	0.0			
					50	N/A	0.0			
		55.5'-63': Poorly-graded SAND (95% sand, 5% silt), fine grained sand, black, wet, no odor, no sheen.	SP					B24-070209-58		Bentonite
60										
					100	N/A	0.0			
65		63'-63.8': Poorly-graded SAND with silt (90% sand, 10% silt), fine grained sand, brown, wet, no odor, no sheen.	SP-SM							
		63.8'-70': Poorly-graded SAND (95% sand, 5% silt), fine grained sand, black, wet, no odor, no sheen.	SP					B24-070209-66		
70										Bentonite
75										
80										

Well Construction Information

Monument Type:	NA	**Filter Pack:**	NA	**Ground Surface Elevation (ft):**	NA
Casing Diameter (inches):	2-inch	**Surface Seal:**	Asphalt	**Top of Casing Elevation (ft):**	NA
Screen Slot Size (inches):	0.004	**Annular Seal:**	NA	**Boring Abandonment:**	Bentonite
Screened Interval (ft bgs):	4' intervals			**Surveyed Location:** X: NA	Y: NA

FARALLON consulting
975 5th Avenue Northwest
Issaquah, Washington 98027

Log of Boring: B25

Client: Capital Industries Inc.
Project: Capital Industries Inc.
Location: Seattle, WA

Farallon PN: 457-004

Logged By: Ken Scott

Date/Time Started:	7/30/09 0825	**Sampler Type:**	Macrocore 60-inch
Date/Time Completed:	7/30/09 0920	**Drive Hammer (lbs.):**	NA
Equipment:	Geoprobe 6600	**Depth of Water ATD (ft bgs):**	10' bgs
Drilling Company:	Cascade Drilling	**Total Boring Depth (ft bgs):**	10' bgs
Drilling Foreman:	Kasey Goble	**Total Well Depth (ft bgs):**	NA
Drilling Method:	Direct-push		

Depth (feet bgs.)	Sample Interval	Lithologic Description	USCS	% Recovery	Blow Counts 8/8/8	PID (ppm*)	Sample ID	Sample Analyzed
0		0'-3": Asphalt	AC					
		3"-4.5': Poorly-graded SAND (95% sand, 5% silt), fine grained sand, brown, moist, slight odor, no sheen.	SP	100	N/A	121	B25-073009-2	X
5		4.5'-5.5': Silty SAND (65% sand, 35% silt), fine grained sand, brown, moist, no odor, no sheen.	SM	100	N/A	0.0	B25-073009-5	X
		5.5'-7.0': Poorly-graded SAND (95% sand, 5% silt), fine grained sand, black, moist, no odor, no sheen.	SP					
		7.0'-10.0': Silty SAND (70% sand, 30% silt), fine grained sand, brown, moist to wet, no odor, no sheen.	SM	80	N/A	0.0	B25-073009-7	X
10				80	N/A	0.0	B25-073009-9	

Boring/Well Construction Details: Asphalt cap; Bentonite; Initial water level

Well Construction Information

Monument Type:	NA	**Filter Pack:**	NA	**Ground Surface Elevation (ft):**	NA
Casing Diameter (inches):	NA	**Surface Seal:**	NA	**Top of Casing Elevation (ft):**	NA
Screen Slot Size (inches):	NA	**Annular Seal:**	NA	**Boring Abandonment:**	Bentonite
Screened Interval (ft bgs):	NA			**Surveyed Location:** X: NA	Y: NA

FARALLON consulting
975 5th Avenue Northwest
Issaquah, Washington 98027

Log of Boring: B26

Client: Capital Industries Inc.
Project: Capital Industries Inc.
Location: Seattle, WA

Farallon PN: 457-004

Logged By: Ken Scott

Date/Time Started:	7/30/09 0935	**Sampler Type:**	Macrocore 60-inch
Date/Time Completed:	7/30/09 1030	**Drive Hammer (lbs.):**	NA
Equipment:	Geoprobe 6600	**Depth of Water ATD (ft bgs):**	NE
Drilling Company:	Cascade Drilling	**Total Boring Depth (ft bgs):**	10' bgs
Drilling Foreman:	Kasey Goble	**Total Well Depth (ft bgs):**	NA
Drilling Method:	Direct-push		

Depth (feet bgs.)	Sample Interval	Lithologic Description	USCS	USGS Graphic	% Recovery	Blow Counts 8/8/8	PID (ppm*)	Sample ID	Sample Analyzed	Boring/Well Construction Details
0		0'-3": Organic-rich soil, brown, moist, no odor, no sheen.	OL							
		2"-3.5': SILT with Sand (70% silt, 30% sand), fine grained sand, light-brown, moist, no odor, no sheen.	ML		100	N/A	0.0	B26-073009-2	X	
		3.5'-7.0': Silty SAND (65% sand, 35% silt), fine grained sand, brown, moist, no odor, no sheen.	SM		100	N/A	0.0	B26-073009-5	X	Bentonite
5		7.0'-8.5': Poorly-graded SAND (95% sand, 5% silt), fine grained sand, black, moist, no odor, no sheen.	SP		80	N/A	0.0	B26-073009-7	X	
		8.5'-10.0': Silty SAND (70% sand, 30% silt), fine grained sand, brown, moist, no odor, no sheen.	SM		80	N/A	0.0	B26-073009-9		
10										

Well Construction Information

Monument Type: NA
Casing Diameter (inches): NA
Screen Slot Size (inches): NA
Screened Interval (ft bgs): NA

Filter Pack: NA
Surface Seal: NA
Annular Seal: NA

Ground Surface Elevation (ft): NA
Top of Casing Elevation (ft): NA
Boring Abandonment: Bentonite
Surveyed Location: X: NA Y: NA

PARALLON CONSULTING
320 3rd Avenue NE
Issaquah, WA 98027

Log of Boring: MW-1

ient: Capital Industries
oject: Capital Industries
cation: Seattle, Washington
rallon PN: 457-001
gged By: T. Mulhern

Date/Time Started:	2/7/06 1100	**Sampler Type:**	Dames & Moore
Date/Time Completed:	2/7/06 1230	**Drive Hammer (lbs.):**	140
Equipment:	Limited Access Rig	**Depth of Water ATD (ft bgs):**	8
Drilling Company:	Cascade Drilling	**Total Boring Depth (ft bgs):**	18
Drilling Foreman:	Dave	**Total Well Depth (ft bgs):**	17
Drilling Method:	HSA		

Sample Interval	Lithologic Description	USCS	USGS Graphic	% Recovery	Blow Counts 8/8/8	PID (ppm)	Sample ID	Sample Analyzed	Well Construction Details
	ASPHALT.	AC							Concrete
	Clear for utilities using vac-truck to 5 feet.								Bentonite
	SILT, minor fine sand, medium brown motled with rust orange, wet, soft, no odor.	ML		80	2/11/12	0.4	MW1-5-6.5	X	#2/12 Monterey Sand
	Same as above, very stiff, no odor.	ML							
	SAND, trace silt, fine grained, dark gray, saturated, dense, no odor.	SP		80	13/50/6	0.6	MW1-8-9		Screen
	Same as above, no odor.	SP		100	10/50/6	0.8	MW1-10-11.5		
	Same as above, loose, no odor.	SP		100	10/17/23	0.8	MW1-15-16.5	X	

Well Construction Information

nent Type:	Flush Mount	**Filter Pack:**	#2/12 Monterey Sand
Diameter (inches):	2"	**Surface Seal:**	Cement
Slot Size (inches):	0.010	**Annular Seal:**	Bentonite
ed Interval (ft bgs):	7-17		

Ground Surface Elevation (ft):	16.73
Top of Casing Elevation (ft):	16.34
Boring Abandonment:	N/A
Surveyed Location: X: N/A	Y: N/A


PARALLON CONSULTING
320 3rd Avenue NE
Issaquah, WA 98027

Log of Boring: MW-2

ient: Capital Industries
oject: Capital Industries
cation: Seattle, Washington
rallon PN: 457-001
gged By: T. Mulhern

Date/Time Started:	2/7/06 1500	**Sampler Type:**	Dames & Moore
Date/Time Completed:	2/7/06 1600	**Drive Hammer (lbs.):**	140
Equipment:	Limited Access Rig	**Depth of Water ATD (ft bgs):**	8
Drilling Company:	Cascade Drilling	**Total Boring Depth (ft bgs):**	20
Drilling Foreman:	Dave	**Total Well Depth (ft bgs):**	19.5
Drilling Method:	HSA		

Sample Interval	Lithologic Description	USCS	% Recovery	Blow Counts 8/8/8	PID (ppm)	Sample ID	Sample Analyzed
	CONCRETE.	CO					
	SAND, minor silt, yellow-brown, moist, dense, no odor.	SP	50	16/80/6	6.1	MW2-3.5-4	X
	Sandy SILT, with organics, fine grained, dark brown, moist, very stiff, no odor.	SM-ML					
	SILT, trace fine sand, medium gray, moist, stiff, no odor.	ML	70	7/14/14	1.5	MW2-6-6.5	X
	Same as above, medium stiff, no odor.	ML	90	6/8/9	2.0	MW2-8.5-9	X
	Becomes sandy SILT, wet to saturated, no odor.	SM-ML					
	Same as above.	SM-ML	50	6/9/10	1.6	MW2-11-11.5	X
	SAND, minor silt, fine grained, dark gray, saturated, very loose, no odor.	SP					
	Same as above, dense, no odor.	SP	90	17/50/6	1.2	MW2-15-16.5	

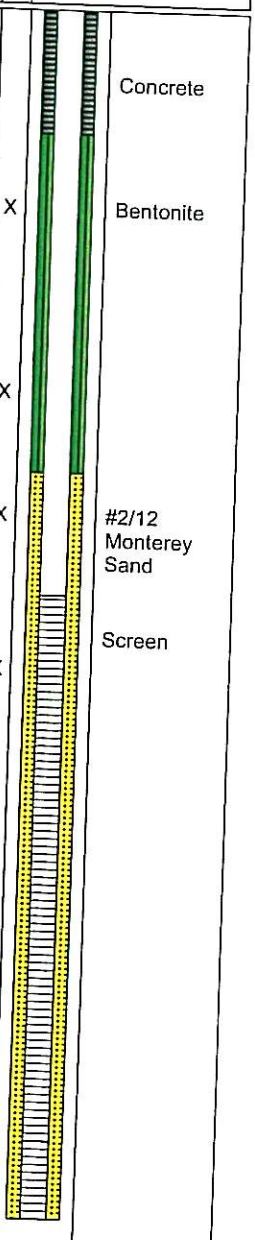

Well Construction Details

Well Construction Information

ment Type:	Flush Mount	**Filter Pack:**	#2/12 Monterey Sand	**Ground Surface Elevation (ft):**	16.91
g Diameter (inches):	4"	**Surface Seal:**	Cement	**Top of Casing Elevation (ft):**	16.48
n Slot Size (inches):	0.010	**Annular Seal:**	Bentonite	**Boring Abandonment:**	N/A
ed Interval (ft bgs):	9.5-19.5			**Surveyed Location:** X: N/A	Y: N/A

PARALLON CONSULTING
320 3rd Avenue NE
Issaquah, WA 98027

Log of Boring: MW-3

ient: Capital Industries
oject: Capital Industries
ocation: Seattle, Washington
rallon PN: 457-001
ogged By: T. Mulhern

Date/Time Started:	2/6/06 0845	**Sampler Type:**	Dames & Moore
Date/Time Completed:	2/6/06 1000	**Drive Hammer (lbs.):**	300
Equipment:	CME	**Depth of Water ATD (ft bgs):**	7
Drilling Company:	Cascade Drilling	**Total Boring Depth (ft bgs):**	20
Drilling Foreman:	Andy	**Total Well Depth (ft bgs):**	17
Drilling Method:	HSA		

Sample Interval	Lithologic Description	USCS	USGS Graphic	% Recovery	Blow Counts 8/8/8	PID (ppm)	Sample ID	Sample Analyzed	Well Construction Details
	ASPHALT.	AC							Concrete
	SILT, trace fine sand, medium brown, moist, soft, no odor.	ML		100	4/6/6	0.3	MW3-2.5-4		Bentonite
	Becomes with rust mottling, moist to wet, very soft, no odor.			100	2/2/3	0.1	MW3-4-5.5	X	
				100		0.0	MW3-5.5-7		#2/12 Monterey Sand
	SAND, trace silt, fine grained, dark gray with rust mottling, saturated, no odor.	SP		100		0.0	MW3-7-8.5		▽
	Same as above, no odor.	SP		100		0.3	MW3-10-11.5		Screen
	Same as above, no mottling, no odor.	SP		100		0.1	MW3-15-16.5	X	
	Same as above, no odor.	SP		100		0.2			

nent Type: Flush Mount
g Diameter (inches): 2"
n Slot Size (inches): 0.010
ed Interval (ft bgs): 7-17

Well Construction Information

Filter Pack: #2/12 Monterey Sand
Surface Seal: Cement
Annular Seal: Bentonite

Ground Surface Elevation (ft): 16.13
Top of Casing Elevation (ft): 15.74
Boring Abandonment: N/A
Surveyed Location: X: N/A Y: N/A

PARALLON CONSULTING
320 3rd Avenue NE
Issaquah, WA 98027

Log of Boring: MW-4

ient: Capital Industries
oject: Capital Industries
cation: Seattle, Washington
rallon PN: 457-001
gged By: T. Mulhern

Date/Time Started:	2/6/06 1015	**Sampler Type:**	Dames & Moore
Date/Time Completed:	2/6/06 1130	**Drive Hammer (lbs.):**	300
Equipment:	CME	**Depth of Water ATD (ft bgs):**	7
Drilling Company:	Cascade Drilling	**Total Boring Depth (ft bgs):**	18.5
Drilling Foreman:	Andy	**Total Well Depth (ft bgs):**	17
Drilling Method:	HSA		

Sample Interval	Lithologic Description	USCS	USGS Graphic	% Recovery	Blow Counts 8/8/8	PID (ppm)	Sample ID	Sample Analyzed	Well Construction Details
	ASPHALT.	AC							Concrete
	Clear for utilities using vac-truck to 5'.								Bentonite
	Sandy SILT, fine grained, medium gray with rust mottling, wet, soft, no odor.	ML		100	2/4/4	0.1	MW4-5-6.5	X	#2/12 Monterey Sand
	SAND, minor silt, medium gray, saturated, no odor.	SP		100	—	0.9	MW4-6.5-8		▽
									Screen
	SAND, trace silt, fine grained dark gray, saturated, loose, no odor.	SP		100	5/9/17	1.0	MW4-10-11.5		
	Same as above, loose, no odor.	SP		100	8/10/12	1.2	MW4-14-15.5		
	Same as above, loose, no odor.	SP		100	12/7/7	1.3	MW4-17-18.5	X	

Well Construction Information

nent Type:	Flush Mount	**Filter Pack:**	#2/12 Monterey Sand
g Diameter (inches):	2"	**Surface Seal:**	Cement
n Slot Size (inches):	0.010	**Annular Seal:**	Bentonite
ed Interval (ft bgs):	7-17		

Ground Surface Elevation (ft):	16.04
Top of Casing Elevation (ft):	15.62
Boring Abandonment:	N/A
Surveyed Location: X: N/A	Y: N/A

FARALLON CONSULTING
320 3rd Avenue NE
Issaquah, WA 98027

Log of Boring: MW-5

ient: Capital Industries
oject: Capital Industries
cation: Seattle, Washington
rallon PN: 457-001
gged By: T. Mulhern

Date/Time Started:	2/7/06 0915	**Sampler Type:**	Dames & Moore
Date/Time Completed:	2/7/06 1045	**Drive Hammer (lbs.):**	140
Equipment:	Limited Access Rig	**Depth of Water ATD (ft bgs):**	10-11
Drilling Company:	Cascade Drilling	**Total Boring Depth (ft bgs):**	20
Drilling Foreman:	Dave	**Total Well Depth (ft bgs):**	19
Drilling Method:	HSA		

Sample Interval	Lithologic Description	USCS	USGS Graphic	% Recovery	Blow Counts 8/8/8	PID (ppm)	Sample ID	Sample Analyzed	Well Construction Details
	ASPHALT.	AC							Concrete
	Clear for utilities using vac-truck to 5'.								Bentonite
	SAND, with silt, fine grained, medium brown, moist, very loose, no odor.	SP							
	SILT, trace fine sand, medium gray, wet, soft, no odor.	ML		90	3/9/8	0.4	MW5-5-6.5	X	
	Same as above, no odor. Becomes minor sand at 8'.	ML		100	--	0.4	MW5-6-7.5		#2/12 Monterey Sand
	Same as above, becomes with sand.	ML							Screen
	Silty SAND, fine grained, dark gray, saturated, trace wood, loose, no odor.	SP-SM			14/15/18	0.4	MW5-10-11.5	X	
	SAND, trace silt, fine grained, dark gray, trace wood, saturated, dense, no odor.	SP			50/6	2.0	MW5-12.5-14		

Well Construction Information

nent Type: Flush Mount
Diameter (inches): 2"
Slot Size (inches): 0.010
ed Interval (ft bgs): 9-19

Filter Pack: #2/12 Monterey Sand
Surface Seal: Cement
Annular Seal: Bentonite

Ground Surface Elevation (ft): 16.30
Top of Casing Elevation (ft): 15.90
Boring Abandonment: N/A
Surveyed Location: X: N/A Y: N/A

PARALLON CONSULTING
320 3rd Avenue NE
Issaquah, WA 98027

Log of Boring: MW-6

ient: Capital Industries
oject: Capital Industries
cation: Seattle, Washington
rallon PN: 457-001
gged By: T. Mulhern

Date/Time Started:	2/7/06 1245	**Sampler Type:**	Dames & Moore
Date/Time Completed:	2/7/06 1445	**Drive Hammer (lbs.):**	140
Equipment:	Limited Access Rig	**Depth of Water ATD (ft bgs):**	8.5
Drilling Company:	Cascade Drilling	**Total Boring Depth (ft bgs):**	18
Drilling Foreman:	Dave	**Total Well Depth (ft bgs):**	18
Drilling Method:	HSA		

Sample Interval	Lithologic Description	USCS	USGS Graphic	% Recovery	Blow Counts 8/8/8	PID (ppm)	Sample ID	Sample Analyzed	Well Construction Details
	CONCRETE.	CO							Concrete
	SAND, minor silt, fine grained, yellow-brown, moist, soft, no odor.	SP							
	SILT, trace fine sand, medium brown with orange mottling, moist, soft, no odor.	ML		75	9/13/13	1.9	MW6-2.5-3	X	Bentonite
	Same as above, moist to wet, loose, no odor.	ML		60	7/8/12	10.3	MW6-5-6.5	X	
	Same as above, no odor.	SP							#2/12 Monterey Sand
	SAND, trace silt, fine grained, dark gray, saturated, no odor.	SP		80	—	4.6	MW6-7.5-8.5	X	▽
	Same as above, loose, no odor.	SP		75	12/13/11	2.3	MW6-10-11.5		Screen
	NO RECOVERY.								

Well Construction Information

ment Type:	Flush Mount	**Filter Pack:**	#2/12 Monterey Sand	**Ground Surface Elevation (ft):**	17.79
g Diameter (inches):	4"	**Surface Seal:**	Cement	**Top of Casing Elevation (ft):**	17.43
n Slot Size (inches):	0.010	**Annular Seal:**	Bentonite	**Boring Abandonment:**	N/A
ed Interval (ft bgs):	18			**Surveyed Location:** X: N/A	Y: N/A

PARALLON CONSULTING
320 3rd Avenue NE
Issaquah, WA 98027

Log of Boring: MW-7

ient: Capital Industries
oject: Capital Industries
cation: Seattle, Washington
rallon PN: 457-001
gged By: T. Mulhern

Date/Time Started:	2/6/06 1215	**Sampler Type:**	Dames & Moore
Date/Time Completed:	2/6/06 1345	**Drive Hammer (lbs.):**	300
Equipment:	CME	**Depth of Water ATD (ft bgs):**	8.5
Drilling Company:	Cascade Drilling	**Total Boring Depth (ft bgs):**	16.5
Drilling Foreman:	Andy	**Total Well Depth (ft bgs):**	17
Drilling Method:	HSA		

Sample Interval	Lithologic Description	USCS	USGS Graphic	% Recovery	Blow Counts 8/8/8	PID (ppm)	Sample ID	Sample Analyzed	Well Construction Details
	ASPHALT.	AC							Concrete
	Clear for utilities using vac-truck to 5'.								Bentonite
	SILT, minor sand, fine grained, medium gray with rust brown mottling, moist, very soft, no odor.	ML		100	1/2/4	0.1	MW7-5-6.5	X	#2/12 Monterey Sand
	SAND, trace silt, fine grained, dark gray, saturated, loose, no odor.	SP		80	6/7/8	0.2	MW7-6.5-8		Screen
	Same as above, loose.	SP		100	5/8/11	0.2	MW7-10-11.5	X	
	Same as above.	SP		100	--	0.0	MW7-15-16.5		

nent Type: Flush Mount
l Diameter (inches): 2"
l Slot Size (inches): 0.010
ed Interval (ft bgs): 7-17

Well Construction Information

Filter Pack: #2/12 Monterey Sand
Surface Seal: Cement
Annular Seal: Bentonite

Ground Surface Elevation (ft): 17.30
Top of Casing Elevation (ft): 16.93
Boring Abandonment: N/A
Surveyed Location: X: N/A Y: N/A

FARALLON CONSULTING
320 3rd Avenue NE
Issaquah, WA 98027

Log of Boring: MW-8

ient: Capital Industries
oject: Capital Industries
cation: Seattle, Washington
rallon PN: 457-001
gged By: T. Mulhern

Date/Time Started:	2/6/06 1400	**Sampler Type:**	Dames & Moore
Date/Time Completed:	2/6/06 1530	**Drive Hammer (lbs.):**	300
Equipment:	CME	**Depth of Water ATD (ft bgs):**	8
Drilling Company:	Cascade Drilling	**Total Boring Depth (ft bgs):**	18
Drilling Foreman:	Andy	**Total Well Depth (ft bgs):**	18
Drilling Method:	HSA		

Sample Interval	Lithologic Description	USCS	USGS Graphic	% Recovery	Blow Counts 8/8/8	PID (ppm)	Sample ID	Sample Analyzed	Well Construction Details
	GRAVEL fill.	GP							Concrete
	Clear for utilities using vac-truck to 5'.								Bentonite
	SILT, with fine sand, medium gray-brown with rust mottling, moist, soft, no odor.	ML		100	4/3/4	0.0	MW8-5-6.5	X	#2/12 Monterey Sand
	Same as above, wet, very soft. At 8'Becomes SAND, trace silt, fine grained, dark gray, saturated, very loose, no odor.	ML		100	2/2/2	0.0	MW8-6.5-8		Screen
	Same as above, loose, no odor.	SP		100	7/7/5	0.0	MW8-10-11.5		
	Same as above, loose to medium dense, no odor.	SP		100	9/5/17	0.0	MW8-16.5-18	X	

Well Construction Information

nent Type:	Flush Mount	**Filter Pack:**	#2/12 Monterey Sand
Diameter (inches):	2"	**Surface Seal:**	Cement
Slot Size (inches):	0.010	**Annular Seal:**	Bentonite
ed Interval (ft bgs):	8-18		

Ground Surface Elevation (ft):	17.02
Top of Casing Elevation (ft):	16.68
Boring Abandonment:	N/A
Surveyed Location: X: N/A	Y: N/A

FARALLON consulting
975 5th Avenue Northwest
Issaquah, Washington 98027

Log of Boring: CI-7-40


Client: Capital Industries
Project: Capital Industries
Location: Seattle, WA

Farallon PN: 457-004

Logged By: J. Ruark

Date/Time Started:	2/8/2010	**Sampler Type:**	NA
Date/Time Completed:	2/8/2010	**Drive Hammer (lbs.):**	NA
Equipment:	CME 75	**Depth of Water ATD (ft bgs):**	NA
Drilling Company:	Cascade Drilling	**Total Boring Depth (ft bgs):**	40
Drilling Foreman:	Andy	**Total Well Depth (ft bgs):**	40
Drilling Method:	Hollow Stem Auger		

Depth (feet bgs.)	Sample Interval	Lithologic Description	USCS	USGS Graphic	% Recovery	Blow Counts 8/8/8	PID (ppm)	Sample ID	Sample Analyzed	Boring/Well Construction Details
0		Lithology data not collected due to heaving sands.								Monument
5										
10										Bentonite Seal
15										
20										Casing
25										
30										2/12 Sand Pack
35										0.01 Slot PVC Well Screen
40										



Well Construction Information

Monument Type: Flush Mount
Casing Diameter (inches): 2.0
Screen Slot Size (inches): 0.01
Screened Interval (ft bgs): 30-40

Filter Pack: 2/12 Sand
Surface Seal: Grout
Annular Seal: Bentonite

Ground Surface Elevation (ft): NA
Top of Casing Elevation (ft): NA
Boring Abandonment: NA
Surveyed Location: **X:** NA **Y:** NA

FARALLON consulting
975 5th Avenue Northwest
Issaquah, Washington 98027

Log of Boring: CI-7-60

Client: Capital Industries
Project: Capital Industries
Location: Seattle, WA

Farallon PN: 457-004

Logged By: D. Clement

Date/Time Started:	2/9/2010	**Sampler Type:**	NA
Date/Time Completed:	2/9/2010	**Drive Hammer (lbs.):**	NA
Equipment:	CME 75	**Depth of Water ATD (ft bgs):**	NA
Drilling Company:	Cascade Drilling	**Total Boring Depth (ft bgs):**	60
Drilling Foreman:	Andy	**Total Well Depth (ft bgs):**	60
Drilling Method:	Hollow Stem Auger		

Depth (feet bgs.)	Sample Interval	Lithologic Description	USCS	USGS Graphic	% Recovery	Blow Counts 8/8/8	PID (ppm)	Sample ID	Sample Analyzed	Boring/Well Construction Details
0–60		Lithology data not collected due to heaving sands.								Monument; Bentonite Seal; Casing; 2/12 Sand Pack; 0.01 Slot PVC Well Screen



Well Construction Information

Monument Type: Flush Mount
Casing Diameter (inches): 2.0
Screen Slot Size (inches): 0.01
Screened Interval (ft bgs): 50-60

Filter Pack: 2/12 Sand
Surface Seal: Grout
Annular Seal: Bentonite

Ground Surface Elevation (ft): NA
Top of Casing Elevation (ft): NA
Boring Abandonment: NA
Surveyed Location: **X:** NA **Y:** NA

FARALLON consulting
975 5th Avenue Northwest
Issaquah, Washington 98027

Log of Boring: CI-8-40


Client: Capital Industries
Project: Capital Industries
Location: Seattle, WA

Farallon PN: 457-004

Logged By: J. Ruark

Date/Time Started:	2/8/2010	**Sampler Type:**	NA
Date/Time Completed:	2/8/2010	**Drive Hammer (lbs.):**	NA
Equipment:	CME 75	**Depth of Water ATD (ft bgs):**	NA
Drilling Company:	Cascade Drilling	**Total Boring Depth (ft bgs):**	40
Drilling Foreman:	Andy	**Total Well Depth (ft bgs):**	40
Drilling Method:	Hollow Stem Auger		

Depth (feet bgs.)	Sample Interval	Lithologic Description	USCS	USGS Graphic	% Recovery	Blow Counts 8/8/8	PID (ppm)	Sample ID	Sample Analyzed	Boring/Well Construction Details
0		Lithology data not collected due to heaving sands.								Monument
5										
10										Bentonite Seal
15										
20										Casing
25										
30										2/12 Sand Pack
35										0.01 Slot PVC Well Screen
40										



Well Construction Information

Monument Type: Flush Mount
Casing Diameter (inches): 2.0
Screen Slot Size (inches): 0.01
Screened Interval (ft bgs): 30-40

Filter Pack: 2/12 Sand
Surface Seal: Grout
Annular Seal: Bentonite

Ground Surface Elevation (ft): NA
Top of Casing Elevation (ft): NA
Boring Abandonment: NA
Surveyed Location: **X:** NA **Y:** NA

FARALLON consulting
975 5th Avenue Northwest
Issaquah, Washington 98027

Log of Boring: CI-8-60

Client: Capital Industries
Project: Capital Industries
Location: Seattle, WA

Farallon PN: 457-004

Logged By: J. Ruark

Date/Time Started:	2/8/2010	**Sampler Type:**	NA
Date/Time Completed:	2/8/2010	**Drive Hammer (lbs.):**	NA
Equipment:	CME 75	**Depth of Water ATD (ft bgs):**	NA
Drilling Company:	Cascade Drilling	**Total Boring Depth (ft bgs):**	60
Drilling Foreman:	Andy	**Total Well Depth (ft bgs):**	60
Drilling Method:	Hollow Stem Auger		

Depth (feet bgs.)	Sample Interval	Lithologic Description	USCS	USGS Graphic	% Recovery	Blow Counts 8/8/8	PID (ppm)	Sample ID	Sample Analyzed	Boring/Well Construction Details
0–60		Lithology data not collected due to heaving sands.								Monument; Bentonite Seal; Casing; 2/12 Sand Pack; 0.01 Slot PVC Well Screen



Well Construction Information

Monument Type: Flush Mount
Casing Diameter (inches): 2.0
Screen Slot Size (inches): 0.01
Screened Interval (ft bgs): 50-60

Filter Pack: 2/12 Sand
Surface Seal: Grout
Annular Seal: Bentonite

Ground Surface Elevation (ft): NA
Top of Casing Elevation (ft): NA
Boring Abandonment: NA
Surveyed Location: **X:** NA **Y:** NA

FARALLON consulting
975 5th Avenue Northwest
Issaquah, Washington 98027

Log of Boring: CI-9-40

Client: Capital Industries
Project: Capital Industries
Location: Seattle, WA

Farallon PN: 457-004

Logged By: J. Ruark

Date/Time Started:	5/12/10	**Sampler Type:**	NA
Date/Time Completed:	5/12/10	**Drive Hammer (lbs):**	NA
Equipment:	CME 75	**Depth of Water (ft bgs):**	NA
Drilling Company:	Cascade Drilling	**Total Boring Depth (ft bgs):**	40
Drilling Foreman:	Scott Curtis	**Total Well Depth (ft bgs):**	40
Drilling Method:	Hollow Stem Auger		

Depth (feet bgs)	Sample Interval	Lithologic Description	USCS	USGS Graphic	% Recovery	Blow Counts	PID (ppmv)	Sample ID	Sample Analyzed	Boring/Well Construction Details
0–40		For lithologic description refer to log of boring CI-9-70								Monument; Casing; Bentonite Seal; 2/12 Sand Pack; 0.01 Slot PVC Well Screen

Well Construction Information

Monument Type:	Flush Mount	**Filter Pack:**	2/12 Sand	**Ground Surface Elevation (ft msl):**	NA
Casing Diameter (in):	2.0	**Surface Seal:**	Cement	**Top of Casing Elevation (ft msl):**	NA
Screen Slot Size (in):	0.01	**Annular Seal:**	Bentonite	**Surveyed Location:**	**X:**NA
Screened Interval (ft bgs):	30-40	**Boring Abandonment:**	NA		**Y:**NA

FARALLON consulting
975 5th Avenue Northwest
Issaquah, Washington 98027

Log of Boring: CI-9-70


Client: Capital Industries
Project: Capital Industries
Location: Seattle, WA

Farallon PN: 457-004

Logged By: J. Ruark

Date/Time Started:	5/25/2010 0910	**Sampler Type:**	D and M Split Spoon 18"x2"
Date/Time Completed:	5/25/2010 1215	**Drive Hammer (lbs):**	300
Equipment:	CME 75	**Depth of Water (ft bgs):**	7.0
Drilling Company:	Cascade Drilling	**Total Boring Depth (ft bgs):**	70.0
Drilling Foreman:	Scott	**Total Well Depth (ft bgs):**	70.0
Drilling Method:	Hollow Stem Auger		

Depth (feet bgs)	Sample Interval	Lithologic Description	USCS	USGS Graphic	% Recovery	Blow Counts	PID (ppmv)	Sample ID	Sample Analyzed	Boring/Well Construction Details
10		10.0-11.3' Poorly graded SAND (95% sand, 5% silt), fine to medium sand, black to grey, dense, wet, no odor.	SP		85	9/14/15	1.5	CI-9-70-11 @ 0915		

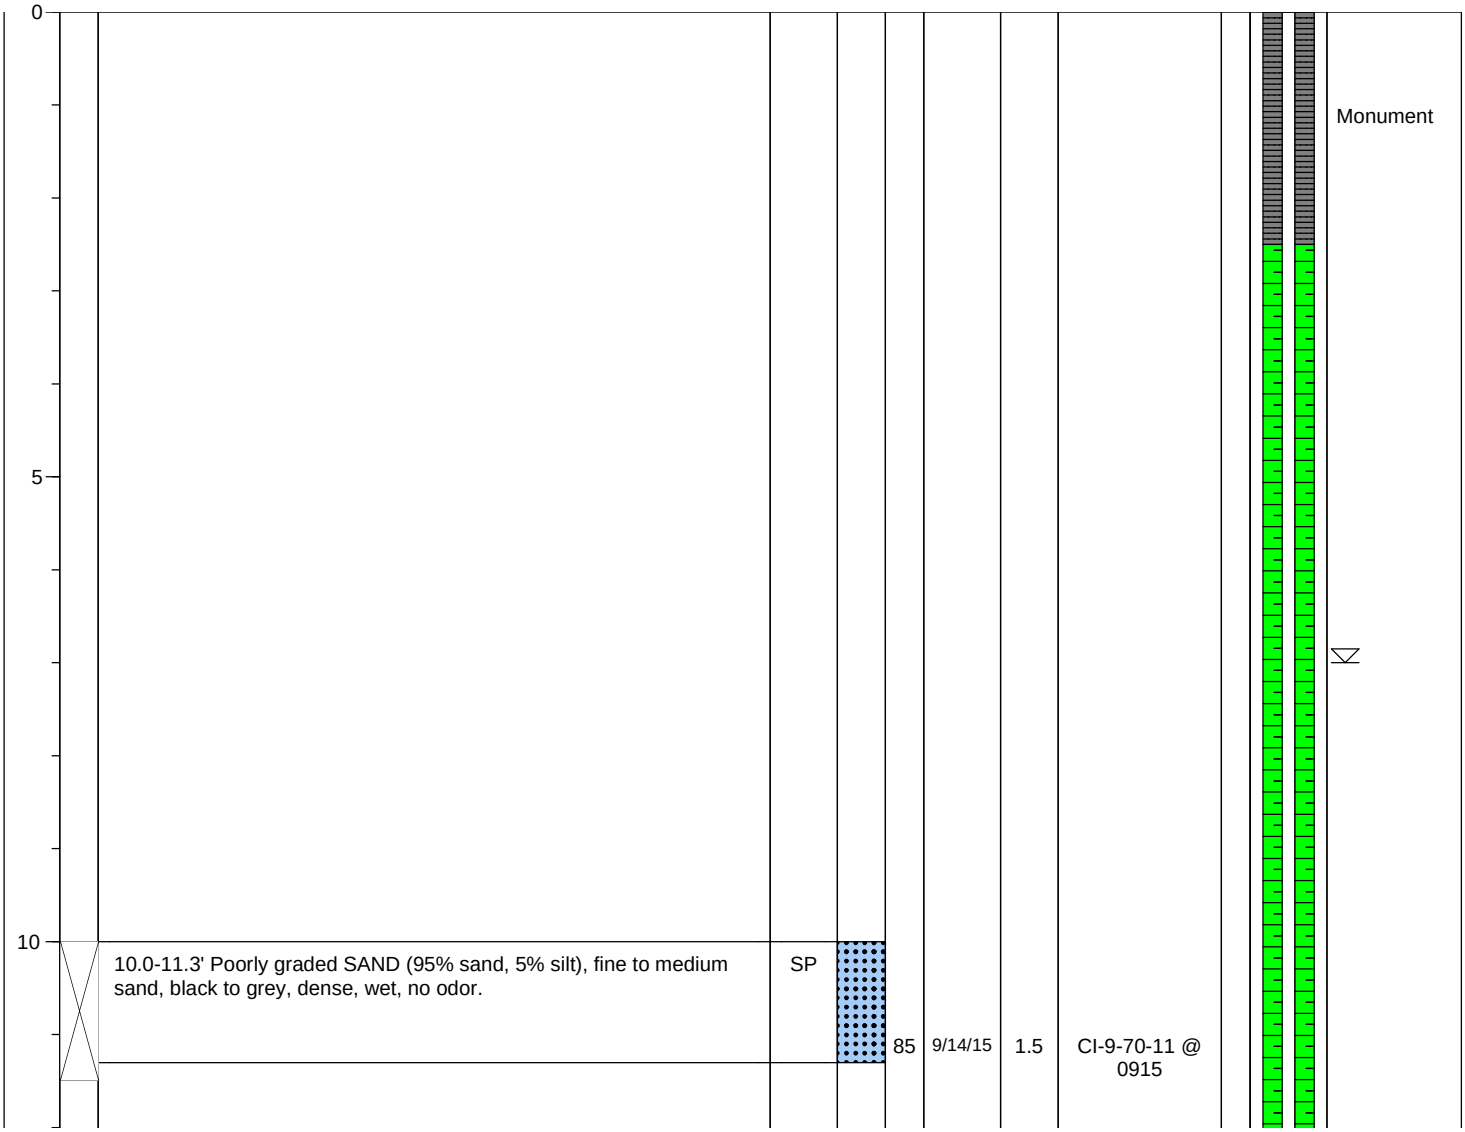


Well Construction Information

Monument Type:	Flush Mount	**Filter Pack:**	2/12 Sand	**Ground Surface Elevation (ft msl):**	NA
Casing Diameter (in):	2.0	**Surface Seal:**	Grout	**Top of Casing Elevation (ft msl):**	NA
Screen Slot Size (in):	0.01	**Annular Seal:**	Bentonite	**Surveyed Location:**	**X:**NA
Screened Interval (ft bgs):	60.0-70.0	**Boring Abandonment:**	NA		**Y:**NA

FARALLON consulting
975 5th Avenue Northwest
Issaquah, Washington 98027

Log of Boring: CI-9-70

Depth (feet bgs)	Sample Interval	Lithologic Description	USCS	USGS Graphic	% Recovery	Blow Counts	PID (ppmv)	Sample ID	Sample Analyzed	Well Construction Details
15										
20		20.0-21.5' Poorly graded SAND (95% sand, 5% silt), fine to medium sand, black to grey, very dense, wet, no odor.	SP		100	15/18/20	1.7	CI-9-70-20 @ 0923		Bentonite Seal
25										




Well Construction Information

Monument Type:	Flush Mount	**Filter Pack:**	2/12 Sand	**Ground Surface Elevation (ft msl):**	NA
Casing Diameter (in):	2.0	**Surface Seal:**	Grout	**Top of Casing Elevation (ft msl):**	NA
Screen Slot Size (in):	0.01	**Annular Seal:**	Bentonite	**Surveyed Location:**	**X:**NA
Screened Interval (ft bgs):	60.0-70.0	**Boring Abandonment:**	NA		**Y:**NA

FARALLON consulting
975 5th Avenue Northwest
Issaquah, Washington 98027

Log of Boring: CI-9-70

Depth (feet bgs)	Sample Interval	Lithologic Description	USCS	USGS Graphic	% Recovery	Blow Counts	PID (ppmv)	Sample ID	Sample Analyzed	Well Construction Details
30		30.0-31.5' Poorly graded SAND (95% sand, 5% silt), fine to medium sand, black to grey, dense, wet, no odor.	SP		100	18/20/27	2.3	CI-9-70-30 @ 0930		
35										
40		40.0-41.1' Poorly graded SAND (95% sand, 5% silt), fine to medium sand, black to grey, dense, wet, no odor.	SP		75	18/23/28	1.7	CI-9-70-40 @ 0941		Casing




Well Construction Information

Monument Type:	Flush Mount	**Filter Pack:**	2/12 Sand	**Ground Surface Elevation (ft msl):**	NA
Casing Diameter (in):	2.0	**Surface Seal:**	Grout	**Top of Casing Elevation (ft msl):**	NA
Screen Slot Size (in):	0.01	**Annular Seal:**	Bentonite	**Surveyed Location:**	**X:**NA
Screened Interval (ft bgs):	60.0-70.0	**Boring Abandonment:**	NA		**Y:**NA

FARALLON consulting
975 5th Avenue Northwest
Issaquah, Washington 98027

Log of Boring: CI-9-70

Depth (feet bgs)	Sample Interval	Lithologic Description	USCS	USGS Graphic	% Recovery	Blow Counts	PID (ppmv)	Sample ID	Sample Analyzed	Well Construction Details
45										
50		50.0-50.2' Poorly graded SAND (95% sand, 5% silt), fine sand, black to grey, dense, wet, no odor. 50.2-51.5' Poorly graded SAND (95% sand, 5% silt), fine to medium sand, black to grey, dense, wet, no odor.	SP		100	21/30/33	2.3	CI-9-70-50 @ 0949		
55										




Well Construction Information

Monument Type:	Flush Mount	**Filter Pack:**	2/12 Sand	**Ground Surface Elevation (ft msl):**	NA
Casing Diameter (in):	2.0	**Surface Seal:**	Grout	**Top of Casing Elevation (ft msl):**	NA
Screen Slot Size (in):	0.01	**Annular Seal:**	Bentonite	**Surveyed Location:**	**X:**NA
Screened Interval (ft bgs):	60.0-70.0	**Boring Abandonment:**	NA		**Y:**NA

FARALLON consulting
975 5th Avenue Northwest
Issaquah, Washington 98027

Log of Boring: CI-9-70

Depth (feet bgs)	Sample Interval	Lithologic Description	USCS	USGS Graphic	% Recovery	Blow Counts	PID (ppmv)	Sample ID	Sample Analyzed	Well Construction Details
60		60.0-61.5' Poorly graded SAND (95% sand, 5% silt), fine to medium sand, black to grey, dense, wet, no odor, wood debris, 0.2' silt lense at 60.3'.	SP		100	26/30/35	1.6	CI-9-70-60 @ 0959		2/12 Sand Pack
65										0.01 Slot PVC Well Screen
70		70.0-71.5' Poorly graded SANd (95% sand, 5% silt), fine to medium sand, black to grey, very dense, wet, no odor.	SP		100	20/26/31	2.6	CI-9-70-70 @ 1005		




Well Construction Information

Monument Type:	Flush Mount	**Filter Pack:**	2/12 Sand	**Ground Surface Elevation (ft msl):**	NA
Casing Diameter (in):	2.0	**Surface Seal:**	Grout	**Top of Casing Elevation (ft msl):**	NA
Screen Slot Size (in):	0.01	**Annular Seal:**	Bentonite	**Surveyed Location:**	**X:**NA
Screened Interval (ft bgs):	60.0-70.0	**Boring Abandonment:**	NA		**Y:**NA

FARALLON consulting
975 5th Avenue Northwest
Issaquah, Washington 98027

Log of Boring: CI-9-70

Depth (feet bgs)	Sample Interval	Lithologic Description	USCS	USGS Graphic	% Recovery	Blow Counts	PID (ppmv)	Sample ID	Sample Analyzed	Well Construction Details

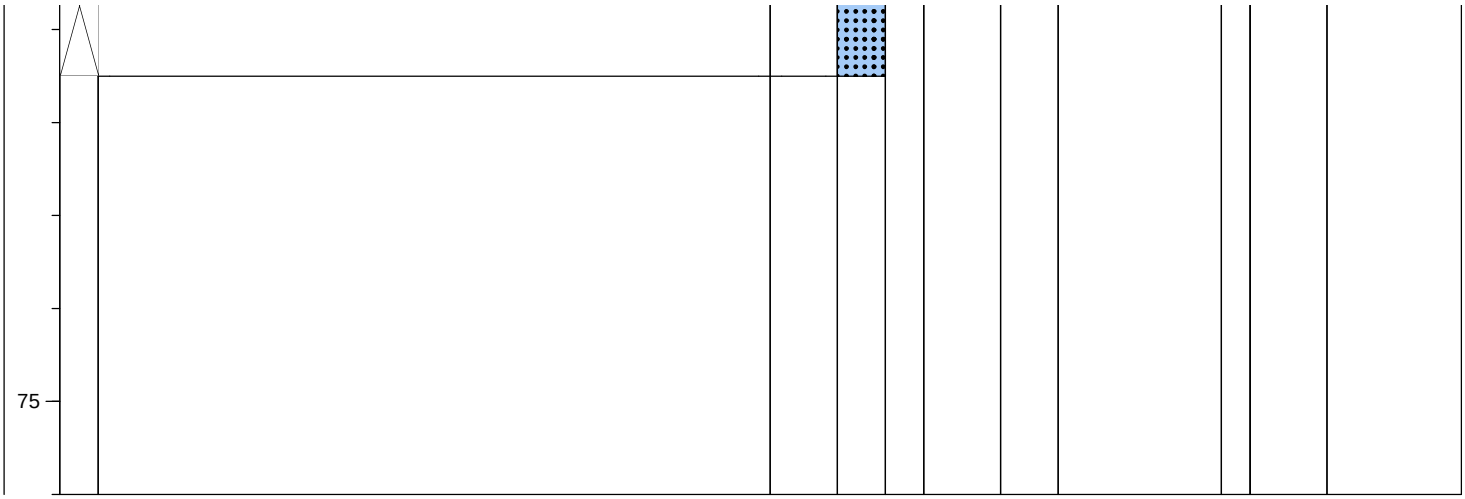

Well Construction Information

Monument Type:	Flush Mount	**Filter Pack:**	2/12 Sand	**Ground Surface Elevation (ft msl):**	NA
Casing Diameter (in):	2.0	**Surface Seal:**	Grout	**Top of Casing Elevation (ft msl):**	NA
Screen Slot Size (in):	0.01	**Annular Seal:**	Bentonite	**Surveyed Location:**	**X:**NA
Screened Interval (ft bgs):	60.0-70.0	**Boring Abandonment:**	NA		**Y:**NA

FARALLON consulting
975 5th Avenue Northwest
Issaquah, Washington 98027

Log of Boring: CI-9-WT

Client: Capital Industries
Project: Capital Industries
Location: Seattle, WA

Farallon PN: 457-004

Logged By: J. Ruark

Date/Time Started:	5/25/10	**Sampler Type:**	NA
Date/Time Completed:	5/25/10	**Drive Hammer (lbs):**	NA
Equipment:	CME 75	**Depth of Water (ft bgs):**	NA
Drilling Company:	Cascade Drilling	**Total Boring Depth (ft bgs):**	20
Drilling Foreman:	Scott Curtis	**Total Well Depth (ft bgs):**	20
Drilling Method:	Hollow Stem Auger		

Depth (feet bgs)	Sample Interval	Lithologic Description	USCS	USGS Graphic	% Recovery	Blow Counts	PID (ppmv)	Sample ID	Sample Analyzed	Boring/Well Construction Details
0		For lithologic description refer to log of boring CI-9-70.								Monument; Bentonite Seal; Casing; 2/12 Sand Pack; 0.01 Slot PVC Well Screen
5										
10										
15										
20										

Well Construction Information

Monument Type:	Flush Mount	**Filter Pack:**	2/12 Sand	**Ground Surface Elevation (ft msl):**	NA
Casing Diameter (in):	2.0	**Surface Seal:**	Cement	**Top of Casing Elevation (ft msl):**	NA
Screen Slot Size (in):	0.01	**Annular Seal:**	Bentonite	**Surveyed Location:**	**X:**NA
Screened Interval (ft bgs):	10-20	**Boring Abandonment:**	NA		**Y:**NA

FARALLON consulting
975 5th Avenue Northwest
Issaquah, Washington 98027

Log of Boring: CI-10-20


Client: Capital Industries
Project: Capital Industries
Location: Seattle, WA

Farallon PN: 457-004

Logged By: J. Ruark

Date/Time Started:	2/11/2010	**Sampler Type:**	NA
Date/Time Completed:	2/11/2010	**Drive Hammer (lbs.):**	NA
Equipment:	CME 75	**Depth of Water ATD (ft bgs):**	NA
Drilling Company:	Cascade Drilling	**Total Boring Depth (ft bgs):**	20
Drilling Foreman:	Andy	**Total Well Depth (ft bgs):**	20
Drilling Method:	Hollow Stem Auger		

Depth (feet bgs.)	Sample Interval	Lithologic Description	USCS	USGS Graphic	% Recovery	Blow Counts 8/8/8	PID (ppm)	Sample ID	Sample Analyzed	Boring/Well Construction Details
0		Lithology data not collected due to heaving sands.								Monument; Bentonite Seal; Casing; 2/12 Sand Pack; 0.01 Slot PVC Well Screen
5										
10										
15										
20										



Well Construction Information

Monument Type: Flush Mount
Casing Diameter (inches): 2.0
Screen Slot Size (inches): 0.01
Screened Interval (ft bgs): 10-20

Filter Pack: 2/12 Sand
Surface Seal: Grout
Annular Seal: Bentonite

Ground Surface Elevation (ft): NA
Top of Casing Elevation (ft): NA
Boring Abandonment: NA
Surveyed Location: **X:** NA **Y:** NA

FARALLON consulting
975 5th Avenue Northwest
Issaquah, Washington 98027

Log of Boring: CI-10-35


Client: Capital Industries
Project: Capital Industries
Location: Seattle, WA

Farallon PN: 457-004

Logged By: J. Ruark

Date/Time Started:	2/11/2010	**Sampler Type:**	NA
Date/Time Completed:	2/11/2010	**Drive Hammer (lbs.):**	NA
Equipment:	CME 75	**Depth of Water ATD (ft bgs):**	NA
Drilling Company:	Cascade Drilling	**Total Boring Depth (ft bgs):**	35
Drilling Foreman:	Andy	**Total Well Depth (ft bgs):**	35
Drilling Method:	Hollow Stem Auger		

Depth (feet bgs.)	Sample Interval	Lithologic Description	USCS	USGS Graphic	% Recovery	Blow Counts 8/8/8	PID (ppm)	Sample ID	Sample Analyzed	Boring/Well Construction Details
0		Lithology data not collected due to heaving sands.								Monument
5										
10										Bentonite Seal
15										Casing
20										
25										2/12 Sand Pack
30										0.01 Slot PVC Well Screen
35										



Well Construction Information

Monument Type: Flush Mount
Casing Diameter (inches): 2.0
Screen Slot Size (inches): 0.01
Screened Interval (ft bgs): 25-35

Filter Pack: 2/12 Sand
Surface Seal: Grout
Annular Seal: Bentonite

Ground Surface Elevation (ft): NA
Top of Casing Elevation (ft): NA
Boring Abandonment: NA
Surveyed Location: **X:** NA **Y:** NA

FARALLON consulting
975 5th Avenue Northwest
Issaquah, Washington 98027

Log of Boring: CI-10-65

Client: Capital Industries
Project: Capital Industries
Location: Seattle, WA

Farallon PN: 457-004

Logged By: J. Ruark

Date/Time Started:	2/11/2010	**Sampler Type:**	NA
Date/Time Completed:	2/11/2010	**Drive Hammer (lbs.):**	NA
Equipment:	CME 75	**Depth of Water ATD (ft bgs):**	NA
Drilling Company:	Cascade Drilling	**Total Boring Depth (ft bgs):**	65
Drilling Foreman:	Andy	**Total Well Depth (ft bgs):**	65
Drilling Method:	Hollow Stem Auger		

Depth (feet bgs.)	Sample Interval	Lithologic Description	USCS	USGS Graphic	% Recovery	Blow Counts 8/8/8	PID (ppm)	Sample ID	Sample Analyzed	Boring/Well Construction Details
0–65		Lithology data not collected due to heaving sands.								Monument; Bentonite Seal; Casing; 2/12 Sand Pack; 0.01 Slot PVC Well Screen

Well Construction Information

Monument Type: Flush Mount
Casing Diameter (inches): 2.0
Screen Slot Size (inches): 0.01
Screened Interval (ft bgs): 50-65

Filter Pack: 2/12 Sand
Surface Seal: Grout
Annular Seal: Bentonite

Ground Surface Elevation (ft): NA
Top of Casing Elevation (ft): NA
Boring Abandonment: NA
Surveyed Location: **X:** NA **Y:** NA

FARALLON consulting
975 5th Avenue Northwest
Issaquah, Washington 98027

Log of Boring: CI-11-30

Client: Capital Industries
Project: Capital Industries
Location: Seattle, WA

Farallon PN: 457-004

Logged By: R. Hibbs

Date/Time Started:	5/27/10	**Sampler Type:**	NA
Date/Time Completed:	5/27/10	**Drive Hammer (lbs):**	NA
Equipment:	CME 75	**Depth of Water (ft bgs):**	NA
Drilling Company:	Cascade Drilling	**Total Boring Depth (ft bgs):**	30
Drilling Foreman:	Scott Curtis	**Total Well Depth (ft bgs):**	30
Drilling Method:	Hollow Stem Auger		

Depth (feet bgs)	Sample Interval	Lithologic Description	USCS	USGS Graphic	% Recovery	Blow Counts	PID (ppmv)	Sample ID	Sample Analyzed	Boring/Well Construction Details
0–30		For lithologic description refer to log of boring CI-11-60								Monument; Casing; Bentonite Seal; 2/12 Sand Pack; 0.01 Slot PVC Well Screen

Well Construction Information

Monument Type:	Flush Mount	**Filter Pack:**	2/12 Sand	**Ground Surface Elevation (ft msl):**	NA
Casing Diameter (in):	2.0	**Surface Seal:**	Cement	**Top of Casing Elevation (ft msl):**	NA
Screen Slot Size (in):	0.01	**Annular Seal:**	Bentonite	**Surveyed Location:**	**X:**NA
Screened Interval (ft bgs):	20-30	**Boring Abandonment:**	NA		**Y:**NA

FARALLON consulting
975 5th Avenue Northwest
Issaquah, Washington 98027

Log of Boring: CI-11-60


Client: Capital Industries
Project: Capital Industries
Location: Seattle, WA

Farallon PN: 457-004

Logged By: R.Hibbs

Date/Time Started:	5/27/2010 0800	**Sampler Type:**	D and M Split Spoon 18"x2"
Date/Time Completed:	5/27/2010 1130	**Drive Hammer (lbs):**	300
Equipment:	CME 75	**Depth of Water (ft bgs):**	10.0
Drilling Company:	Cascade Drilling	**Total Boring Depth (ft bgs):**	61.5
Drilling Foreman:	Scott	**Total Well Depth (ft bgs):**	60.0
Drilling Method:	Hollow Stem Auger		

Depth (feet bgs)	Sample Interval	Lithologic Description	USCS	USGS Graphic	% Recovery	Blow Counts	PID (ppmv)	Sample ID	Sample Analyzed	Boring/Well Construction Details
10		10.0-11.5' Poorly graded SAND (95% sand, 5% silt), fine to medium sand, black, wet, no odor.	SP		100	8/10/15	4.4	CI-11-60-10 @ 0815		Bentonite Seal
20		20.0-21.5' Poorly graded SAND (95% sand, 5% silt), fine to medium sand, black, wet, no odor, organic material observed at 20.0' bgs.	SP		100	6/12/15	3.4	CI-11-60-20 @ 0825		Casing
30		30.0-31.5' Poorly graded SAND (95% sand, 5% silt), fine to medium sand, black, wet, no odor.	SP		100	12/18/23	5.5	CI-11-60-30 @ 0835		

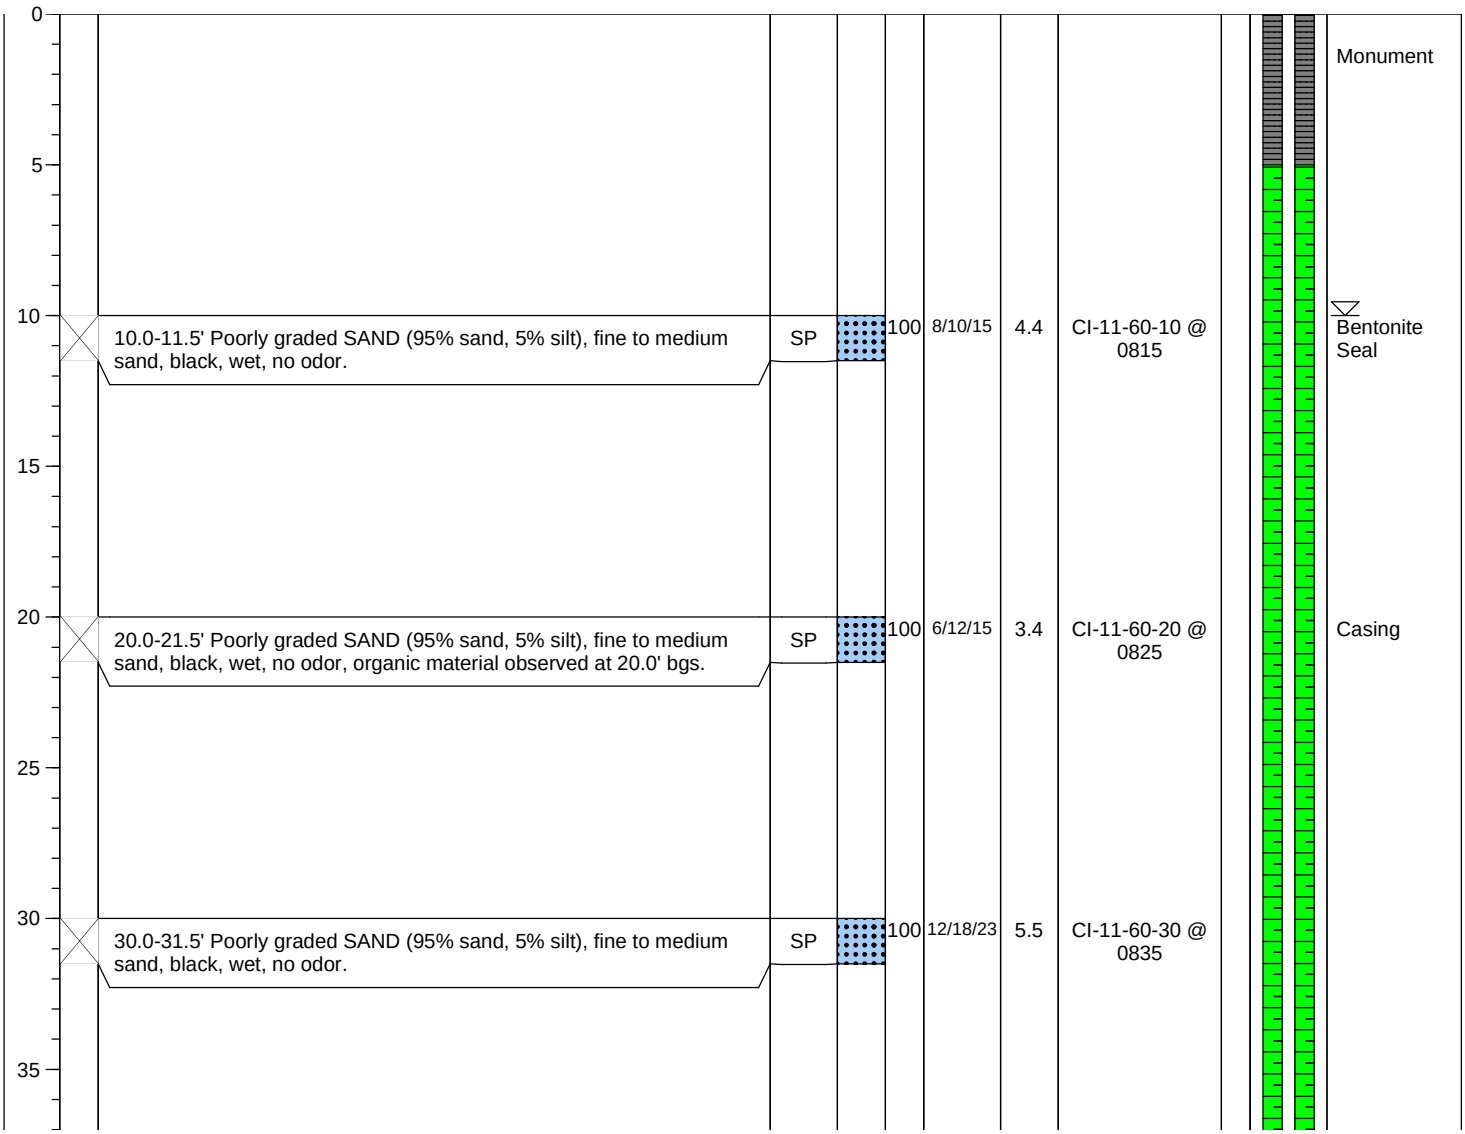

Well Construction Information

Monument Type:	Flush Mount	**Filter Pack:**	2/12 Sand	**Ground Surface Elevation (ft msl):**	NA
Casing Diameter (in):	2.0	**Surface Seal:**	Grout	**Top of Casing Elevation (ft msl):**	NA
Screen Slot Size (in):	0.01	**Annular Seal:**	Bentonite	**Surveyed Location:**	**X:**NA
Screened Interval (ft bgs):	50.0-60.0	**Boring Abandonment:**	NA		**Y:**NA

FARALLON consulting
975 5th Avenue Northwest
Issaquah, Washington 98027

Log of Boring: CI-11-60

Depth (feet bgs)	Sample Interval	Lithologic Description	USCS	USGS Graphic	% Recovery	Blow Counts	PID (ppmv)	Sample ID	Sample Analyzed	Well Construction Details
40		40.0-41.5' Poorly graded SAND (95% sand, 5% silt), fine to medium sand, black, wet, no odor.	SP		100	18/23/25	3.6	CI-11-60-40 @ 0845		
45										
50		50.0-51.5' Poorly graded SAND (95% sand, 5% silt), fine to medium sand, black, wet, no odor.	SP		100	20/28/32	7.5	CI-11-60-50 @ 0900		2/12 Sand Pack
55										0.01 Slot PVC Well Screen
60					0	20/26/30				

Well Construction Information

Monument Type:	Flush Mount	**Filter Pack:**	2/12 Sand	**Ground Surface Elevation (ft msl):**	NA
Casing Diameter (in):	2.0	**Surface Seal:**	Grout	**Top of Casing Elevation (ft msl):**	NA
Screen Slot Size (in):	0.01	**Annular Seal:**	Bentonite	**Surveyed Location:**	**X:**NA
Screened Interval (ft bgs):	50.0-60.0	**Boring Abandonment:**	NA		**Y:**NA

FARALLON consulting
975 5th Avenue Northwest
Issaquah, Washington 98027

Log of Boring: CI-11-WT

Client: Capital Industries
Project: Capital Industries
Location: Seattle, WA

Farallon PN: 457-004

Logged By: J. Ruark

Date/Time Started:	5/27/10	**Sampler Type:**	NA
Date/Time Completed:	5/27/10	**Drive Hammer (lbs):**	NA
Equipment:	CME 75	**Depth of Water (ft bgs):**	NA
Drilling Company:	Cascade Drilling	**Total Boring Depth (ft bgs):**	20
Drilling Foreman:	Scott Curtis	**Total Well Depth (ft bgs):**	20
Drilling Method:	Hollow Stem Auger		

Depth (feet bgs)	Sample Interval	Lithologic Description	USCS	USGS Graphic	% Recovery	Blow Counts	PID (ppmv)	Sample ID	Sample Analyzed	Boring/Well Construction Details
0		For lithologic description refer to log of boring CI-11-60.								Monument; Casing; Bentonite Seal; 2/12 Sand Pack; 0.01 Slot PVC Well Screen
5										
10										
15										
20										

Well Construction Information

Monument Type:	Flush Mount	**Filter Pack:**	2/12 Sand	**Ground Surface Elevation (ft msl):**	NA
Casing Diameter (in):	2.0	**Surface Seal:**	Cement	**Top of Casing Elevation (ft msl):**	NA
Screen Slot Size (in):	0.01	**Annular Seal:**	Bentonite	**Surveyed Location:**	**X:**NA
Screened Interval (ft bgs):	10-20	**Boring Abandonment:**	NA		**Y:**NA

FARALLON consulting
975 5th Avenue Northwest
Issaquah, Washington 98027

Log of Boring: CI-12-30


Client: Capital Industries
Project: Capital Industries
Location: Seattle, WA

Farallon PN: 457-004

Logged By: K. Scott

Date/Time Started:	3/4/2010	**Sampler Type:**	NA
Date/Time Completed:	3/4/2010	**Drive Hammer (lbs.):**	NA
Equipment:	CME 75	**Depth of Water ATD (ft bgs):**	NA
Drilling Company:	Cascade Drilling	**Total Boring Depth (ft bgs):**	30
Drilling Foreman:	Steve Choate	**Total Well Depth (ft bgs):**	30
Drilling Method:	Hollow Stem Auger		

Depth (feet bgs.)	Sample Interval	Lithologic Description	USCS	USGS Graphic	% Recovery	Blow Counts 8/8/8	PID (ppm)	Sample ID	Sample Analyzed	Boring/Well Construction Details
0		Lithology data not collected due to heaving sands.								Monument
5										Bentonite Seal
10										
15										Casing
20										2/12 Sand Pack
25										0.01 Slot PVC Well Screen
30										



Well Construction Information

Monument Type: Flush Mount
Casing Diameter (inches): 2.0
Screen Slot Size (inches): 0.01
Screened Interval (ft bgs): 20-30

Filter Pack: 2/12 Sand
Surface Seal: Grout
Annular Seal: Bentonite

Ground Surface Elevation (ft): NA
Top of Casing Elevation (ft): NA
Boring Abandonment: NA
Surveyed Location: **X:** NA **Y:** NA

FARALLON consulting
975 5th Avenue Northwest
Issaquah, Washington 98027

Log of Boring: CI-12-60

Client: Capital Industries
Project: Capital Industries
Location: Seattle, WA

Farallon PN: 457-004

Logged By: K. Scott

Date/Time Started:	3/4/2010	**Sampler Type:**	NA
Date/Time Completed:	3/4/2010	**Drive Hammer (lbs.):**	NA
Equipment:	CME 75	**Depth of Water ATD (ft bgs):**	NA
Drilling Company:	Cascade Drilling	**Total Boring Depth (ft bgs):**	60
Drilling Foreman:	Steve Choate	**Total Well Depth (ft bgs):**	60
Drilling Method:	Hollow Stem Auger		

Depth (feet bgs.)	Sample Interval	Lithologic Description	USCS	USGS Graphic	% Recovery	Blow Counts 8/8/8	PID (ppm)	Sample ID	Sample Analyzed	Boring/Well Construction Details
0–60		Lithology data not collected due to heaving sands.								Monument; Bentonite Seal; Casing; 2/12 Sand Pack; 0.01 Slot PVC Well Screen



Well Construction Information

Monument Type: Flush Mount
Casing Diameter (inches): 2.0
Screen Slot Size (inches): 0.01
Screened Interval (ft bgs): 50-60

Filter Pack: 2/12 Sand
Surface Seal: Grout
Annular Seal: Bentonite

Ground Surface Elevation (ft): NA
Top of Casing Elevation (ft): NA
Boring Abandonment: NA
Surveyed Location: **X:** NA **Y:** NA

FARALLON consulting
975 5th Avenue Northwest
Issaquah, Washington 98027

Log of Boring: CI-12-WT

Client: Capital Industries
Project: Capital Industries
Location: Seattle, WA

Farallon PN: 457-004

Logged By: K. Scott

Date/Time Started:	3/4/2010	**Sampler Type:**	NA
Date/Time Completed:	3/4/2010	**Drive Hammer (lbs.):**	NA
Equipment:	CME 75	**Depth of Water ATD (ft bgs):**	NA
Drilling Company:	Cascade Drilling	**Total Boring Depth (ft bgs):**	20
Drilling Foreman:	Steve Choate	**Total Well Depth (ft bgs):**	20
Drilling Method:	Hollow Stem Auger		

Depth (feet bgs.)	Sample Interval	Lithologic Description	USCS	USGS Graphic	% Recovery	Blow Counts 8/8/8	PID (ppm)	Sample ID	Sample Analyzed	Boring/Well Construction Details
0		Lithology data not collected due to heaving sands.								Monument; Bentonite Seal; Casing; 2/12 Sand Pack; 0.01 Slot PVC Well Screen
5										
10										
15										
20										

Well Construction Information

Monument Type: Flush Mount
Casing Diameter (inches): 2.0
Screen Slot Size (inches): 0.01
Screened Interval (ft bgs): 10-20

Filter Pack: 2/12 Sand
Surface Seal: Grout
Annular Seal: Bentonite

Ground Surface Elevation (ft): NA
Top of Casing Elevation (ft): NA
Boring Abandonment: NA
Surveyed Location: **X:** NA **Y:** NA

FARALLON consulting
975 5th Avenue Northwest
Issaquah, Washington 98027

Log of Boring: CI-13-30

Client: Capital Industries
Project: Capital Industries
Location: Seattle, WA

Farallon PN: 457-004

Logged By: J. Ruark

Date/Time Started:	6/2/10	**Sampler Type:**	NA
Date/Time Completed:	6/2/10	**Drive Hammer (lbs):**	NA
Equipment:	CME 75	**Depth of Water (ft bgs):**	NA
Drilling Company:	Cascade Drilling	**Total Boring Depth (ft bgs):**	30
Drilling Foreman:	Scott Curtis	**Total Well Depth (ft bgs):**	30
Drilling Method:	Hollow Stem Auger		

Depth (feet bgs)	Sample Interval	Lithologic Description	USCS	USGS Graphic	% Recovery	Blow Counts	PID (ppmv)	Sample ID	Sample Analyzed	Boring/Well Construction Details
0		For lithologic description refer to log of boring CI-13-60								Monument
5										Casing
10										Bentonite Seal
15										
20										2/12 Sand Pack
25										0.01 Slot PVC Well Screen
30										

Well Construction Information

Monument Type:	Flush Mount	**Filter Pack:**	2/12 Sand	**Ground Surface Elevation (ft msl):**	NA
Casing Diameter (in):	2.0	**Surface Seal:**	Cement	**Top of Casing Elevation (ft msl):**	NA
Screen Slot Size (in):	0.01	**Annular Seal:**	Bentonite	**Surveyed Location:**	**X:**NA
Screened Interval (ft bgs):	20-30	**Boring Abandonment:**	NA		**Y:**NA

FARALLON consulting
975 5th Avenue Northwest
Issaquah, Washington 98027

Log of Boring: CI-13-60

Client: Capital Industries
Project: Capital Industries
Location: Seattle, WA

Farallon PN: 457-004

Logged By: J.Ruark

Date/Time Started:	6/1/2010 1300	**Sampler Type:**	D and M Split Spoon 18"x2"
Date/Time Completed:	6/1/2010 1545	**Drive Hammer (lbs):**	300
Equipment:	CME 75	**Depth of Water (ft bgs):**	9.0
Drilling Company:	Cascade Drilling	**Total Boring Depth (ft bgs):**	61.5
Drilling Foreman:	Curtis	**Total Well Depth (ft bgs):**	60.0
Drilling Method:	Hollow Stem Auger		

Depth (feet bgs)	Sample Interval	Lithologic Description	USCS	USGS Graphic	% Recovery	Blow Counts	PID (ppmv)	Sample ID	Sample Analyzed	Boring/Well Construction Details
10		10.0-11.2' Poorly graded SAND (95% sand, 5% silt), fine to medium sand, brown to grey, medium dense, wet, no odor.	SP		75	5/6/5	0.3	CI-13-60-10 @ 1415		Bentonite Seal
20		20.0-21.5' Poorly graded SAND (100% sand), fine to medium sand, grey, very dense, wet, no odor.	SP		100	15/15/17	0.3	CI-13-60-20 @ 1421		Casing
30		30.0-31.5' Poorly graded SAND (100% sand), fine to medium sand, grey, very dense, wet, no odor, wood debris.	SP		70	12/15/19	0.6	CI-13-60-30 @ 1445		
		30.1-31.0' Poorly graded SAND (100% sand), fine to medium sand, grey, very dense, wet, no odor.								


Well Construction Information

Monument Type:	Flush Mount	**Filter Pack:**	2/12 Sand	**Ground Surface Elevation (ft msl):**	NA
Casing Diameter (in):	2.0	**Surface Seal:**	Grout	**Top of Casing Elevation (ft msl):**	NA
Screen Slot Size (in):	0.01	**Annular Seal:**	Bentonite	**Surveyed Location:**	**X:**NA
Screened Interval (ft bgs):	50.0-60.0	**Boring Abandonment:**	NA		**Y:**NA

FARALLON consulting
975 5th Avenue Northwest
Issaquah, Washington 98027

Log of Boring: CI-13-60

Depth (feet bgs)	Sample Interval	Lithologic Description	USCS	USGS Graphic	% Recovery	Blow Counts	PID (ppmv)	Sample ID	Sample Analyzed	Well Construction Details
40		40.0-40.8' Poorly graded SAND (100% sand), fine to medium sand, grey, dense, wet, no odor.	SP		50	4/17/19	0.4	CI-13-60-40 @ 1500		
45										
50		50.0-50.2' Poorly graded SAND (100% sand), fine to medium sand, grey, very dense, wet, no odor.	SP		15	20/4/50	0.2	CI-13-60-50 @ 1515		2/12 Sand Pack
55										0.01 Slot PVC Well Screen
60					0					

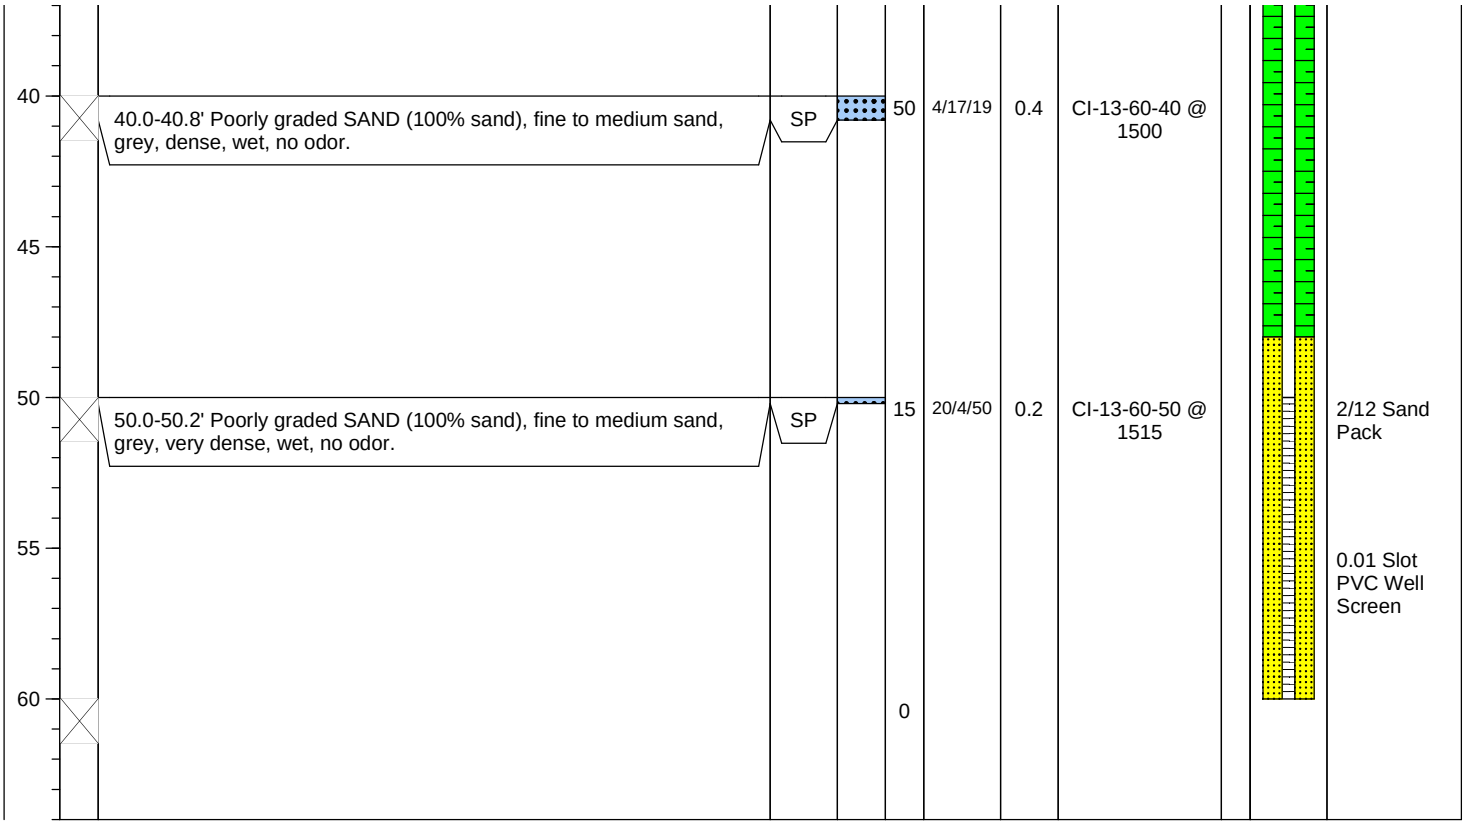

Well Construction Information

Monument Type:	Flush Mount	**Filter Pack:**	2/12 Sand	**Ground Surface Elevation (ft msl):**	NA
Casing Diameter (in):	2.0	**Surface Seal:**	Grout	**Top of Casing Elevation (ft msl):**	NA
Screen Slot Size (in):	0.01	**Annular Seal:**	Bentonite	**Surveyed Location:**	**X:**NA
Screened Interval (ft bgs):	50.0-60.0	**Boring Abandonment:**	NA		**Y:**NA

FARALLON consulting
975 5th Avenue Northwest
Issaquah, Washington 98027

Log of Boring: CI-137-50

Client: Capital Industries
Project: Capital Industries
Location: Seattle, WA

Farallon PN: 457-004

Logged By: D. Clement

Date/Time Started:	2/9/2010	**Sampler Type:**	NA
Date/Time Completed:	2/9/2010	**Drive Hammer (lbs.):**	NA
Equipment:	CME 75	**Depth of Water ATD (ft bgs):**	NA
Drilling Company:	Cascade Drilling	**Total Boring Depth (ft bgs):**	50
Drilling Foreman:	Andy	**Total Well Depth (ft bgs):**	50
Drilling Method:	Hollow Stem Auger		

Depth (feet bgs.)	Sample Interval	Lithologic Description	USCS	USGS Graphic	% Recovery	Blow Counts 8/8/8	PID (ppm)	Sample ID	Sample Analyzed	Boring/Well Construction Details
0–50		Lithology data not collected due to heaving sands.								Monument; Bentonite Seal; Casing; 2/12 Sand Pack; 0.01 Slot PVC Well Screen

Well Construction Information

Monument Type: Flush Mount
Casing Diameter (inches): 2.0
Screen Slot Size (inches): 0.01
Screened Interval (ft bgs): 40-50

Filter Pack: 2/12 Sand
Surface Seal: Grout
Annular Seal: Bentonite

Ground Surface Elevation (ft): NA
Top of Casing Elevation (ft): NA
Boring Abandonment: NA
Surveyed Location: **X:** NA **Y:** NA

FARALLON consulting
975 5th Avenue Northwest
Issaquah, Washington 98027

Log of Boring: CI-13-WT

Client: Capital Industries
Project: Capital Industries
Location: Seattle, WA

Farallon PN: 457-004

Logged By: J. Ruark

Date/Time Started:	6/2/10	**Sampler Type:**	NA
Date/Time Completed:	6/2/10	**Drive Hammer (lbs):**	NA
Equipment:	CME 75	**Depth of Water (ft bgs):**	NA
Drilling Company:	Cascade Drilling	**Total Boring Depth (ft bgs):**	19.5
Drilling Foreman:	Scott Curtis	**Total Well Depth (ft bgs):**	19.5
Drilling Method:	Hollow Stem Auger		

Depth (feet bgs)	Sample Interval	Lithologic Description	USCS	USGS Graphic	% Recovery	Blow Counts	PID (ppmv)	Sample ID	Sample Analyzed	Boring/Well Construction Details
0		For lithologic description refer to log of boring CI-13-60.								Monument; Casing; Bentonite Seal; 2/12 Sand Pack; 0.01 Slot PVC Well Screen
5										
10										
15										
20										

Well Construction Information

Monument Type:	Flush Mount	**Filter Pack:**	2/12 Sand	**Ground Surface Elevation (ft msl):**	NA
Casing Diameter (in):	2.0	**Surface Seal:**	Cement	**Top of Casing Elevation (ft msl):**	NA
Screen Slot Size (in):	0.01	**Annular Seal:**	Bentonite	**Surveyed Location:**	**X:**NA
Screened Interval (ft bgs):	9.5-19.5	**Boring Abandonment:**	NA		**Y:**NA

FARALLON consulting
975 5th Avenue Northwest
Issaquah, Washington 98027

Log of Boring: CI-14-35

Client: Capital Industries
Project: Capital Industries
Location: Seattle, WA

Farallon PN: 457-004

Logged By: R. Hibbs

Date/Time Started:	5/26/10	**Sampler Type:**	NA
Date/Time Completed:	5/26/10	**Drive Hammer (lbs):**	NA
Equipment:	CME 75	**Depth of Water (ft bgs):**	NA
Drilling Company:	Cascade Drilling	**Total Boring Depth (ft bgs):**	35
Drilling Foreman:	Scott Curtis	**Total Well Depth (ft bgs):**	35
Drilling Method:	Hollow Stem Auger		

Depth (feet bgs)	Sample Interval	Lithologic Description	USCS	USGS Graphic	% Recovery	Blow Counts	PID (ppmv)	Sample ID	Sample Analyzed	Boring/Well Construction Details
0–35		For lithologic description refer to log of boring CI-14-70								Monument; Casing; Bentonite Seal; 2/12 Sand Pack; 0.01 Slot PVC Well Screen

Well Construction Information

Monument Type:	Flush Mount	**Filter Pack:**	2/12 Sand	**Ground Surface Elevation (ft msl):**	NA
Casing Diameter (in):	2.0	**Surface Seal:**	Cement	**Top of Casing Elevation (ft msl):**	NA
Screen Slot Size (in):	0.01	**Annular Seal:**	Bentonite	**Surveyed Location:**	**X:**NA
Screened Interval (ft bgs):	25-35	**Boring Abandonment:**	NA		**Y:**NA

FARALLON consulting
975 5th Avenue Northwest
Issaquah, Washington 98027

Log of Boring: CI-14-70

Client: Capital Industries
Project: Capital Industries
Location: Seattle, WA

Farallon PN: 457-004

Logged By: R.Hibbs

Date/Time Started:	5/26/2010 0815	**Sampler Type:**	D and M Split Spoon 18"x2"
Date/Time Completed:	5/25/2010 1000	**Drive Hammer (lbs):**	300
Equipment:	CME 75	**Depth of Water (ft bgs):**	10.0
Drilling Company:	Cascade Drilling	**Total Boring Depth (ft bgs):**	71.5
Drilling Foreman:	Scott	**Total Well Depth (ft bgs):**	70.0
Drilling Method:	Hollow Stem Auger		

Depth (feet bgs)	Sample Interval	Lithologic Description	USCS	USGS Graphic	% Recovery	Blow Counts	PID (ppmv)	Sample ID	Sample Analyzed	Boring/Well Construction Details
10		10.0-11.0' Poorly graded SAND (95% sand, 5% silt), fine to medium sand, black to grey, moist, no odor.	SP							
		11.0-11.5' Silty SAND (60% sand, 40% silt), fine sand, moist, brown, no odor.	SM		100	10/11/13	3.4	CI-14-70-11 @ 0835		
20		20.0-21.5' Poorly graded SAND (95% sand, 5% silt), fine to medium sand, black to grey, wet, no odor.	SP		100	10/15/18	9.1	CI-14-70-20 @ 0840		

Monument

Bentonite Seal

Well Construction Information

Monument Type:	Flush Mount	**Filter Pack:**	2/12 Sand	**Ground Surface Elevation (ft msl):**	NA
Casing Diameter (in):	2.0	**Surface Seal:**	Grout	**Top of Casing Elevation (ft msl):**	NA
Screen Slot Size (in):	0.01	**Annular Seal:**	Bentonite	**Surveyed Location:**	**X:**NA
Screened Interval (ft bgs):	60.0-70.0	**Boring Abandonment:**	NA		**Y:**NA

FARALLON consulting
975 5th Avenue Northwest
Issaquah, Washington 98027

Log of Boring: CI-14-70

Depth (feet bgs)	Sample Interval	Lithologic Description	USCS	USGS Graphic	% Recovery	Blow Counts	PID (ppmv)	Sample ID	Sample Analyzed	Well Construction Details
30		30.0-31.0' Poorly graded SAND (95% sand, 5% silt), fine to medium sand, black to grey, wet, no odor.	SP		75	18/23/25	7.7	CI-14-70-30 @ 0845		
40		40.0-41.5' Poorly graded SAND (95% sand, 5% silt), fine to medium sand, black to grey, wet, no odor, 0.2' silty sand lense at 40.2' bgs.	SP		100	18/28/32	3.4	CI-14-70-40 @ 0850		Casing

Well Construction Information

Monument Type:	Flush Mount	**Filter Pack:**	2/12 Sand	**Ground Surface Elevation (ft msl):**	NA
Casing Diameter (in):	2.0	**Surface Seal:**	Grout	**Top of Casing Elevation (ft msl):**	NA
Screen Slot Size (in):	0.01	**Annular Seal:**	Bentonite	**Surveyed Location:**	**X:**NA
Screened Interval (ft bgs):	60.0-70.0	**Boring Abandonment:**	NA		**Y:**NA

FARALLON consulting
975 5th Avenue Northwest
Issaquah, Washington 98027

Log of Boring: CI-14-70

Depth (feet bgs)	Sample Interval	Lithologic Description	USCS	USGS Graphic	% Recovery	Blow Counts	PID (ppmv)	Sample ID	Sample Analyzed	Well Construction Details
50		50.-51.5' Poorly graded SAND (95% sand, 5% silt), fine to medium sand, black to grey, wet, no odor.	SP		100	28/32/37	2.9	CI-14-70-50 @ 0910		
55										
60		60.0-61.0' SILT (90% silt, 10% sand), fine sand, grey, wet, no odor.	ML							2/12 Sand Pack
		61.0-61.5' Poorly graded SAND (95% sand, 5% silt), fine to medium sand, grey to black, wet, no odor.	SP			23/30/38	5.0	CI-14-70-61 @ 0927		
65										0.01 Slot PVC Well Screen
70		70.0-71.5' Poorly graded SAND (95% sand, 5% silt), fine to medium sand, grey to black, wet, no odor.	SP		100	24/33/38	6.1	CI-14-70-70 @ 0935		
75										

Well Construction Information

Monument Type:	Flush Mount	**Filter Pack:**	2/12 Sand	**Ground Surface Elevation (ft msl):**	NA
Casing Diameter (in):	2.0	**Surface Seal:**	Grout	**Top of Casing Elevation (ft msl):**	NA
Screen Slot Size (in):	0.01	**Annular Seal:**	Bentonite	**Surveyed Location:**	**X:**NA
Screened Interval (ft bgs):	60.0-70.0	**Boring Abandonment:**	NA		**Y:**NA

FARALLON consulting
975 5th Avenue Northwest
Issaquah, Washington 98027

Log of Boring: CI-14-WT

Client: Capital Industries
Project: Capital Industries
Location: Seattle, WA

Farallon PN: 457-004

Logged By: R. Hibbs

Date/Time Started:	5/26/10	**Sampler Type:**	NA
Date/Time Completed:	5/26/10	**Drive Hammer (lbs):**	NA
Equipment:	CME 75	**Depth of Water (ft bgs):**	NA
Drilling Company:	Cascade Drilling	**Total Boring Depth (ft bgs):**	20
Drilling Foreman:	Scott Curtis	**Total Well Depth (ft bgs):**	20
Drilling Method:	Hollow Stem Auger		

Depth (feet bgs)	Sample Interval	Lithologic Description	USCS	USGS Graphic	% Recovery	Blow Counts	PID (ppmv)	Sample ID	Sample Analyzed	Boring/Well Construction Details
0		For lithologic description refer to log of boring CI-14-70.								Monument
5										Casing
										Bentonite Seal
10										2/12 Sand Pack
15										0.01 Slot PVC Well Screen
20										

Well Construction Information

Monument Type:	Flush Mount	**Filter Pack:**	2/12 Sand	**Ground Surface Elevation (ft msl):**	NA
Casing Diameter (in):	2.0	**Surface Seal:**	Cement	**Top of Casing Elevation (ft msl):**	NA
Screen Slot Size (in):	0.01	**Annular Seal:**	Bentonite	**Surveyed Location:**	**X:**NA
Screened Interval (ft bgs):	10-20	**Boring Abandonment:**	NA		**Y:**NA

FARALLON consulting
975 5th Avenue Northwest
Issaquah, Washington 98027

Log of Boring: CI-15-40


Client: Capital Industries
Project: Capital Industries
Location: Seattle, WA

Farallon PN: 457-004

Logged By: K. Scott

Date/Time Started:	3/3/2010	**Sampler Type:**	NA
Date/Time Completed:	3/3/2010	**Drive Hammer (lbs.):**	NA
Equipment:	CME 75	**Depth of Water ATD (ft bgs):**	NA
Drilling Company:	Cascade Drilling	**Total Boring Depth (ft bgs):**	40
Drilling Foreman:	Steve Choate	**Total Well Depth (ft bgs):**	40
Drilling Method:	Hollow Stem Auger		

Depth (feet bgs.)	Sample Interval	Lithologic Description	USCS	USGS Graphic	% Recovery	Blow Counts 8/8/8	PID (ppm)	Sample ID	Sample Analyzed	Boring/Well Construction Details
0		Lithology data not collected due to heaving sands.								Monument
5										
10										Bentonite Seal
15										
20										Casing
25										
30										2/12 Sand Pack
35										0.01 Slot PVC Well Screen
40										



Well Construction Information

Monument Type: Flush Mount
Casing Diameter (inches): 2.0
Screen Slot Size (inches): 0.01
Screened Interval (ft bgs): 30-40

Filter Pack: 2/12 Sand
Surface Seal: Grout
Annular Seal: Bentonite

Ground Surface Elevation (ft): NA
Top of Casing Elevation (ft): NA
Boring Abandonment: NA
Surveyed Location: **X:** NA **Y:** NA

FARALLON consulting
975 5th Avenue Northwest
Issaquah, Washington 98027

Log of Boring: CI-15-60

Client: Capital Industries
Project: Capital Industries
Location: Seattle, WA

Farallon PN: 457-004

Logged By: K. Scott

Date/Time Started:	3/3/2010	**Sampler Type:**	NA
Date/Time Completed:	3/3/2010	**Drive Hammer (lbs.):**	NA
Equipment:	CME 75	**Depth of Water ATD (ft bgs):**	NA
Drilling Company:	Cascade Drilling	**Total Boring Depth (ft bgs):**	60
Drilling Foreman:	Steve Choate	**Total Well Depth (ft bgs):**	60
Drilling Method:	Hollow Stem Auger		

Depth (feet bgs.)	Sample Interval	Lithologic Description	USCS	USGS Graphic	% Recovery	Blow Counts 8/8/8	PID (ppm)	Sample ID	Sample Analyzed	Boring/Well Construction Details
0–60		Lithology data not collected due to heaving sands.								Monument; Bentonite Seal; Casing; 2/12 Sand Pack; 0.01 Slot PVC Well Screen

Well Construction Information

Monument Type: Flush Mount
Casing Diameter (inches): 2.0
Screen Slot Size (inches): 0.01
Screened Interval (ft bgs): 50-60

Filter Pack: 2/12 Sand
Surface Seal: Grout
Annular Seal: Bentonite

Ground Surface Elevation (ft): NA
Top of Casing Elevation (ft): NA
Boring Abandonment: NA
Surveyed Location: **X:** NA **Y:** NA

FARALLON consulting
975 5th Avenue Northwest
Issaquah, Washington 98027

Log of Boring: CI-16-30

Client: Capital Industries
Project: Capital industries
Location: Seattle, WA

Farallon PN: 457-004

Logged By: Dincer Kayhan

Date/Time Started:	3/19/12	**Sampler Type:**	NA
Date/Time Completed:	3/19/12	**Drive Hammer (lbs.):**	NA
Equipment:	CME 75	**Depth of Water ATD (ft bgs):**	9.0
Drilling Company:	Cascade Drilling	**Total Boring Depth (ft bgs):**	30
Drilling Foreman:	Scott Krueger	**Total Well Depth (ft bgs):**	30
Drilling Method:	Hollow Stem Auger		

Depth (feet bgs.)	Sample Interval	Lithologic Description	USCS	USGS Graphic	% Recovery	Blow Counts 8/8/8	PID (ppm)	Sample ID	Sample Analyzed	Boring/Well Construction Details
0		For lithologic description refer to log of boring CI-16-60.								Grout
5										Water level
10										Bentonite Seal
15										2/12 Sand Pack
20										0.01 Slot PVC Well Screen
25										
30										

Well Construction Information

Monument Type: Flush Mount
Casing Diameter (inches): 2.0
Screen Slot Size (inches): 0.01
Screened Interval (ft bgs): 20-30

Filter Pack: 2-12 Sand
Surface Seal: Grout
Annular Seal: Bentonite

Ground Surface Elevation (ft): NA
Top of Casing Elevation (ft): NA
Boring Abandonment: NA
Surveyed Location: X: NA Y: NA

FARALLON consulting
975 5th Avenue Northwest
Issaquah, Washington 98027

Log of Boring: CI-16-60

Client: Capital Industries
Project: Capital industries
Location: Seattle, WA

Farallon PN: 457-004

Logged By: Dincer Kayhan

Date/Time Started:	3/19/12	**Sampler Type:**	D&M SP 18
Date/Time Completed:	3/19/12	**Drive Hammer (lbs.):**	140
Equipment:	CME 75	**Depth of Water ATD (ft bgs):**	9.0
Drilling Company:	Cascade Drilling	**Total Boring Depth (ft bgs):**	61.5
Drilling Foreman:	Scott Krueger	**Total Well Depth (ft bgs):**	60.0
Drilling Method:	Hollow Stem Auger		

Depth (feet bgs.)	Sample Interval	Lithologic Description	USCS	USGS Graphic	% Recovery	Blow Counts 8/8/8	PID (ppm)	Sample ID	Sample Analyzed	Boring/Well Construction Details
10		10.0-11.3' Poorly graded SAND with silt (90% sand, 10% silt), fine sand, brown, very loose, moist, no odor.	SP-SM		100	2/3/4		NA		Water level
		11.3-11.5' SILT (95% silt, 5% sand), fine sand, brown, medium stiff, moist, no odor.	ML							
20		20.0-21.5' Poorly graded SAND with silt (90% sand, 10% silt), fine sand, brown, very loose, saturated, no odor.	SP-SM		100	5/6/7		NA		
30		30.0-31.5' No recovery.			0	3/5/8		NA		

Grout

Bentonite Seal

Well Construction Information

Monument Type: Flush Mount
Casing Diameter (inches): 2.0
Screen Slot Size (inches): 0.01
Screened Interval (ft bgs): 50-60

Filter Pack: 2-12 Sand
Surface Seal: Grout
Annular Seal: Bentonite

Ground Surface Elevation (ft): NA
Top of Casing Elevation (ft): NA
Boring Abandonment: NA
Surveyed Location: **X:** NA **Y:** NA

FARALLON consulting
975 5th Avenue Northwest
Issaquah, Washington 98027

Log of Boring: CI-16-60

Client: Capital Industries
Project: Capital industries
Location: Seattle, WA

Farallon PN: 457-004

Logged By: Dincer Kayhan

Date/Time Started:	3/19/12	**Sampler Type:**	D&M SP 18
Date/Time Completed:	3/19/12	**Drive Hammer (lbs.):**	140
Equipment:	CME 75	**Depth of Water ATD (ft bgs):**	9.0
Drilling Company:	Cascade Drilling	**Total Boring Depth (ft bgs):**	61.5
Drilling Foreman:	Scott Krueger	**Total Well Depth (ft bgs):**	60.0
Drilling Method:	Hollow Stem Auger		

Depth (feet bgs.)	Sample Interval	Lithologic Description	USCS	% Recovery	Blow Counts 8/8/8	Sample ID	Boring/Well Construction Details
35							
40		40.0-41.0' No recovery.		35	9/15/18	NA	
		41.0-41.4' Poorly graded SAND with silt (85% sand, 15% silt), fine sand, brown, loose saturated, no odor.	SP-SM				
		41.4-41.5' No recovery.					
45							
50		50.0-51.4' No recovery.		2	12/16/19	NA	
		51.4-51.5' Lean CLAY with sand (95% clay, 5% sand), fine sand, olive gray, very stiff, saturated, no odor.	CL				2/12 Sand Pack
55							0.01 Slot PVC Well Screen
60		60.0-61.5' Silty SAND (80% sand, 20% silt), fine sand, dark gray, dense, saturated, no odor.	SM	100	12/18/23	NA	

Well Construction Information

Monument Type: Flush Mount
Casing Diameter (inches): 2.0
Screen Slot Size (inches): 0.01
Screened Interval (ft bgs): 50-60

Filter Pack: 2-12 Sand
Surface Seal: Grout
Annular Seal: Bentonite

Ground Surface Elevation (ft): NA
Top of Casing Elevation (ft): NA
Boring Abandonment: NA
Surveyed Location: **X:** NA **Y:** NA

FARALLON consulting
975 5th Avenue Northwest
Issaquah, Washington 98027

Log of Boring: CI-16-WT

Client: Capital Industries
Project: Capital industries
Location: Seattle, WA

Farallon PN: 457-004

Logged By: Dincer Kayhan

Date/Time Started:	3/19/12	**Sampler Type:**	NA
Date/Time Completed:	3/19/12	**Drive Hammer (lbs.):**	NA
Equipment:	CME 75	**Depth of Water ATD (ft bgs):**	9.0
Drilling Company:	Cascade Drilling	**Total Boring Depth (ft bgs):**	20
Drilling Foreman:	Scott Krueger	**Total Well Depth (ft bgs):**	20
Drilling Method:	Hollow Stem Auger		

Depth (feet bgs.)	Sample Interval	Lithologic Description	USCS	USGS Graphic	% Recovery	Blow Counts 8/8/8	PID (ppm)	Sample ID	Sample Analyzed	Boring/Well Construction Details
0		For lithologic description refer to log of boring CI-16-60.								Grout; Bentonite Seal; Water level; 2/12 Sand Pack; 0.01 Slot PVC Well Screen
5										
10										
15										
20										

Well Construction Information

Monument Type: Flush Mount
Casing Diameter (inches): 2.0
Screen Slot Size (inches): 0.01
Screened Interval (ft bgs): 10-20

Filter Pack: 2-12 Sand
Surface Seal: Grout
Annular Seal: Bentonite

Ground Surface Elevation (ft): NA
Top of Casing Elevation (ft): NA
Boring Abandonment: NA
Surveyed Location: X: NA Y: NA

FARALLON consulting
975 5th Avenue Northwest
Issaquah, Washington 98027

Log of Boring: CI-17-30

Client: Capital Industries
Project: Capital Industries
Location: Seattle, WA

Farallon PN: 457-004

Logged By: Dincer Kayhan

Date/Time Started:	3/16/12	**Sampler Type:**	D&M SP 18
Date/Time Completed:	3/16/12	**Drive Hammer (lbs.):**	140
Equipment:	CME 75	**Depth of Water ATD (ft bgs):**	NE
Drilling Company:	Cascade Drilling	**Total Boring Depth (ft bgs):**	31.5
Drilling Foreman:	James Goble	**Total Well Depth (ft bgs):**	30.0
Drilling Method:	Hollow Stem Auger		

Depth (feet bgs.)	Sample Interval	Lithologic Description	USCS	USGS Graphic	% Recovery	Blow Counts 8/8/8	PID (ppm)	Sample ID	Sample Analyzed	Boring/Well Construction Details
10		10.0-10.5' SILT with sand (85% silt, 15% sand), fine sand, black, medium stiff, moist, no odor, wood debris.	ML		100	5/5/7		NA		Bentonite Seal
		10.5-11.5' Poorly graded SAND with silt (90% sand, 10% silt), fine sand, black, loose, moist, no odor.	SP-SM							
20		20.0-21.0' Poorly graded SAND with silt (90% sand, 10% silt), fine sand, black, loose, moist, no odor, contains a stringer of clay.	SP-SM		80	12/15/20		NA		2/12 Sand Pack
30		30.0-31.5 Poorly graded SAND with silt (90% sand, 10% silt), fine sand, black, loose, moist, no odor.	SP-SM		100	16/19/22		NA		0.01 Slot PVC Well Screen

Grout

Well Construction Information

Monument Type: Flush Mount
Casing Diameter (inches): 2.0
Screen Slot Size (inches): 0.01
Screened Interval (ft bgs): 20-30

Filter Pack: 2-12 Sand
Surface Seal: Grout
Annular Seal: Bentonite

Ground Surface Elevation (ft): NA
Top of Casing Elevation (ft): NA
Boring Abandonment: NA
Surveyed Location: **X:** NA **Y:** NA

FARALLON consulting
975 5th Avenue Northwest
Issaquah, Washington 98027

Log of Boring: CI-17-WT

Client: Capital Industries
Project: Capital Industries
Location: Seattle, WA

Farallon PN: 457-004

Logged By: Dincer Kayhan

Date/Time Started:	3/16/12	**Sampler Type:**	NA
Date/Time Completed:	3/16/12	**Drive Hammer (lbs.):**	NA
Equipment:	CME 75	**Depth of Water ATD (ft bgs):**	NA
Drilling Company:	Cascade Drilling	**Total Boring Depth (ft bgs):**	20
Drilling Foreman:	James Goble	**Total Well Depth (ft bgs):**	20
Drilling Method:	Hollow Stem Auger		

Depth (feet bgs.)	Sample Interval	Lithologic Description	USCS	USGS Graphic	% Recovery	Blow Counts 8/8/8	PID (ppm)	Sample ID	Sample Analyzed	Boring/Well Construction Details
0		For lithologic description refer to log of boring CI-17-30.								Grout; Bentonite Seal; 2/12 Sand Pack; 0.01 Slot PVC Well Screen
5										
10										
15										
20										

Well Construction Information

Monument Type: Flush Mount
Casing Diameter (inches): 2.0
Screen Slot Size (inches): 0.01
Screened Interval (ft bgs): 10-20

Filter Pack: 2-12 Sand
Surface Seal: Grout
Annular Seal: Bentonite

Ground Surface Elevation (ft): NA
Top of Casing Elevation (ft): NA
Boring Abandonment: NA
Surveyed Location: X: NA Y: NA

FARALLON consulting
975 5th Avenue Northwest
Issaquah, Washington 98027

Log of Boring: CI-18-30

Client: Capital Industries
Project: Capital Industries
Location: Seattle, WA

Farallon PN: 457-004

Logged By: Dincer Kayhan

Date/Time Started:	3/15/12	**Sampler Type:**	D&M SP 18
Date/Time Completed:	3/15/12	**Drive Hammer (lbs.):**	140
Equipment:	CME 75	**Depth of Water ATD (ft bgs):**	NE
Drilling Company:	Cascade Drilling	**Total Boring Depth (ft bgs):**	31.5
Drilling Foreman:	James Goble	**Total Well Depth (ft bgs):**	30
Drilling Method:	Hollow Stem Auger		

Depth (feet bgs.)	Sample Interval	Lithologic Description	USCS	USGS Graphic	% Recovery	Blow Counts 8/8/8	PID (ppm)	Sample ID	Sample Analyzed	Boring/Well Construction Details
10		10.0-11.5' Poorly graded SAND with silt (90% sand, 10% silt), fine sand, brown, loose, moist, no odor.	SP-SM		100	9/8/11		NA		Grout; Bentonite Seal
20		20.0-21.5' Poorly graded SAND with silt (90% sand, 10% silt), fine sand, brown to black, medium dense, moist to saturated at 20.5, no odor.	SP-SM		100	10/13/15		NA		2/12 Sand Pack; 0.01 Slot PVC Well Screen
30		30.0-30.5' Poorly graded SAND with silt (90% sand, 10% silt), fine sand, black, medium dense, saturated, no odor.	SP-SM		80	14/21/19		NA		
		30.5-30.8' SILT (90% silt, 10% sand), fine sand, medium dense, black, no odor.	ML							
35		30.8-31' Poorly graded SAND with silt (90% sand, 10% silt), fine sand, black, medium dense, saturated, no odor.	SP-SM							
40										

Well Construction Information

Monument Type: NA
Casing Diameter (inches): 2.0
Screen Slot Size (inches): 0.01
Screened Interval (ft bgs): 20-30

Filter Pack: 2-12 Sand
Surface Seal: Grout
Annular Seal: Bentonite

Ground Surface Elevation (ft): NA
Top of Casing Elevation (ft): NA
Boring Abandonment: NA
Surveyed Location: X: NA Y: NA

FARALLON consulting
975 5th Avenue Northwest
Issaquah, Washington 98027

Log of Boring: CI-18-WT

Client: Capital Industries
Project: Capital Industries
Location: Seattle, WA

Farallon PN: 457-004

Logged By: Dincer Kayhan

Date/Time Started:	3/15/12	**Sampler Type:**	NA
Date/Time Completed:	3/15/12	**Drive Hammer (lbs.):**	NA
Equipment:	CME 75	**Depth of Water ATD (ft bgs):**	NA
Drilling Company:	Cascade Drilling	**Total Boring Depth (ft bgs):**	20
Drilling Foreman:	James Goble	**Total Well Depth (ft bgs):**	20
Drilling Method:	Hollow Stem Auger		

Depth (feet bgs.)	Sample Interval	Lithologic Description	USCS	USGS Graphic	% Recovery	Blow Counts 8/8/8	PID (ppm)	Sample ID	Sample Analyzed	Boring/Well Construction Details
0		For lithologic description refer to log of boring CI-18-30.								Grout; Bentonite Seal; 2/12 Sand Pack; 0.01 Slot PVC Well Screen
5										
10										
15										
20										

Well Construction Information

Monument Type: Flush Mount
Casing Diameter (inches): 2.0
Screen Slot Size (inches): 0.01
Screened Interval (ft bgs): 10-20

Filter Pack: 2-12 Sand
Surface Seal: Grout
Annular Seal: Bentonite

Ground Surface Elevation (ft): NA
Top of Casing Elevation (ft): NA
Boring Abandonment: NA
Surveyed Location: X: NA Y: NA

FARALLON consulting
975 5th Avenue Northwest
Issaquah, Washington 98027

Log of Boring: CI-19-30

Client: Capital Industries
Project: Capital Industries
Location: Seattle, WA

Farallon PN: 457-004

Logged By: Dincer Kayhan

Date/Time Started:	3/13/12 1070	**Sampler Type:**	D&M SP 18
Date/Time Completed:	3/13/12 1200	**Drive Hammer (lbs.):**	140
Equipment:	CME 75	**Depth of Water ATD (ft bgs):**	12.5
Drilling Company:	Cascade Drilling	**Total Boring Depth (ft bgs):**	31.5
Drilling Foreman:	James Goble	**Total Well Depth (ft bgs):**	30.0
Drilling Method:	Hollow Stem Auger		

Depth (feet bgs.)	Sample Interval	Lithologic Description	USCS	USGS Graphic	% Recovery	Blow Counts 8/8/8	PID (ppm)	Sample ID	Sample Analyzed	Boring/Well Construction Details
0		0.0 - 0.4' Asphalt Black.	AC							Grout
10		10.0-11.0' SILT with sand (80% silt, 20% sand), fine sand, gray to black, stiff, moist, odor, wood debris increases with depth.	ML		100	7/6/7		NA		Bentonite Seal
		11.0-11.5' Lean CLAY (90% clay, 10% silt), gray to brown, stiff, moist, odor, intermittent organics.	CL							Water Level
20		20.0-21.2' Poorly graded SAND with silt (90% sand, 10% silt) fine sand, gray, loose, saturated, pretroleum like odor.	SP-SM		80	10/12/12		NA		2/12 Sand Pack
30		30.0-31.2' SAA.	SP-SM		80	9/13/16		NA		0.01 Slot PVC Well Screen

Well Construction Information

Monument Type: Flush Mount
Casing Diameter (inches): 2.0
Screen Slot Size (inches): 0.01
Screened Interval (ft bgs): 20-30

Filter Pack: 2-12 Sand
Surface Seal: Grout
Annular Seal: Bentonite

Ground Surface Elevation (ft): NA
Top of Casing Elevation (ft): NA
Boring Abandonment: NA
Surveyed Location: **X:** NA **Y:** NA

FARALLON consulting
975 5th Avenue Northwest
Issaquah, Washington 98027

Log of Boring: CI-19-WT

Client: Capital Industries
Project: Capital Industries
Location: Seattle, WA

Farallon PN: 457-004

Logged By: Dincer Kayhan

Date/Time Started:	3/13/12	**Sampler Type:**	NA
Date/Time Completed:	3/13/12	**Drive Hammer (lbs.):**	NA
Equipment:	CME 75	**Depth of Water ATD (ft bgs):**	12.5
Drilling Company:	Cascade Drilling	**Total Boring Depth (ft bgs):**	20
Drilling Foreman:	James Goble	**Total Well Depth (ft bgs):**	20
Drilling Method:	Hollow Stem Auger		

Depth (feet bgs.)	Sample Interval	Lithologic Description	USCS	USGS Graphic	% Recovery	Blow Counts 8/8/8	PID (ppm)	Sample ID	Sample Analyzed	Boring/Well Construction Details
0		For lithologic description refer to log of boring CI-19-30.								Grout; Bentonite Seal; Water Level; 2/12 Sand Pack; 0.01 Slot PVC Well Screen
5										
10										
15										
20										

Well Construction Information

Monument Type: Flush Mount
Casing Diameter (inches): 2.0
Screen Slot Size (inches): 0.01
Screened Interval (ft bgs): 10-20

Filter Pack: 2-12 Sand
Surface Seal: Grout
Annular Seal: Bentonite

Ground Surface Elevation (ft): NA
Top of Casing Elevation (ft): NA
Boring Abandonment: NA
Surveyed Location: X: NA Y: NA

PSC PHILIP SERVICES

Monitoring Well Construction

Well ID: C6-141-50

Facility: Georgetown

Date Start: 3/14/02

Date Complete: 3/14/02

Total Boring Depth: 52'

Borehole Diameter: 8"

Contractor: Cascade Drilling Inc


Drillers: ~~Corey Joh~~ Brian Bose

Drill Rig: CME 75

Geologist: Corey Johnson

Well Diameter: 2"

Location Diagram



DEPTH (feet bgs)

Ground Surface

Bottom of Surface Casing: 11"

Top of Annular Seal: 2'

Top of Chips: 2'

Top of Grout: NA

Bottom Top of Chips: 38'

Top of Sand Pack: 38'

Top of Screen: 40

Bottom of Screen: 50

Bottom of Well Cap: 50' 8"

Bottom of Sand Pack: 51' 8"

Bottom of Boring: 52'

Steel Protective Surface Casing

Diameter: 8"

Length: 12"

(Flush) or Stand-Up (w/bollard posts)

Surface Seal Pac-Mix

Type: cement mix

Amount Used: 70 lbs

Annular Seal Pure Gold

Type: ~~Medium bentonite~~ chips

Amount Used: 700 lbs

Riser Casing

Type: PVC Schedule: 40

Diameter: 2"

Well Packing Material

Type: Colorado #: 8/12

Amount Used: 400 lbs

Screen

Type: PVC Schedule: 40

Slot Width: 020

Diameter: 2"

Backfill Material

Type: Native Amount: Heave

Notes:

Casing/Joint Type - Threaded

Permit # A6T765

Depth (ft)	Graphic Log	Unit	Samples: Sample ID	Samples: Type	Samples: Rec/Att	Samples: Blows	Description	Well Construction
0							Not Logged	 Above ground steel monument with bollards. Locking compression well cap. 2-inch diameter riser pipe stick up ~1 ft. 0 - 1.5 ft: Concrete seal 1.5 - 5 ft: 3/8-inch bentonite chips -1 to 5.5 ft: 2-inch diameter PVC Schedule 40 riser pipe. Joints are threaded with o-ring seals. 5 - 16 ft: 10/20 Colorado silica sand 5.5 - 15.5 ft: 2-inch diameter PVC screen, 0.01-inch slot size Borehole diameter 8.5 inches 15.5 - 15.8 ft: 2-inch diameter PVC end cap
5								
10								
15								
20								
25								
30								

Address: 227 S Orcas St
City, State: Seattle, WA
Tax Parcel ID: 172280-1730
Location (TRS): T24N R4W S20; NE1/4 of SW1/4
Lat/Long: N 204861.78 ft, E 1270566.85 ft
Consulting Firm: Pacific Groundwater Group
Logged by: G. Wallace


Drilling Firm: ESN NW
Drilling Method: HSA
Ecology ID: APJ815
DTW: 8.00 ft bmp 2/1/2008
MP Elevation: 17.08 ft
V. Datum: NAVD 88
Date: 1/3/2008

Figure
Boring Log and As-Built
BDC-1-WT

Blaser Die Casting
Remedial Investigation
JK0504.03

PgG

Depth (ft)	Graphic Log	Unit	Samples: Sample ID	Samples: Type	Samples: Rec/Att	Samples: Blows	Description	Well Construction
0								Flush grade steel monument. Locking compression well cap. 2-inch diameter riser pipe.
							Not Logged	0 - 1.5 ft: Concrete seal
								1.5 - 5 ft: 3/8-inch bentonite chips
5								-1 to 7 ft: 2-inch diameter PVC Schedule 40 riser pipe. Joints are threaded with o-ring seals.
								5 - 16 ft: 10/20 Colorado silica sand
10								Borehole diameter 8.5 inches
								6 - 16 ft: 2-inch diameter PVC screen, 0.01-inch slot size
15								16 ft: 2-inch diameter PVC end cap
20								
25								
30								




Address: 202-228 S Mead St
City, State: Seattle, WA
Tax Parcel ID: 172280-1750
Location (TRS): T24N R4W S20; NE1/4 of SW1/4
Lat/Long: N 204731.51 ft, E 1270581.74 ft
Consulting Firm: Pacific Groundwater Group
Logged by: G. Wallace

Drilling Firm: ESN NW
Drilling Method: HSA
Ecology ID: APJ816
DTW: 6.74 ft bmp 2/1/2008
MP Elevation: 15.73 ft
V. Datum: NAVD 88
Date: 1/3/2008

Figure
Boring Log and As-Built
BDC-2-WT

Blaser Die Casting
Remedial Investigation
JK0504.03

PgG

Depth (ft)	Graphic Log	Unit	Samples: Sample ID	Samples: Type	Samples: Rec/Att	Samples: Blows	Description	Well Construction
0							PEA GRAVEL	 Flush grade steel monument. Locking compression well cap. 2-inch diameter riser pipe. 0 - 1.5 ft: Concrete seal -1 to 7 ft: 2-inch diameter PVC Schedule 40 riser pipe. Joints are threaded with o-ring seals. 1.5 - 6 ft: 3/8-inch bentonite chips 6 - 12 ft: 10/20 Colorado silica sand Borehole diameter 8.5 inches 7 - 12 ft: 2-inch diameter PVC screen, 0.01-inch slot size 12ft: PVC End Cap
5							Moist to saturated, brown to gray, medium SAND	
10								
15								
20								
25								
30								

Address: 5700 3rd Ave S
City, State: Seattle, WA
Tax Parcel ID: 172280-1495
Location (TRS): T24N R4W S20; NE1/4 of SW1/4
Lat/Long: N 204757.71 ft, E 1270624.86 ft
Consulting Firm: Pacific Groundwater Group
Logged by: G. Wallace

Drilling Firm: ESN NW
Drilling Method: HSA
Ecology ID: APJ817
DTW: 6.22 ft bmp 2/1/2008
MP Elevation: 15.29 ft
V. Datum: NAVD 88
Date: 1/3/2008

Figure
Boring Log and As-Built
BDC-3-WT

Blaser Die Casting
Remedial Investigation
JK0504.03

PgG

Depth (ft)	Graphic Log	Unit	Samples: Sample ID	Samples: Type	Samples: Rec/Att	Samples: Blows	Description	Well Construction
0							See BDC-3-60	 Flush mount steel monument. Locking compression well cap. 2-inch diameter riser pipe stick down 0.30 ft.
5								0 - 1 ft: Concrete
								6.60 ft (bgs): Depth to water at time of drilling
10								0.30 - 29.2 ft: 2-inch diameter PVC Schedule 40 riser pipe. Joints are threaded with o-ring seals.
								1 - 18 ft: 3/8-inch bentonite chips
15								Borehole diameter 8.5 inches
								18 - 28 ft: 3/8-inch bentonite pellets
20								
25								28 - 40 ft: Colorado silica sand 10/20 filter pack
30								29.2 - 39.2 ft: 2-inch diameter PVC screen, 0.01-inch slot size
35								
40								39.2 - 39.5 ft: 2-inch diameter pointed PVC end cap


Address: 5700 3rd Ave S
City, State: Seattle, WA
Tax Parcel ID: 172280-1495
Location (TRS): T24N R4W S20; NE1/4 of SW1/4
Lat/Long: N 204754.04 ft, E 1270621.17 ft
Consulting Firm: Pacific Groundwater Group
Logged by: G. Mutti

Drilling Firm: Environmental West
Drilling Method: Sonic
Ecology ID: BAS400
DTW: 6.38 ft bmp 2/1/2008
MP Elevation: 15.06 ft
V. Datum: NAVD 88
Date: 4/14/2009

Figure
Boring Log and As-Built
BDC-3-40

Blaser Die Casting
Remedial Investigation
JK0504.03

PgG

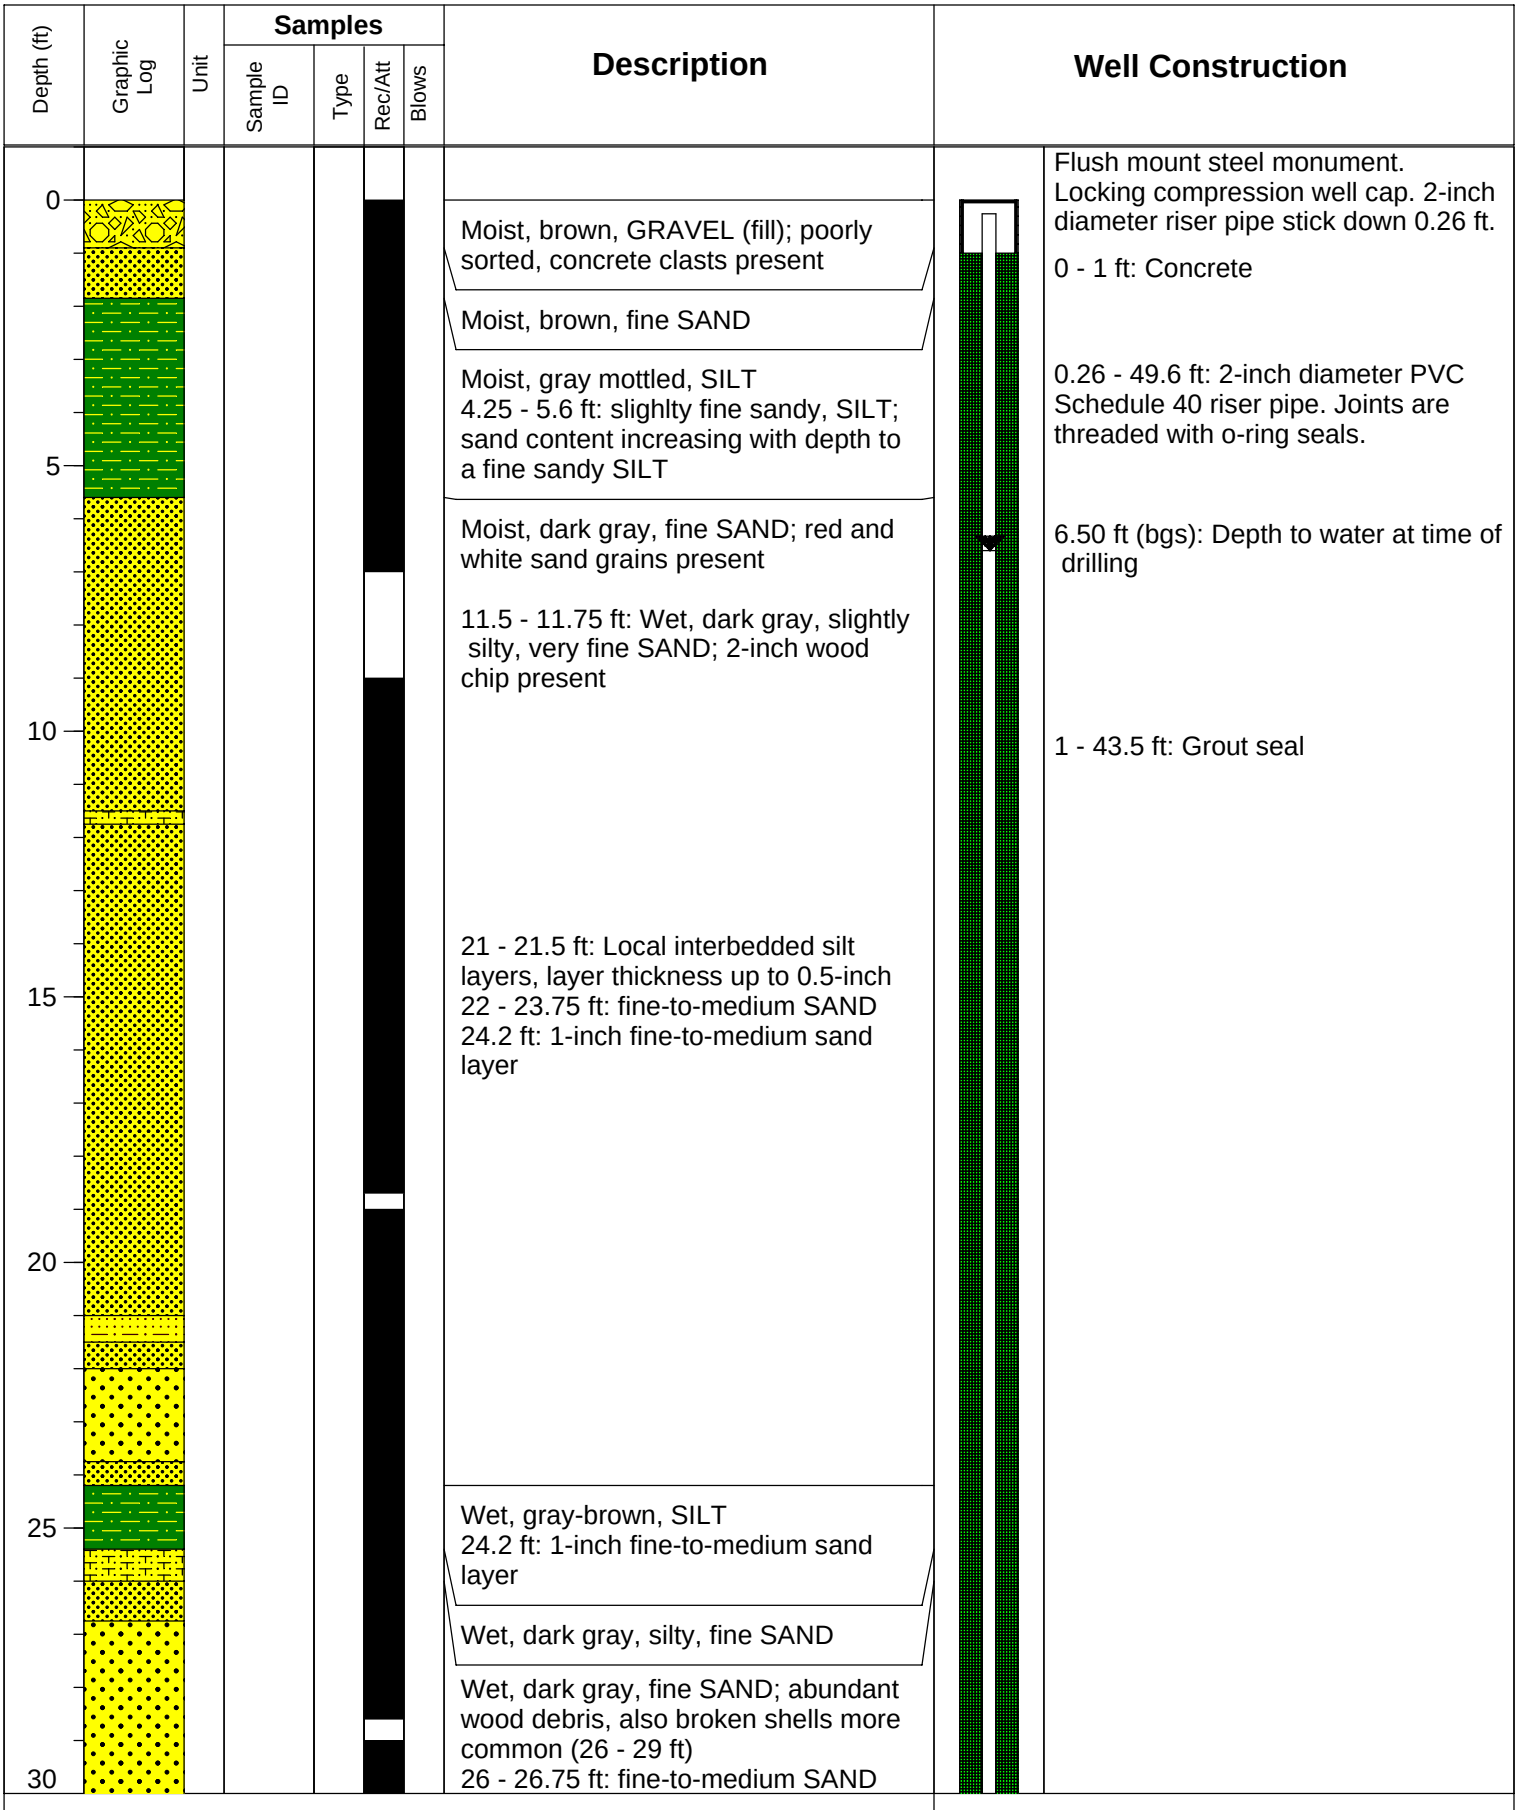


Address: 5700 3rd Ave S
City, State: Seattle, WA
Tax Parcel ID: 172280-1495
Location (TRS): T24N R4W S20; NE1/4 of SW1/4
Lat/Long: N 204760.84 ft, E 1270620.44 ft
Consulting Firm: Pacific Groundwater Group
Logged by: G. Mutti

Drilling Firm: Environmental West
Drilling Method: Sonic
Ecology ID: BAS399
DTW: 6.45 ft bmp 2/1/2008
MP Elevation: 15.14 ft
V. Datum: NAVD 88
Date: 4/13/2009

Figure
Boring Log and As-Built
BDC-3-60

Blaser Die Casting
Remedial Investigation
JK0504.03

PgG

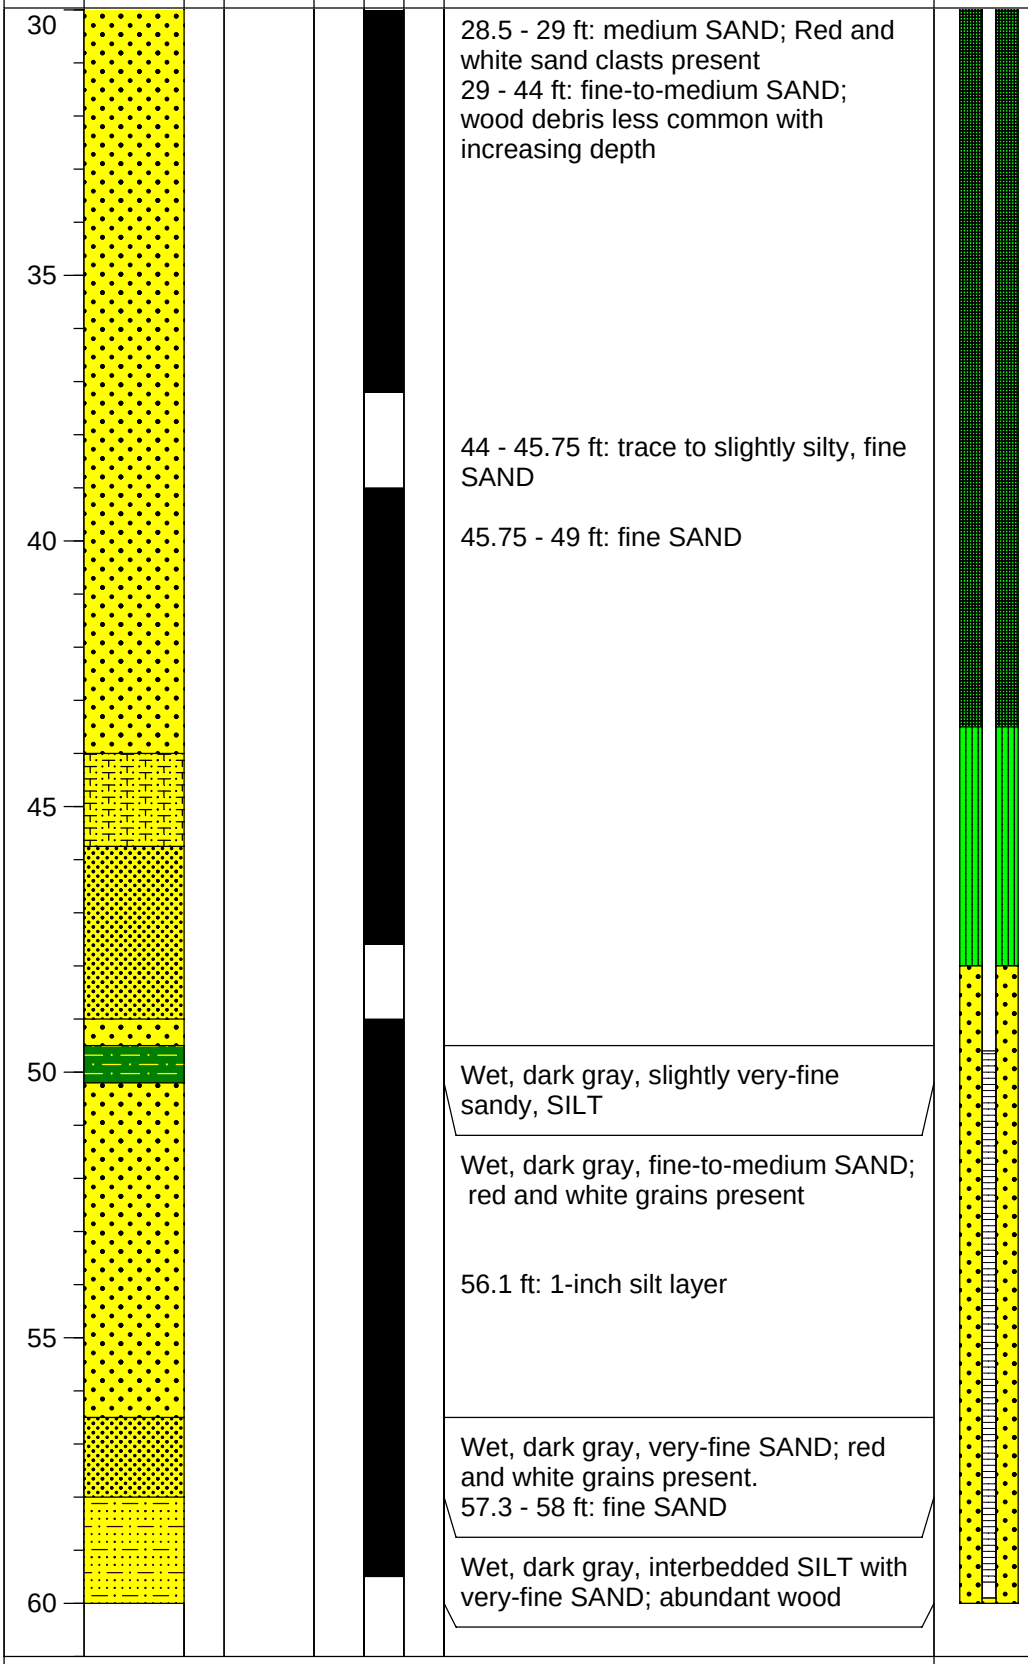

Address: 5700 3rd Ave S
City, State: Seattle, WA
Tax Parcel ID: 172280-1495
Location (TRS): T24N R4W S20; NE1/4 of SW1/4
Lat/Long: N 204760.84 ft, E 1270620.44 ft
Consulting Firm: Pacific Groundwater Group
Logged by: G. Mutti


Drilling Firm: Environmental West
Drilling Method: Sonic
Ecology ID: BAS399
DTW: 6.45 ft bmp 2/1/2008
MP Elevation: 15.14 ft
V. Datum: NAVD 88
Date: 4/13/2009

Figure
Boring Log and As-Built
BDC-3-60

Blaser Die Casting
Remedial Investigation
JK0504.03

PgG

Depth (ft)	Graphic Log	Unit	Samples: Sample ID	Samples: Type	Samples: Rec/Att	Samples: Blows	Description	Well Construction
0								Flush grade steel monument. Locking compression well cap. 2-inch diameter riser pipe.
							Brown, silty SAND	0 - 1.5 ft: Concrete seal
								0.25 to 6 ft: 2-inch diameter PVC Schedule 40 riser pipe. Joints are threaded with o-ring seals.
5							Moist to saturated, gray, silty SAND	1.5 - 5 ft: 3/8-inch bentonite chips
								5 - 16 ft: 10/20 Colorado silica sand
10								Borehole diameter 8.5 inches
								6 - 16 ft: 2-inch diameter PVC screen, 0.01-inch slot size
15								16 ft: 2-inch diameter PVC end cap
20								
25								
30								




Address: 5700 3rd Ave S
City, State: Seattle, WA
Tax Parcel ID: 172280-1495
Location (TRS): T24N R4W S20; NE1/4 of SW1/4
Lat/Long: N 204879.02 ft, E 1270776.02 ft
Consulting Firm: Pacific Groundwater Group
Logged by: G. Wallace

Drilling Firm: ESN NW
Drilling Method: HSA
Ecology ID: APJ818
DTW: 8.50 ft bmp 2/1/2008
MP Elevation: 15.29 ft
V. Datum: NAVD 88
Date: 1/3/2008

Figure
Boring Log and As-Built
BDC-4-WT

Blaser Die Casting
Remedial Investigation
JK0504.03

PgG

Depth (ft)	Graphic Log	Unit	Samples: Sample ID	Samples: Type	Samples: Rec/Att	Samples: Blows	Description	Well Construction
0							Moist to saturated, brown, silty SAND	 Flush grade steel monument. Locking compression well cap. 2-inch diameter riser pipe. 0 - 1.5 ft: Concrete seal 0.25 to 9 ft: 2-inch diameter PVC Schedule 40 riser pipe. Joints are threaded with o-ring seals. 1.5 - 7 ft: 3/8-inch bentonite chips 7 - 19 ft: 10/20 Colorado silica sand Borehole diameter 8.5 inches 9 - 19 ft: 2-inch diameter PVC screen, 0.01-inch slot size 19ft: 2-inch diameter PVC end cap
5								
10								
15								
20								
25								
30								

Address: 202-228 S Mead St
City, State: Seattle, WA
Tax Parcel ID: 172280-1750
Location (TRS): T24N R4W S20; NE1/4 of SW1/4
Lat/Long: N 204650.84 ft, E 1270453.01 ft
Consulting Firm: Pacific Groundwater Group
Logged by: G. Wallace


Drilling Firm: ESN NW
Drilling Method: HSA
Ecology ID: APJ819
DTW: 9.47 ft bmp 2/1/2008
MP Elevation: 18.25 ft
V. Datum: NAVD 88
Date: 1/4/2008

Figure
Boring Log and As-Built
BDC-6-WT

Blaser Die Casting
Remedial Investigation
JK0504.03

PgG

Depth (ft)	Graphic Log	Unit	Samples: Sample ID	Samples: Type	Samples: Rec/Att	Samples: Blows	Description	Well Construction
0							Moist, brown, silty SAND	Flush grade steel monument. Locking compression well cap. 2-inch diameter riser pipe.
								0 - 1.5 ft: Concrete seal
5							Saturated, gray, silty SAND	0.25 to 19 ft: 2-inch diameter PVC Schedule 40 riser pipe. Joints are threaded with o-ring seals.
								Borehole diameter 8.5 inches
10								1.5 - 17 ft: 3/8-inch bentonite chips
15								17 - 29 ft: 10/20 Colorado silica sand
20								19 - 29 ft: 2-inch diameter PVC screen, 0.01-inch slot size
25								29 ft: 2-inch diameter PVC end cap
30								



Address: 202-228 S Mead St
City, State: Seattle, WA
Tax Parcel ID: 172280-1750
Location (TRS): T24N R4W S20; NE1/4 of SW1/4
Lat/Long: N 204651.40 ft, E 1270450.77 ft
Consulting Firm: Pacific Groundwater Group
Logged by: G. Wallace

Drilling Firm: ESN NW
Drilling Method: HSA
Ecology ID: APJ820
DTW: 9.41 ft bmp 2/1/2008
MP Elevation: 18.25 ft
V. Datum: NAVD 88
Date: 1/4/2008


Figure
Boring Log and As-Built
BDC-6-30

Blaser Die Casting
Remedial Investigation
JK0504.03

PgG

[This Page Intentionally Left Blank]

Depth (ft)	Graphic Log	Unit	Samples: Sample ID	Samples: Type	Samples: Rec/Att	Samples: Blows	Description	Well Construction
0								Flush mount steel monument. Locking compression well cap. 2-inch diameter riser pipe stick down 0.62 ft.
								0 - 2 ft: Concrete seal
5								0.62 - 48.4 ft: 2-inch diameter PVC Schedule 40 riser pipe. Joints are threaded with o-ring seals.
10								10.69 ft (bgs): Depth to water at time of drilling
15								
20								2 - 47 ft: 3/8-inch bentonite chips
25								
30								



Address: 202-228 S Mead St
City, State: Seattle, WA
Tax Parcel ID: 172280-1750
Location (TRS): T24N R4W S20; NE1/4 of SW1/4
Lat/Long: N 204650.36 ft, E 1270458.37 ft
Consulting Firm: Pacific Groundwater Group
Logged by: G. Mutti


Drilling Firm: Cascade Drilling, Inc.
Drilling Method: HSA, wood plug
Ecology ID: BBL856
DTW: 9.81 ft bmp 6/2/2009
MP Elevation: 18.20 ft
V. Datum: NAVD 88
Date: 4/28/2009

Figure
Boring Log and As-Built
BDC-6-60

Blaser Die Casting
Remedial Investigation
JK0504.03

PgG

Depth (ft)	Graphic Log	Unit	Samples: Sample ID	Samples: Type	Samples: Rec/Att	Samples: Blows	Description
30							
35							
40							
45							
50						50	52.5 ft: no recovery
55						75	55ft: Wet, gray, silty fine SAND
60						50	57.5 ft: Wet, dark gray, fine SAND; trace very fine sand



Well Construction

Borehole diameter 8.5 inches

47 - 60 ft: Monterey Beach sand 2/12 filter pack

48.4 - 58.4 ft: 2-inch diameter PVC screen, 0.01-inch slot size

58.4 - 58.7 ft: 2-inch diameter PVC end cap

Address: 202-228 S Mead St
City, State: Seattle, WA
Tax Parcel ID: 172280-1750
Location (TRS): T24N R4W S20; NE1/4 of SW1/4
Lat/Long: N 204650.36 ft, E 1270458.37 ft
Consulting Firm: Pacific Groundwater Group
Logged by: G. Mutti


Drilling Firm: Cascade Drilling, Inc.
Drilling Method: HSA, wood plug
Ecology ID: BBL856
DTW: 9.81 ft bmp 6/2/2009
MP Elevation: 18.20 ft
V. Datum: NAVD 88
Date: 4/28/2009

Figure
Boring Log and As-Built
BDC-6-60

Blaser Die Casting
Remedial Investigation
JK0504.03

PgG

Depth (ft)	Graphic Log	Unit	Samples: Sample ID	Samples: Type	Samples: Rec/Att	Samples: Blows	Description	Well Construction
0								Flush mount steel monument. Locking compression well cap. 2-inch diameter riser pipe stick down 0.23 ft.
								0 - 1.5 ft: Concrete seal
5								0.23 - 29.9 ft: 2-inch diameter PVC Schedule 40 riser pipe. Joints are threaded with o-ring seals.
								9.32 ft (bgs): Depth to water at time of drilling
10								
15								1.5 - 28 ft: 3/8-inch bentonite chips
								18 - 28 ft: 3/8-inch bentonite pellets
20								Borehole diameter 8.5 inches
25								
30							36.5 ft: Split spoon sample not collected due to low overhead power lines. Sediments observed on the bottom-most auger flight were wet, gray, fine SAND with organics and silt stringers present.	28 - 41.5 ft: Monterey Beach sand 2/12 filter pack
								29.9 - 39.9 ft: 2-inch diameter PVC screen, 0.01-inch slot size
35								
40								39.9 - 40.2 ft: 2-inch diameter PVC end cap



Address: 5700 3rd Ave S
City, State: Seattle, WA
Tax Parcel ID: 172280-1495
Location (TRS): T24N R4W S20; NE1/4 of SW1/4
Lat/Long: N 204875.35 ft, E 1270880.47 ft
Consulting Firm: Pacific Groundwater Group
Logged by: G. Mutti

Drilling Firm: Cascade Drilling Inc.
Drilling Method: HSA, wood plug
Ecology ID: BBL861
DTW: 9.18 ft bmp 6/2/2009
MP Elevation: 18.19 ft
V. Datum: NAVD 88
Date: 4/30/2009


Figure
Boring Log and As-Built
BDC-10-40

Blaser Die Casting
Remedial Investigation
JK0504.03

PgG

[This Page Intentionally Left Blank]

Depth (ft)	Graphic Log	Unit	Samples: Sample ID	Samples: Type	Samples: Rec/Att	Samples: Blows	Description	Well Construction
0								Flush mount steel monument. Locking compression well cap. 2-inch diameter riser pipe stick down 0.27 ft.
							Not logged due to sand heave	0 - 3 ft: Concrete seal
5								0.27 - 49.7 ft: 2-inch diameter PVC Schedule 40 riser pipe. Joints are threaded with o-ring seals.
								9.35 ft (bgs): Depth to water at time of drilling
10								
15								
								18 - 28 ft: 3/8-inch bentonite pellets
20								
25								2 - 47 ft: 3/8-inch bentonite chips
30								



Address: 5700 3rd Ave S
City, State: Seattle, WA
Tax Parcel ID: 172280-1495
Location (TRS): T24N R4W S20; NE1/4 of SW1/4
Lat/Long: N 204875.27 ft, E 1270886.10 ft
Consulting Firm: Pacific Groundwater Group
Logged by: G. Mutti


Drilling Firm: Cascade Drilling Inc.
Drilling Method: HSA, wood plug
Ecology ID: BBL860
DTW: 9.16 ft bmp 6/2/2009
MP Elevation: 18.24 ft
V. Datum: NAVD 88
Date: 4/30/2009

Figure
Boring Log and As-Built
BDC-10-60

Blaser Die Casting
Remedial Investigation
JK0504.03

PgG

Depth (ft)	Graphic Log	Unit	Samples: Sample ID	Samples: Type	Samples: Rec/Att	Samples: Blows	Description	Well Construction
35								Borehole diameter 8.5 inches
40								
45								
50								47 - 55 ft: Monterey Beach sand 2/12 filter pack 49.7 - 59.7 ft: 2-inch diameter PVC screen, 0.01-inch slot size
55								55 - 60 ft: Filter pack is natural formation (fine sand). After removal of the wood stopper, sand heave filled the auger casing approximately 5 feet. PVC casing was pushed into the liquifed sand for proper depth completion.
60								59.7 - 60 ft: 2-inch diameter PVC end cap



Address: 5700 3rd Ave S
City, State: Seattle, WA
Tax Parcel ID: 172280-1495
Location (TRS): T24N R4W S20; NE1/4 of SW1/4
Lat/Long: N 204875.27 ft, E 1270886.10 ft
Consulting Firm: Pacific Groundwater Group
Logged by: G. Mutti

Drilling Firm: Cascade Drilling Inc.
Drilling Method: HSA, wood plug
Ecology ID: BBL860
DTW: 9.16 ft bmp 6/2/2009
MP Elevation: 18.24 ft
V. Datum: NAVD 88
Date: 4/30/2009

Figure
Boring Log and As-Built
BDC-10-60

Blaser Die Casting
Remedial Investigation
JK0504.03

PgG

Depth (ft)	Graphic Log	Unit	Samples: Sample ID	Samples: Type	Samples: Rec/Att	Samples: Blows	Description	Well Construction
0								Above ground locking steel monument, with 2.78 ft stick up. Three protective steel traffic posts. 2-inch diameter riser pipe stick up 2.61 ft.
								0 - 3 ft: Concrete seal
5								0 - 9.5 ft: 2-inch diameter PVC Schedule 40 riser pipe. Joints are threaded with o-ring seals.
								3 - 8 ft: 3/8-inch bentonite chips
10								8.88 ft (bgs): Depth to water at time of drilling
								8 - 20 ft: Monterey Beach sand 2/12 filter pack
								9.5 - 19.5 ft: 2-inch diameter PVC screen, 0.01-inch slot size
15						50	15 ft: Split-spoon sample collected; no recovery. Wet, gray, fine SAND in shoe	Borehole diameter 8.5 inches
20								19.5 - 19.8 ft: 2-inch diameter PVC end cap
25								
30								



Address: 202-228 S Mead St
City, State: Seattle, WA
Tax Parcel ID: 172280-1750
Location (TRS): T24N R4W S20; NE1/4 of SW1/4
Lat/Long: N 204646.53 ft, E 1270309.90 ft
Consulting Firm: Pacific Groundwater Group
Logged by: G. Mutti

Drilling Firm: Cascade Drilling, Inc.
Drilling Method: HSA, Wood Plug
Ecology ID: BBL859
DTW: 11.40 ft bmp 6/3/2009
MP Elevation: 19.59 ft
V. Datum: NAVD 88
Date: 4/29/2009

Figure
Boring Log and As-Built
BDC-11-WT

Blaser Die Casting
Remedial Investigation
JK0504.03

PgG

Depth (ft)	Graphic Log	Unit	Samples: Sample ID	Samples: Type	Samples: Rec/Att	Samples: Blows	Description	Well Construction
0								Above ground locking steel monument, with 2.9 ft stick up. Three protective steel traffic posts. 2-inch diameter riser pipe stick up 2.41 ft.
								0 - 3 ft: Concrete seal
5								
								8.76 ft (bgs): Depth to water at time of drilling
10								
								0 - 29 ft: 2-inch diameter PVC Schedule 40 riser pipe. Joints are threaded with o-ring seals.
15								
								3 - 28 ft: 3/8-inch bentonite chips
20								
								Borehole diameter 8.5 inches
25								
								28 - 41 ft: Monterey Beach sand 2/12 filter pack
30								29 - 39 ft: 2-inch diameter PVC screen, 0.01-inch slot size
35							35 ft: Wet, gray, fine SAND (0.8 feet recovered)	
								39 - 39.3 ft: 2-inch diameter PVC end cap
40								


Address: 202-228 S Mead St
City, State: Seattle, WA
Tax Parcel ID: 172280-1750
Location (TRS): T24N R4W S20; NE1/4 of SW1/4
Lat/Long: N 204642.57 ft, E 1270319.18 ft
Consulting Firm: Pacific Groundwater Group
Logged by: G. Mutti

Drilling Firm: Cascade Drilling, Inc.
Drilling Method: HSA, Wood Plug
Ecology ID: BBL857
DTW: 11.18 ft bmp 6/3/2009
MP Elevation: 19.37 ft
V. Datum: NAVD 88
Date: 4/28/2009

Figure
Boring Log and As-Built
BDC-11-40

Blaser Die Casting
Remedial Investigation
JK0504.03

PgG

Depth (ft)	Graphic Log	Unit	Samples: Sample ID	Samples: Type	Samples: Rec/Att	Samples: Blows	Description	Well Construction
0								
5								
10								
15								
20								
25								

Above ground locking steel monument, with 2.66 ft stick up. Three protective steel traffic posts. 2-inch diameter riser pipe stick up 2.49 ft.

0 - 3.1 ft: Concrete seal

8.56 ft (bgs): Depth to water at time of drilling

0 - 49.9 ft: 2-inch diameter PVC Schedule 40 riser pipe. Joints threaded with o-ring seals.

3.1 - 47 ft: 3/8-inch bentonite chips

Address: 202-228 S Mead St
City, State: Seattle, WA
Tax Parcel ID: 172280-1750
Location (TRS): T24N R4W S20; NE1/4 of SW1/4
Lat/Long: N 204641.88 ft, E 1270308.20 ft
Consulting Firm: Pacific Groundwater Group
Logged by: G. Mutti


Drilling Firm: Cascade Drilling, Inc.
Drilling Method: HSA, Wood Plug
Ecology ID: BBL860
DTW: 10.93 ft bmp 6/3/2009
MP Elevation: 19.10 ft
V. Datum: NAVD 88
Date: 4/29/2009

Figure
Boring Log and As-Built
BDC-11-60

Blaser Die Casting
Remedial Investigation
JK0504.03

PgG

Depth (ft)	Graphic Log	Unit	Samples: Sample ID	Samples: Type	Samples: Rec/Att	Samples: Blows	Description	Well Construction
30								
35								Borehole diameter 8.5 inches
40								
45								47 - 60 ft: Monterey Beach sand 2/12 filter pack
50								49.9 - 59.9 ft: 2-inch diameter PVC screen, 0.01-inch slot size
55						50	55 ft: Wet, dark gray, fine SAND	
60								59.9 - 60.2 ft: 2-inch diameter PVC end cap



Address: 202-228 S Mead St
City, State: Seattle, WA
Tax Parcel ID: 172280-1750
Location (TRS): T24N R4W S20; NE1/4 of SW1/4
Lat/Long: N 204641.88 ft, E 1270308.20 ft
Consulting Firm: Pacific Groundwater Group
Logged by: G. Mutti


Drilling Firm: Cascade Drilling, Inc.
Drilling Method: HSA, Wood Plug
Ecology ID: BBL860
DTW: 10.93 ft bmp 6/3/2009
MP Elevation: 19.10 ft
V. Datum: NAVD 88
Date: 4/29/2009

Figure
Boring Log and As-Built
BDC-11-60

Blaser Die Casting
Remedial Investigation
JK0504.03

PgG

Depth (ft)	Graphic Log	Unit	Samples: Sample ID	Samples: Type	Samples: Rec/Att	Samples: Blows	Description	Well Construction
0								Flush mount steel monument. Locking compression well cap. 2-inch diameter riser pipe stick down 0.52 ft.
								0 - 3 ft: Concrete seal
5								0.52 - 28.9 ft: 2-inch diameter PVC Schedule 40 riser pipe. Joints are threaded with o-ring seals.
								8.15 ft (bgs): Depth to water at time of drilling
10								
15								
20								3 - 28 ft: 3/8-inch bentonite chips
25								Borehole diameter 8.5 inches
30								28 - 40 ft: Monterey Beach sand 2/12 filter pack
								28.9 - 38.9 ft: 2-inch diameter PVC screen, 0.01-inch slot size
35								
40						12-21-26	39 ft: Wet, gray, fine to very fine, SAND	38.9 - 39.2 ft: 2-inch diameter PVC end cap



Address: 202-228 S Mead St
City, State: Seattle, WA
Tax Parcel ID: 172280-1750
Location (TRS): T24N R4W S20; NE1/4 of SW1/4
Lat/Long: N 204632.89 ft, E 1270546.66 ft
Consulting Firm: Pacific Groundwater Group
Logged by: G. Mutti

Drilling Firm: Cascade Drilling, Inc.
Drilling Method: HSA, wood plug
Ecology ID: BBL855
DTW: 7.74 ft bmp 6/3/2009
MP Elevation: 16.31 ft
V. Datum: NAVD 88
Date: 4/27/2009


Figure
Boring Log and As-Built
CI-MW-1-40

Blaser Die Casting
Remedial Investigation
JK0504.03

PgG

[This Page Intentionally Left Blank]

Depth (ft)	Graphic Log	Unit	Samples: Sample ID	Samples: Type	Samples: Rec/Att	Samples: Blows	Description	Well Construction
0								Flush mount steel monument. Locking compression well cap. 2-inch diameter riser pipe stick down 0.28 ft.
								0 - 3 ft: Concrete seal
5								0.28 - 48.5 ft: 2-inch diameter PVC Schedule 40 riser pipe. Joints are threaded with o-ring seals.
								8.00 ft (bgs): Depth to water at time of drilling
10								
15								
20								
								Borehole diameter 8.5 inches
25								
30								



Address: 202-228 S Mead St
City, State: Seattle, WA
Tax Parcel ID: 172280-1750
Location (TRS): T24N R4W S20; NE1/4 of SW1/4
Lat/Long: N 204633.03 ft, E 1270553.00 ft
Consulting Firm: Pacific Groundwater Group
Logged by: G. Mutti

Drilling Firm: Cascade Drilling, Inc.
Drilling Method: HSA, wood plug
Ecology ID: BBL854
DTW: 8.68 ft bmp 6/3/2009
MP Elevation: 16.04 ft
V. Datum: NAVD 88
Date: 4/27/2009

Figure
Boring Log and As-Built
CI-MW-1-60

Blaser Die Casting
Remedial Investigation
JK0504.03

PgG

Depth (ft)	Graphic Log	Unit	Samples: Sample ID	Samples: Type	Samples: Rec/Att	Samples: Blows	Description	Well Construction
35								3 - 48 ft: 3/8-inch bentonite chips
40								
45								
50								48 - 52.5 ft: Monterey Beach sand 2/12 filter pack 48.5 - 58.5 ft: 2-inch diameter PVC screen, 0.01-inch slot size 52.5 - 61 ft: Natural formation filter pack (fine sand) due to borehole collapse and sand heave.
55						12-50	54ft: Wet, gray, fine SAND	
60						4-21-22	59 ft: Wet, dark gray, fine SAND; trace very fine sand; bottom 0.8 ft of sample has very fine sand to silt interbeds of 1 to 4 inch thickness	58.5 - 58.8 ft: 2-inch diameter PVC end cap


Address: 202-228 S Mead St
City, State: Seattle, WA
Tax Parcel ID: 172280-1750
Location (TRS): T24N R4W S20; NE1/4 of SW1/4
Lat/Long: N 204633.03 ft, E 1270553.00 ft
Consulting Firm: Pacific Groundwater Group
Logged by: G. Mutti

Drilling Firm: Cascade Drilling, Inc.
Drilling Method: HSA, wood plug
Ecology ID: BBL854
DTW: 8.68 ft bmp 6/3/2009
MP Elevation: 16.04 ft
V. Datum: NAVD 88
Date: 4/27/2009

Figure
Boring Log and As-Built
CI-MW-1-60

Blaser Die Casting
Remedial Investigation
JK0504.03

PgG

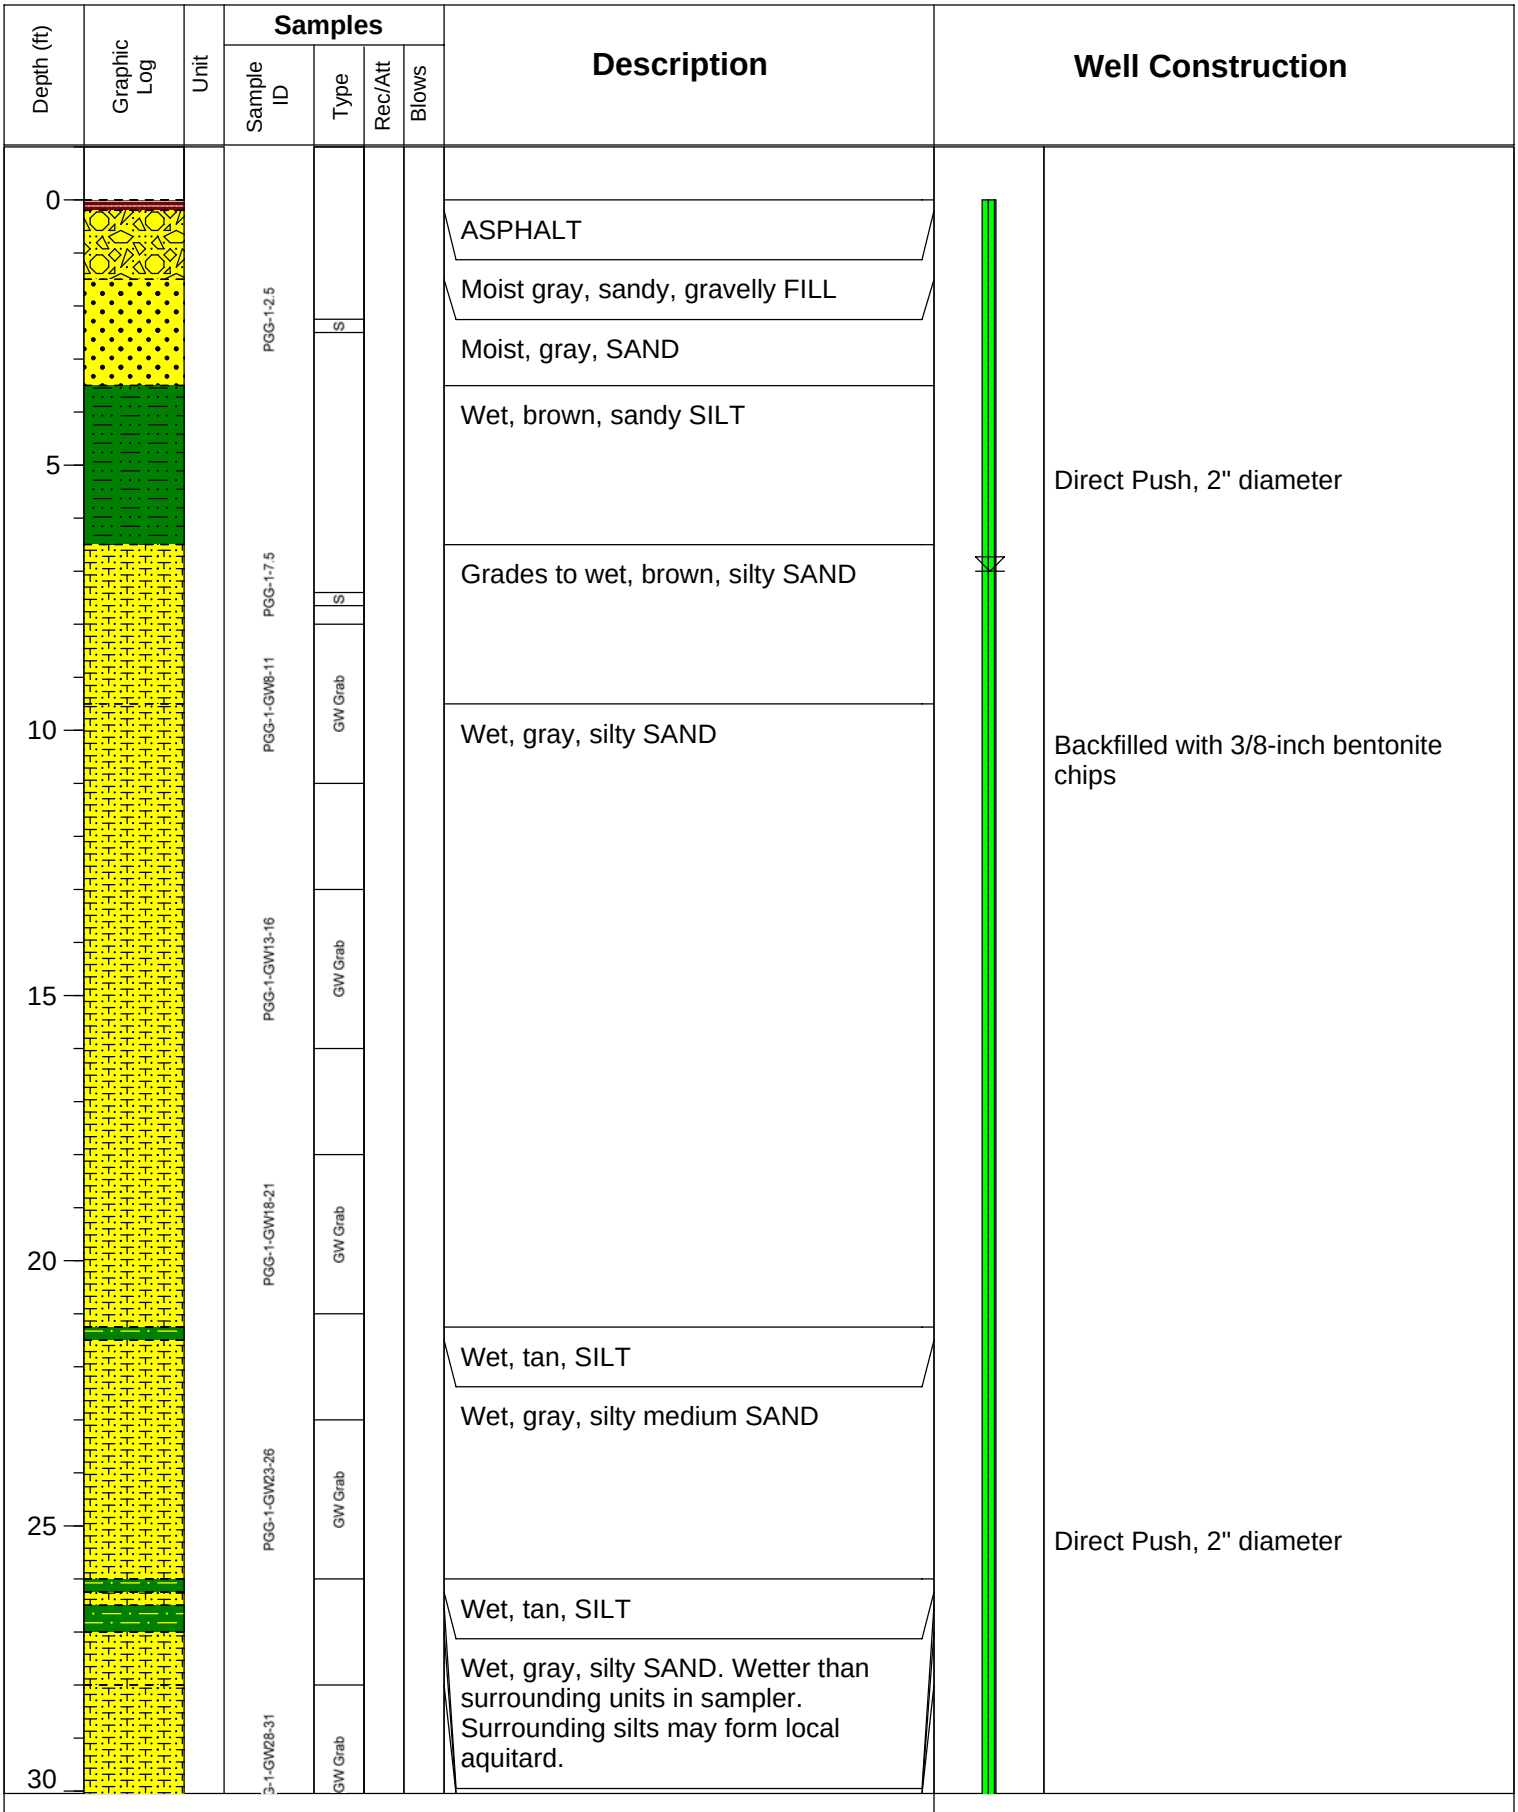

Address: 5700 3rd Ave S
City, State: Seattle, WA
Tax Parcel ID: 172280-1495
Location (TRS): T24N R4W S20; NE1/4 of SW1/4
Lat/Long: N 204767.1 ft, E 1270624 ft
Consulting Firm: Pacific Groundwater Group
Logged by: G. Wallace

Drilling Firm: ESN NW
Drilling Method: Direct Push
Ecology ID: NA
DTW: ~7 ft bmp
MP Elevation: ~13.3 ft
V. Datum: NAVD 88
Date: 9/9/2008

Figure
Boring Log
PGG-1

Blaser Die Casting
Remedial Investigation
JK0504.03

PgG

Depth (ft)	Graphic Log	Unit	Samples: Sample ID	Samples: Type	Samples: Rec/Att	Samples: Blows	Description	Well Construction
							Wet, tan, SILT	Backfilled with 3/8-inch bentonite chips
							Wet, gray, fine-medium silty SAND. Moderately sorted, slight grading to sharp contact with silt above.	
35							Wet, gray medium silty SAND. Poorly sorted, poorly graded.	
40								
45								
50								
55								
60								


Address: 5700 3rd Ave S
City, State: Seattle, WA
Tax Parcel ID: 172280-1495
Location (TRS): T24N R4W S20; NE1/4 of SW1/4
Lat/Long: N 204767.1 ft, E 1270624 ft
Consulting Firm: Pacific Groundwater Group
Logged by: G. Wallace

Drilling Firm: ESN NW
Drilling Method: Direct Push
Ecology ID: NA
DTW: ~7 ft bmp
MP Elevation: ~13.3 ft
V. Datum: NAVD 88
Date: 9/9/2008

Figure
Boring Log
PGG-1

Blaser Die Casting
Remedial Investigation
JK0504.03

PgG

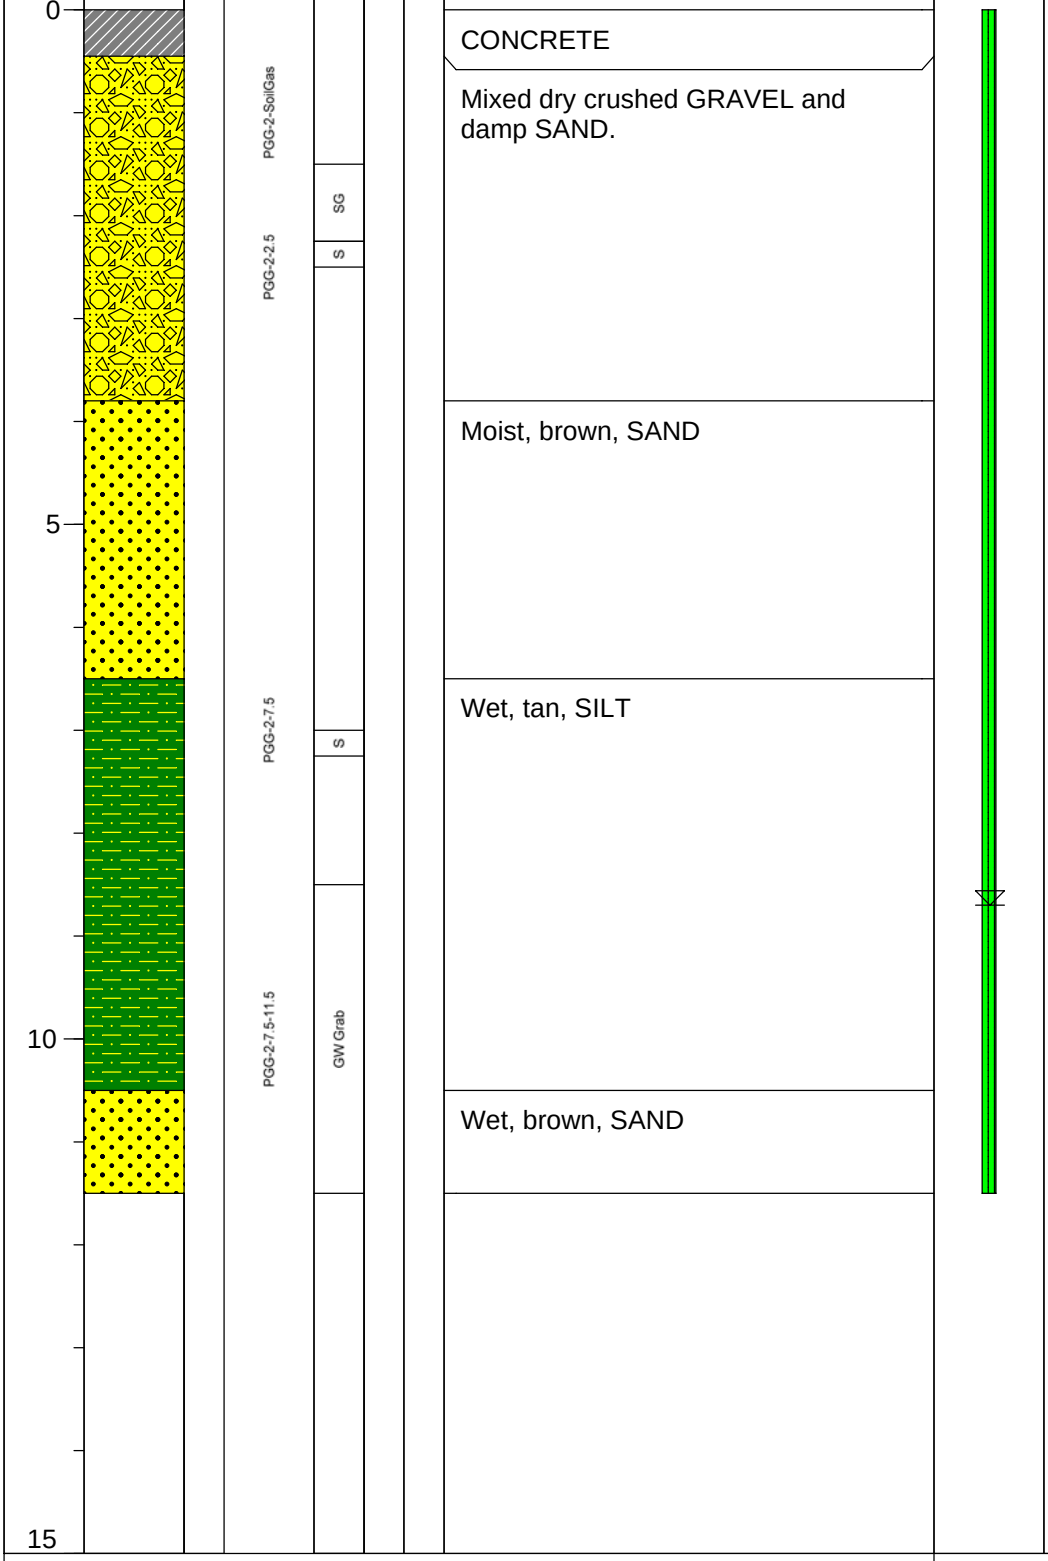


Address: 5700 3rd Ave S
City, State: Seattle, WA
Tax Parcel ID: 172280-1495
Location (TRS): T24N R4W S20; NE1/4 of SW1/4
Lat/Long: N 204783.8 ft, E 1270653 ft
Consulting Firm: Pacific Groundwater Group
Logged by: G. Wallace

Drilling Firm: ESN NW
Drilling Method: Direct Push
Ecology ID: NA
DTW: ~8.7 ft bmp
MP Elevation: ~16.8 ft
V. Datum: NAVD 88
Date: 5/2/2006

Figure
Boring Log
PGG-2

Blaser Die Casting
Remedial Investigation
JK0504.03

PGG

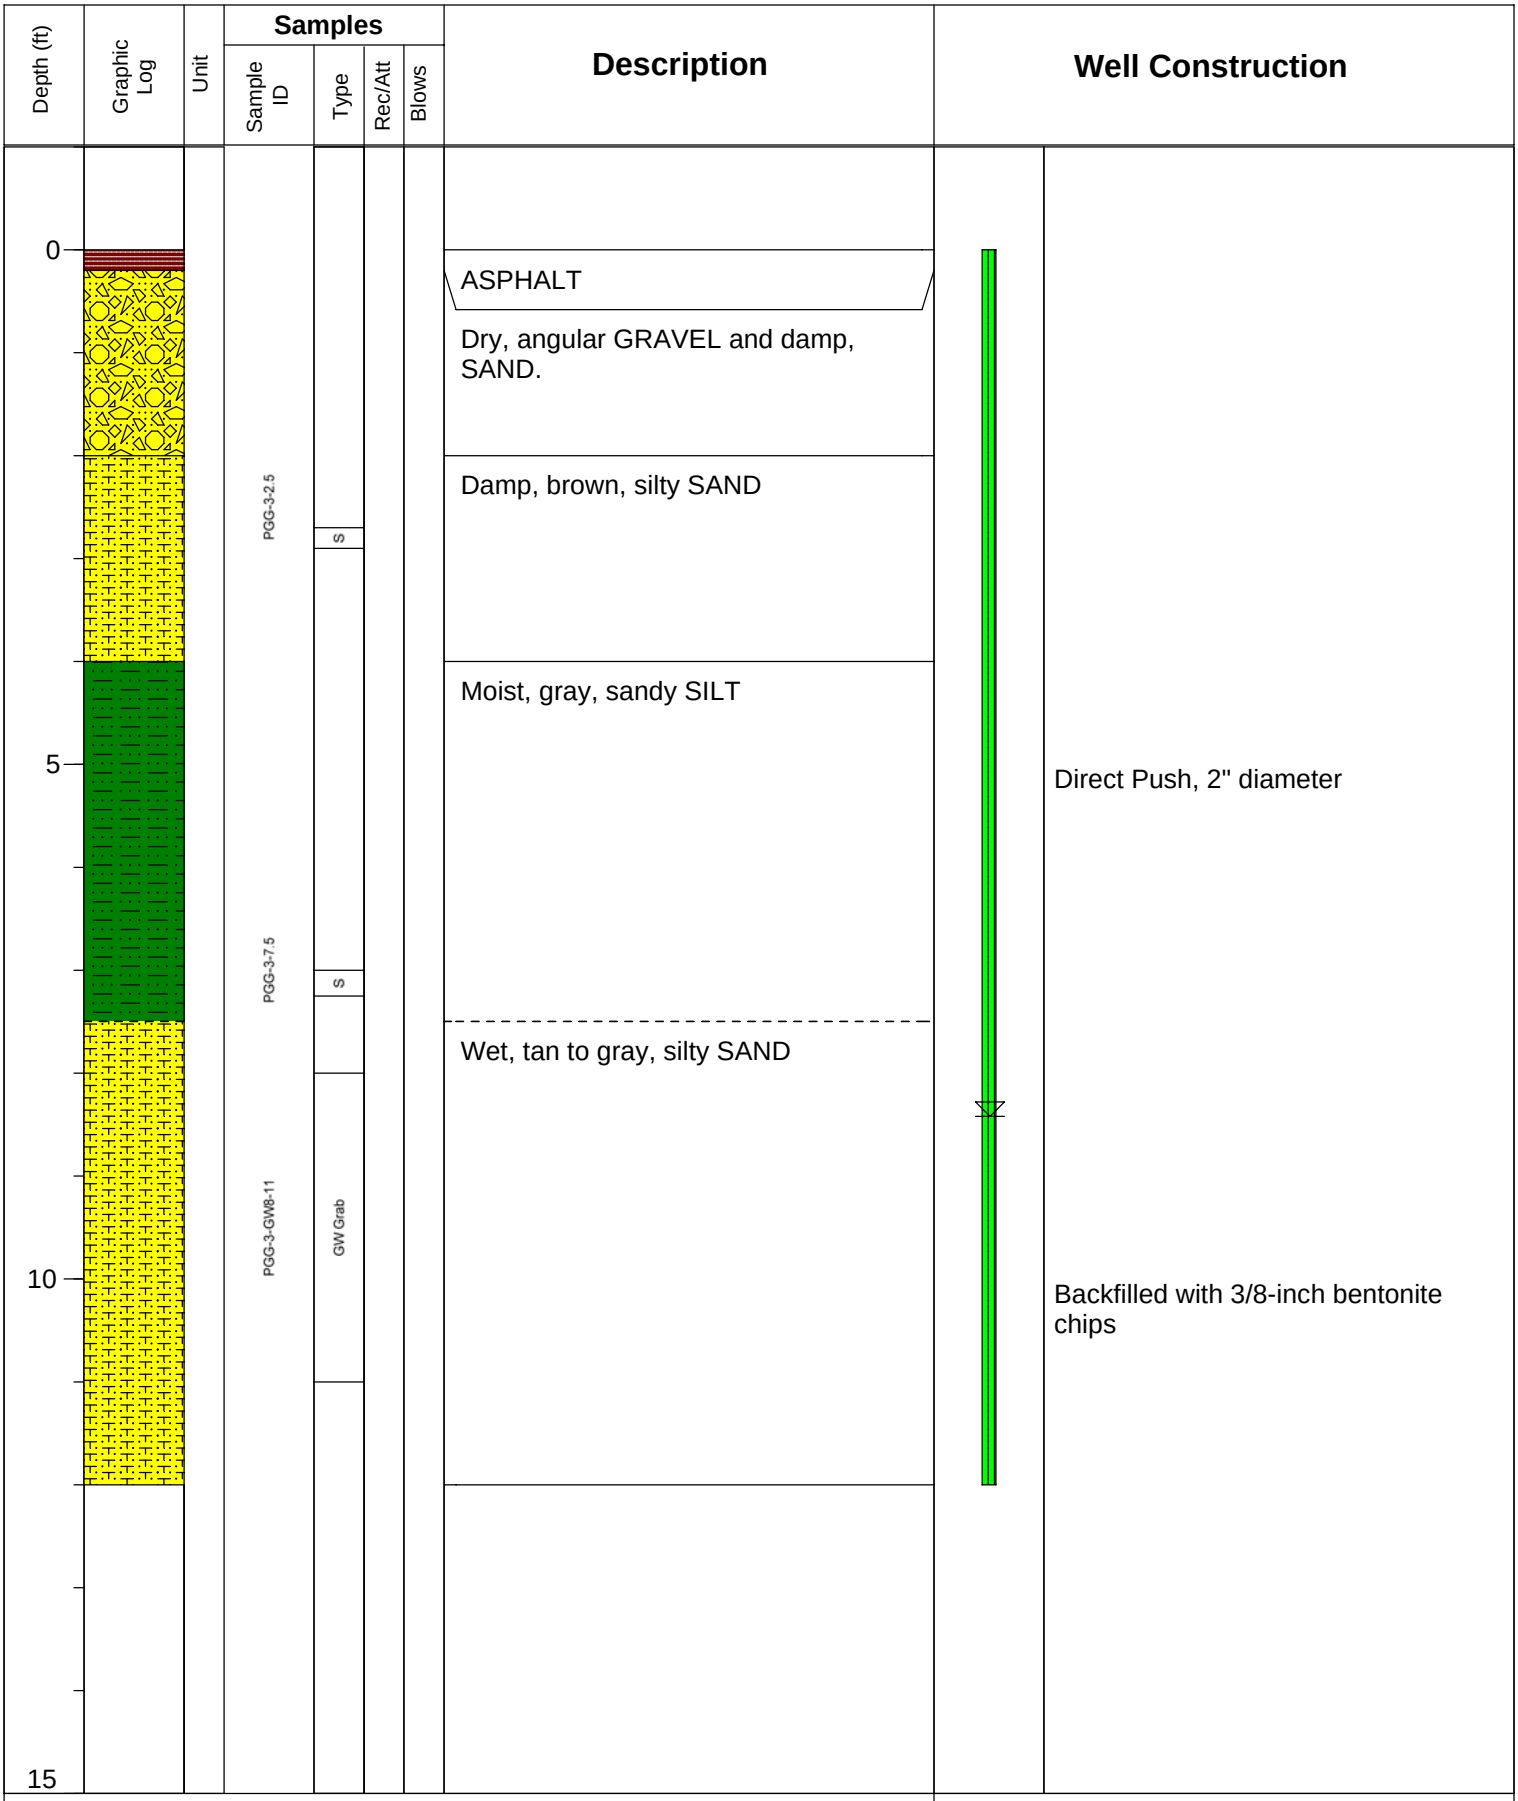


Address: 5700 3rd Ave S
City, State: Seattle, WA
Tax Parcel ID: 172280-1495
Location (TRS): T24N R4W S20; NE1/4 of SW1/4
Lat/Long: N 204822 ft, E 1270632 ft
Consulting Firm: Pacific Groundwater Group
Logged by: G. Wallace

Drilling Firm: ESN NW
Drilling Method: Direct Push
Ecology ID: NA
DTW: ~8.42 ft bmp
MP Elevation: ~14.2 ft
V. Datum: NAVD 88
Date: 5/1/2006

Figure
Boring Log
PGG-3

Blaser Die Casting
Remedial Investigation
JK0504.03

PGG

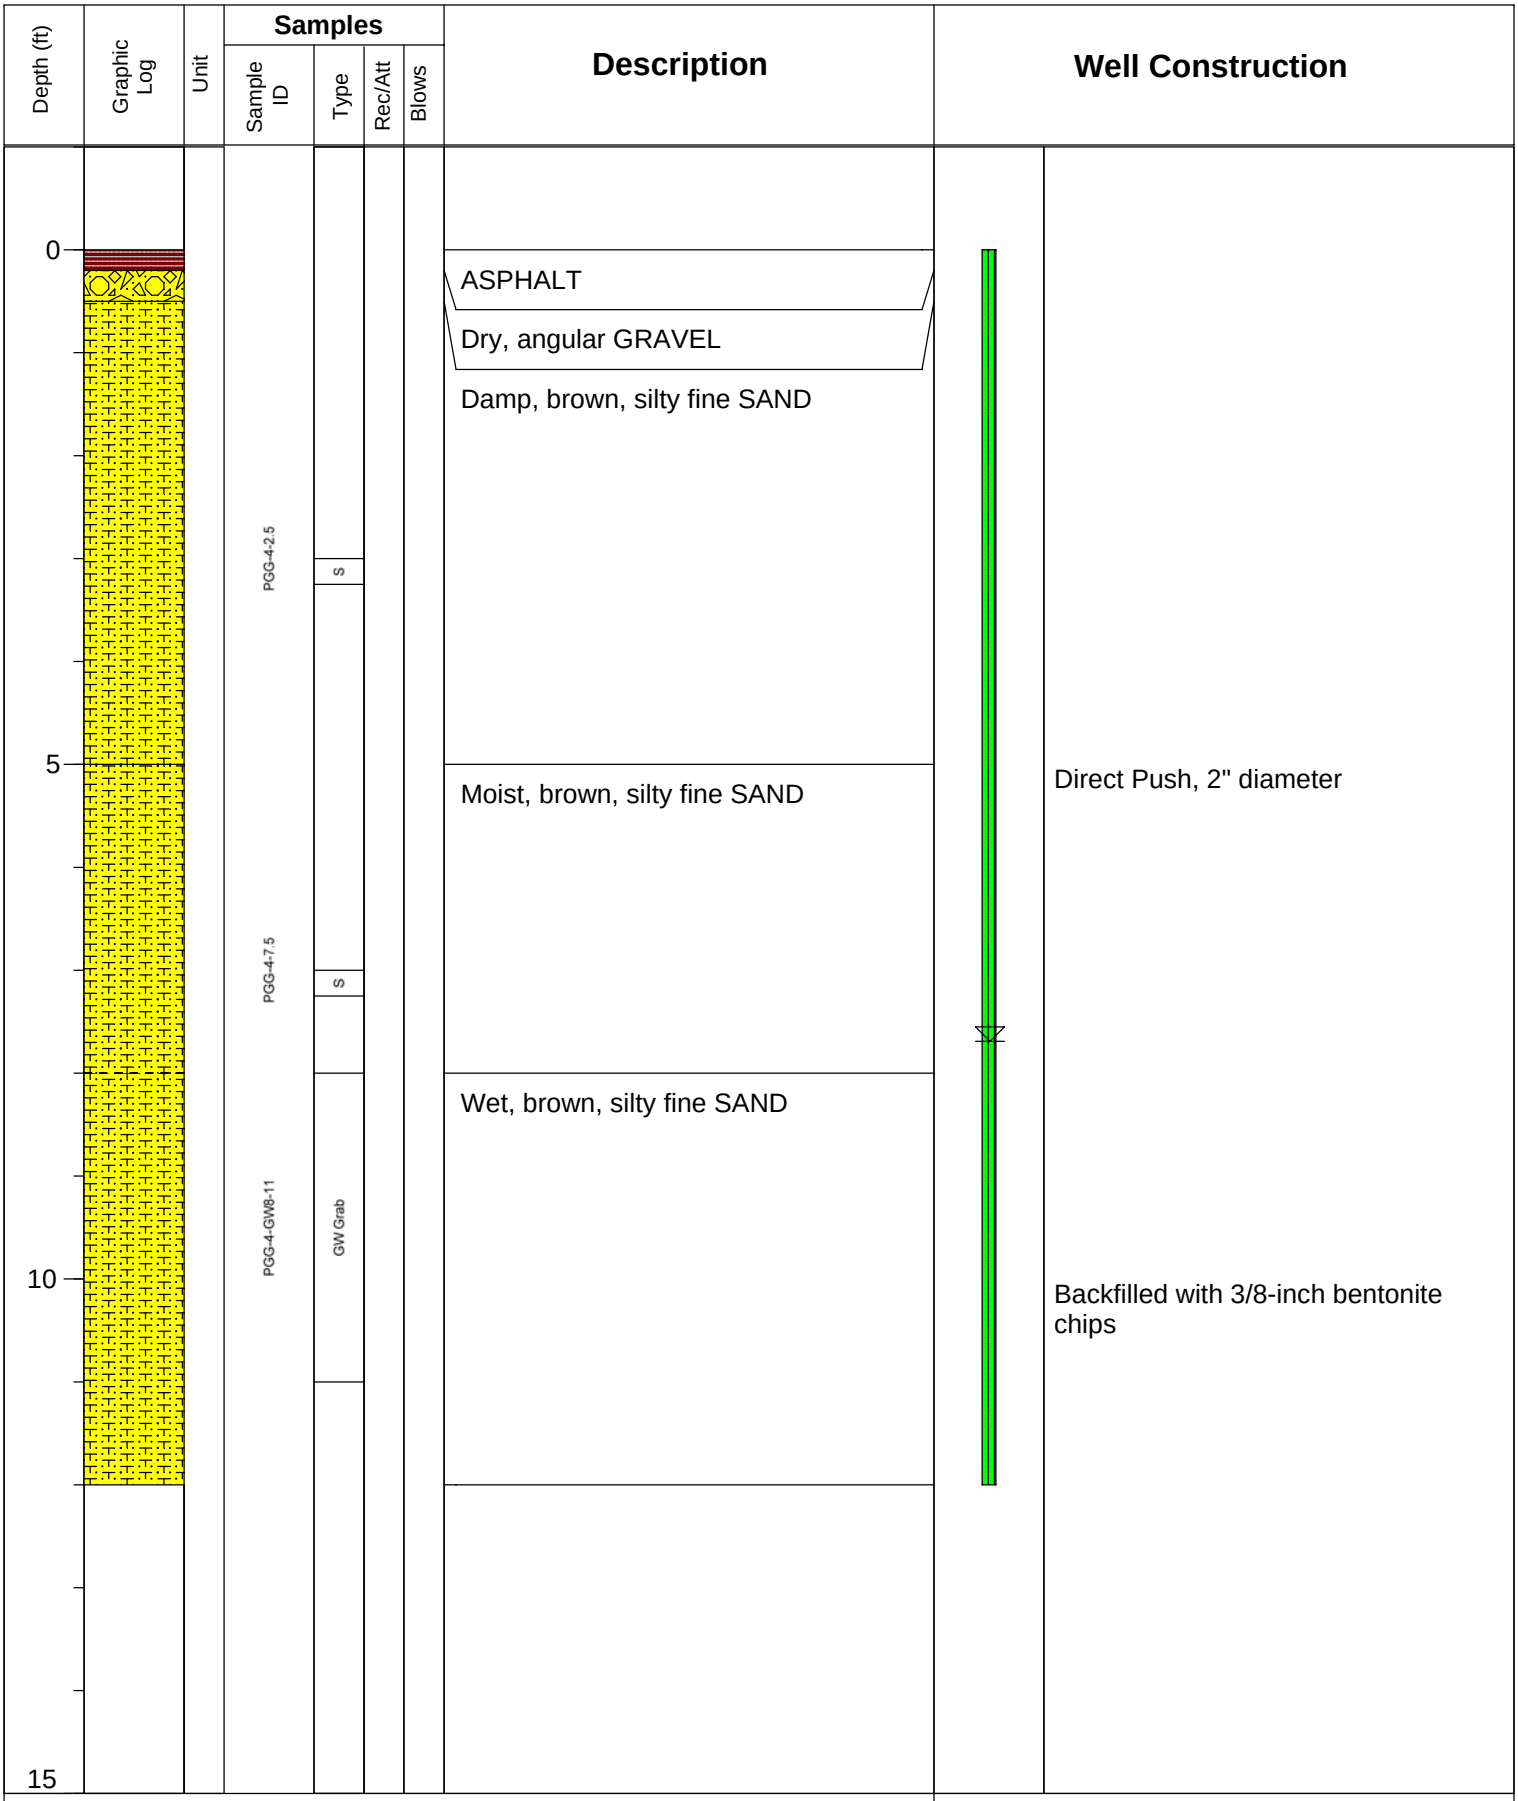

Address: 5700 3rd Ave S
City, State: Seattle, WA
Tax Parcel ID: 172280-1495
Location (TRS): T24N R4W S20; NE1/4 of SW1/4
Lat/Long: N 204804.8 ft, E 1270659 ft
Consulting Firm: Pacific Groundwater Group
Logged by: G. Wallace

Drilling Firm: ESN NW
Drilling Method: Direct Push
Ecology ID: NA
DTW: ~7.69 ft bmp
MP Elevation: ~14.8 ft
V. Datum: NAVD 88
Date: 5/1/2006

Figure
Boring Log
PGG-4

Blaser Die Casting
Remedial Investigation
JK0504.03

PGG

Depth (ft)	Graphic Log	Unit	Samples: Sample ID	Samples: Type	Samples: Rec/Att	Samples: Blows	Description	Well Construction
0							Asphalt	
							No soil samples collected.	
5								Hydropunch, 2" diameter
10			PGG-5-GW8-11	GW Grab				Backfilled with 3/8-inch bentonite chips
15								


Address: 5700 3rd Ave S
City, State: Seattle, WA
Tax Parcel ID: 172280-1495
Location (TRS): T24N R4W S20; NE1/4 of SW1/4
Lat/Long: N 204874.4 ft, E 1270630 ft
Consulting Firm: Pacific Groundwater Group
Logged by: G. Wallace

Drilling Firm: ESN NW
Drilling Method: Direct Push
Ecology ID: NA
DTW: ~7.97 ft bmp
MP Elevation: ~14.8 ft
V. Datum: NAVD 88
Date: 5/1/2006

Figure
Boring Log
PGG-5

Blaser Die Casting
Remedial Investigation
JK0504.03

PGG

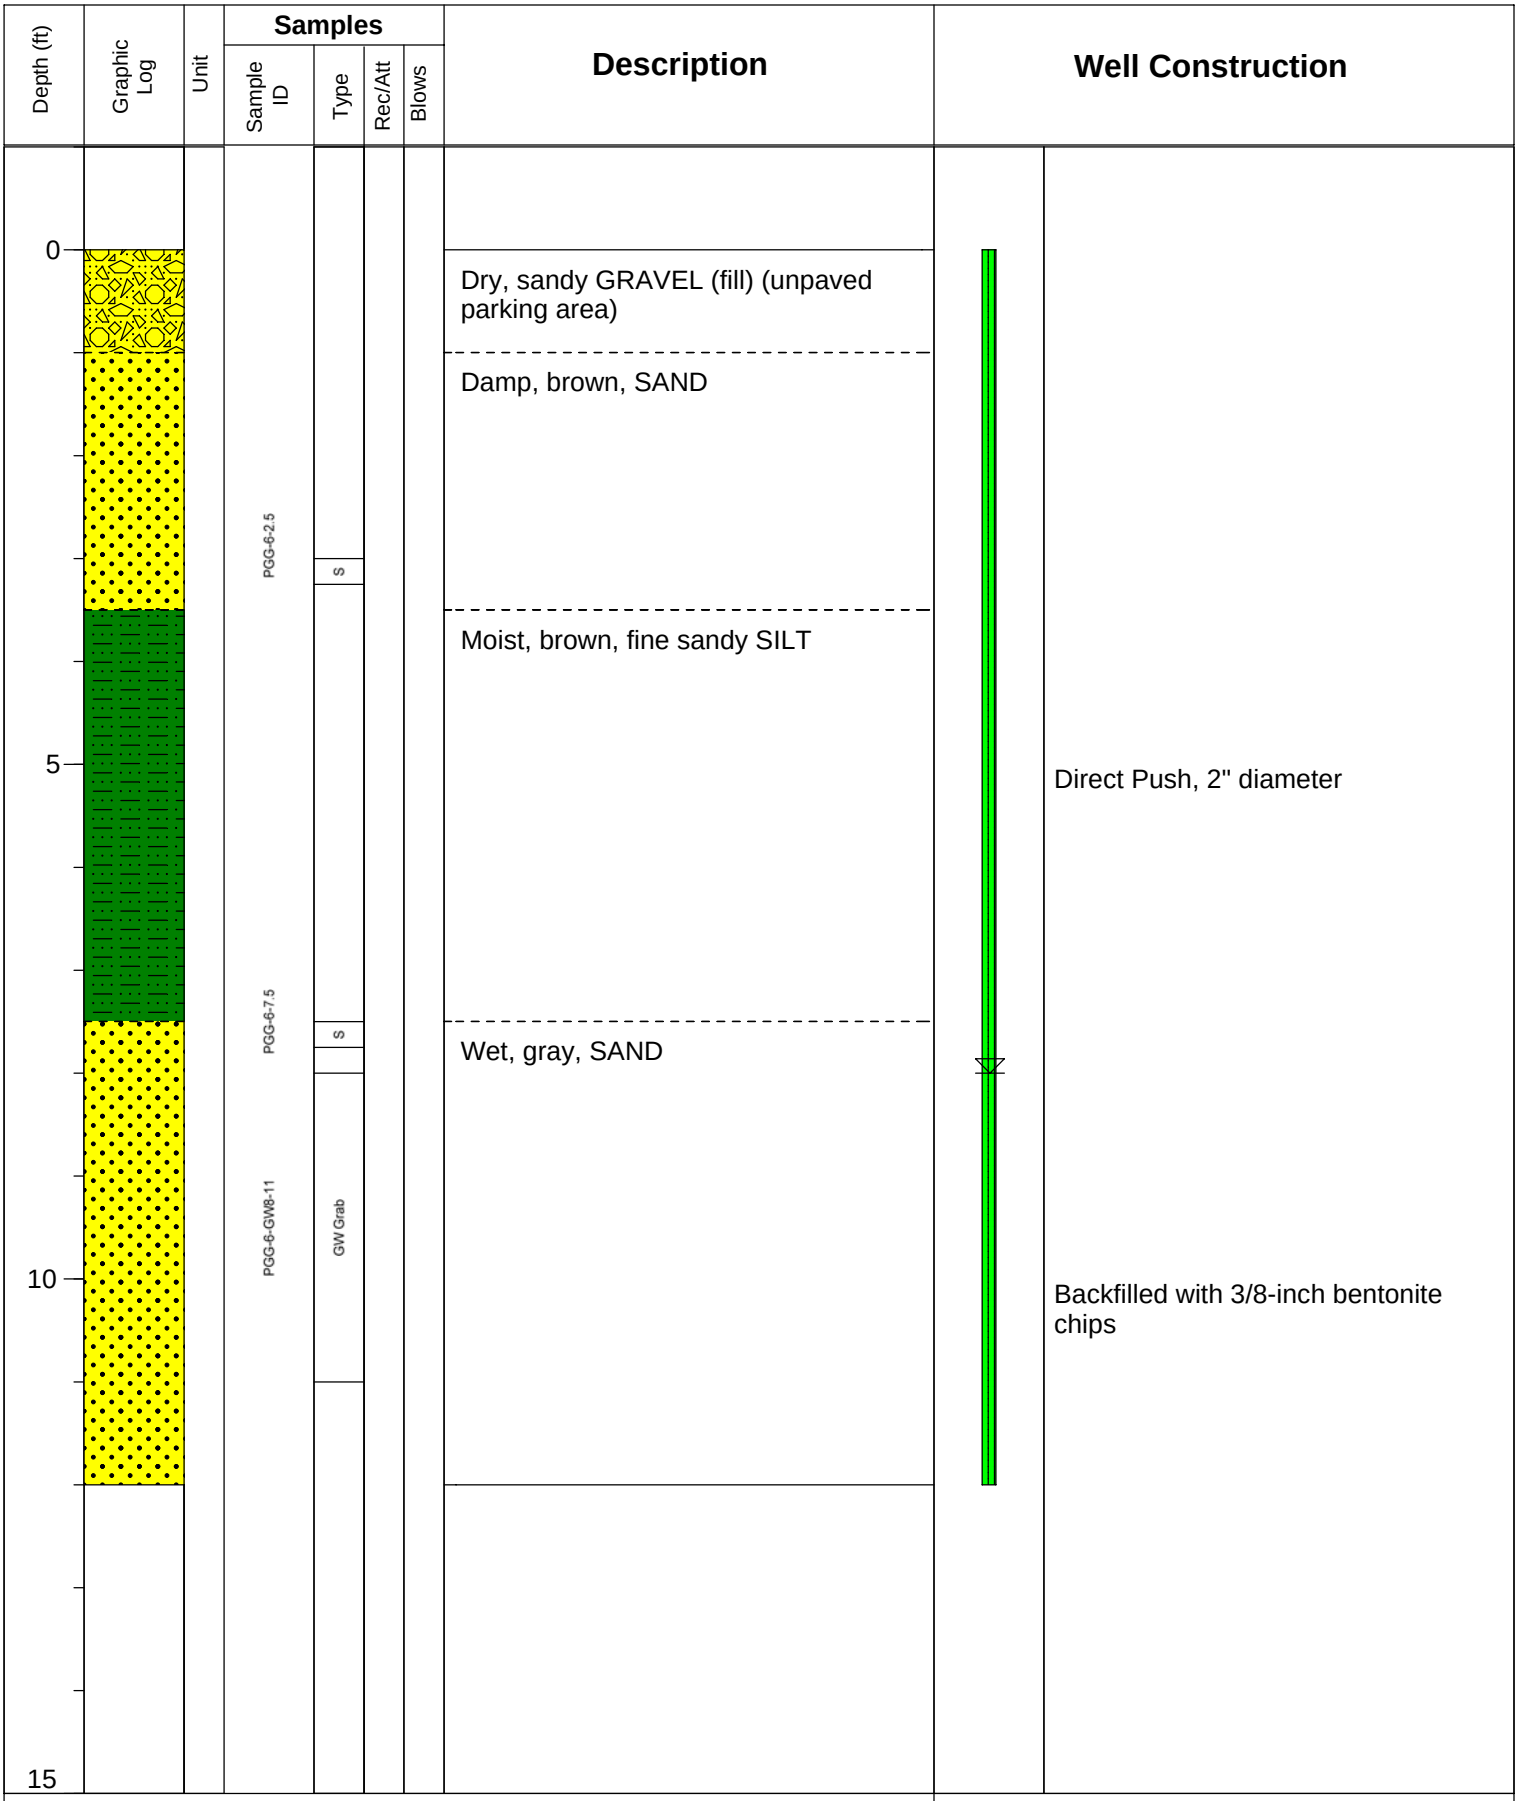


Address: 5700 3rd Ave S
City, State: Seattle, WA
Tax Parcel ID: 172280-1495
Location (TRS): T24N R4W S20; NE1/4 of SW1/4
Lat/Long: N 204795.4 ft, E 1270590 ft
Consulting Firm: Pacific Groundwater Group
Logged by: G. Wallace

Drilling Firm: ESN NW
Drilling Method: Direct Push
Ecology ID: NA
DTW: ~8 ft bmp
MP Elevation: ~13.1 ft
V. Datum: NAVD 88
Date: 5/1/2006

Figure
Boring Log
PGG-6

Blaser Die Casting
Remedial Investigation
JK0504.03

PGG

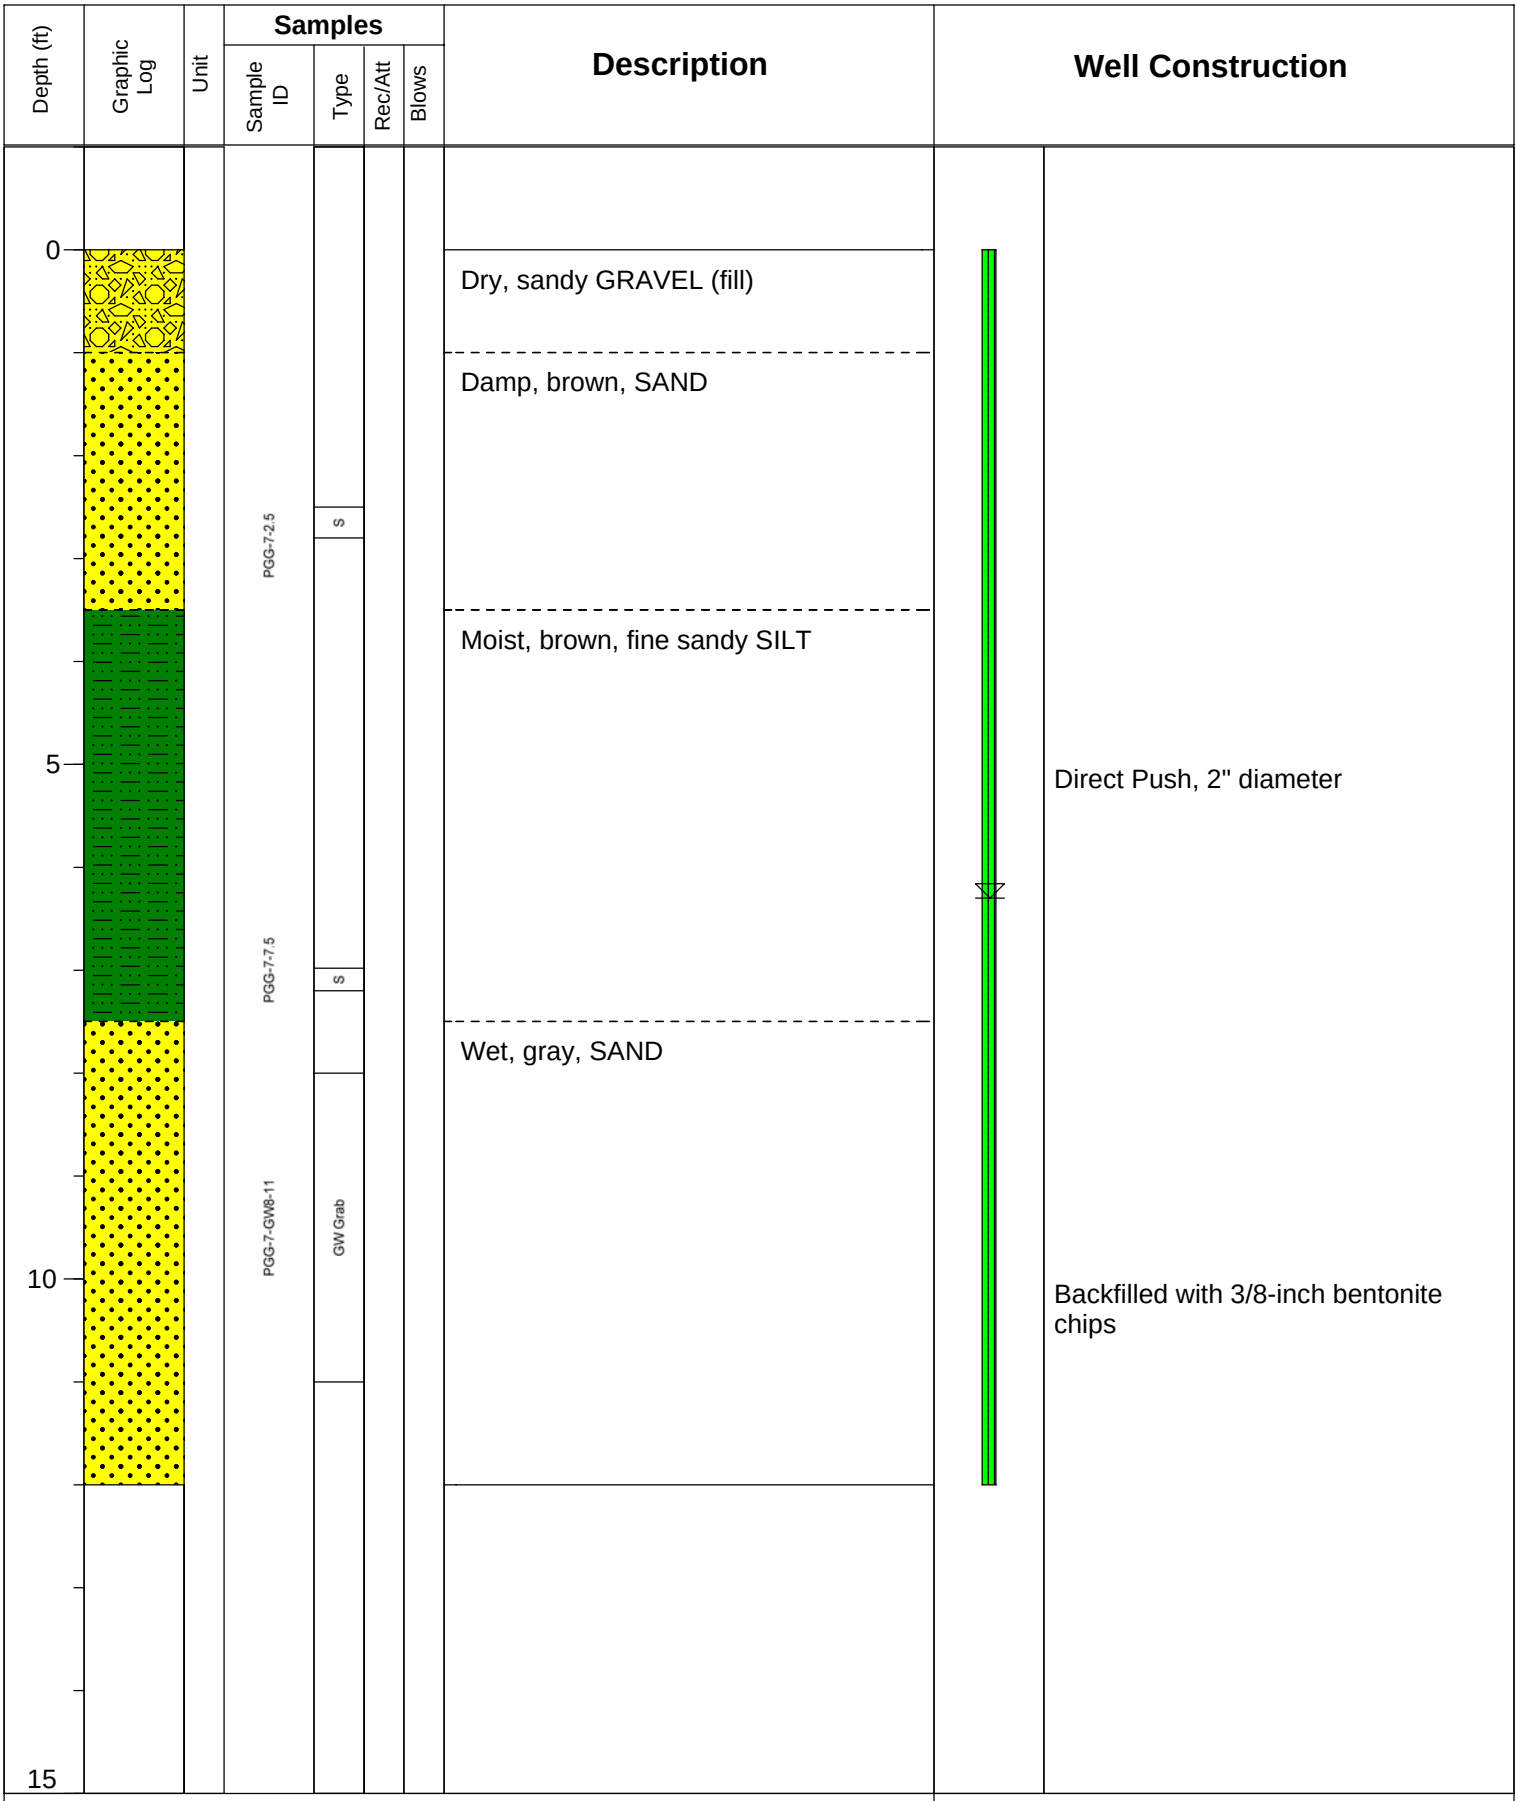


Address: 5700 3rd Ave S
City, State: Seattle, WA
Tax Parcel ID: 172280-1495
Location (TRS): T24N R4W S20; NE1/4 of SW1/4
Lat/Long: N 204785.2 ft, E 1270638 ft
Consulting Firm: Pacific Groundwater Group
Logged by: G. Wallace

Drilling Firm: ESN NW
Drilling Method: Direct Push
Ecology ID: NA
DTW: ~6.3 ft bmp
MP Elevation: ~14.6 ft
V. Datum: NAVD 88
Date: 5/1/2006

Figure
Boring Log
PGG-7

Blaser Die Casting
Remedial Investigation
JK0504.03

PgG

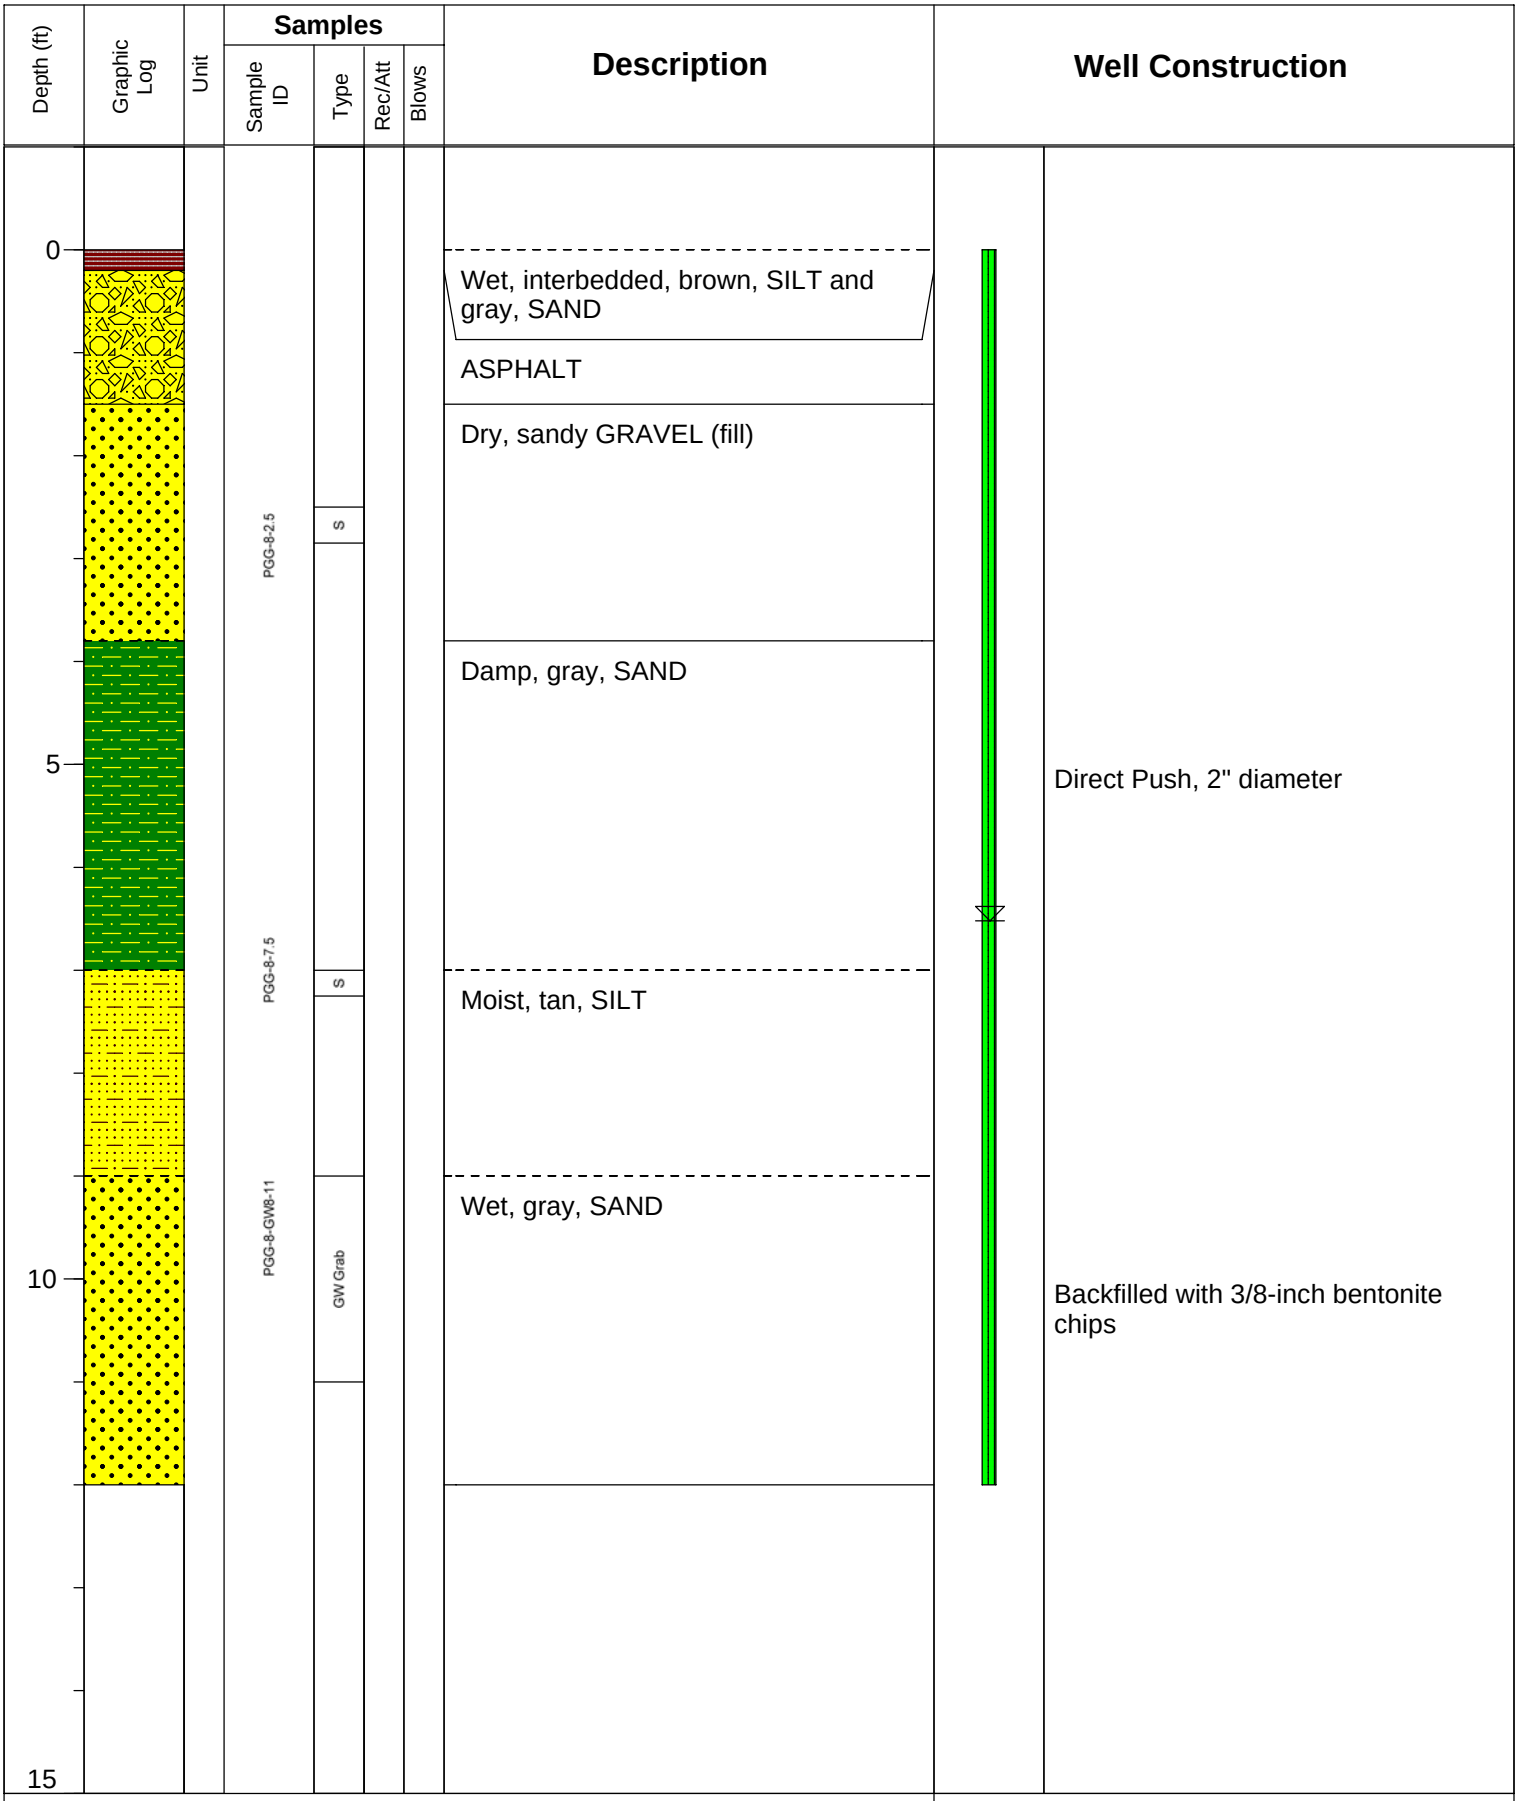


Address: 5700 3rd Ave S
City, State: Seattle, WA
Tax Parcel ID: 172280-1495
Location (TRS): T24N R4W S20; NE1/4 of SW1/4
Lat/Long: N 204779 ft, E 1270618 ft
Consulting Firm: Pacific Groundwater Group
Logged by: G. Wallace

Drilling Firm: ESN NW
Drilling Method: Direct Push
Ecology ID: NA
DTW: ~6.52 ft bmp
MP Elevation: ~13.7 ft
V. Datum: NAVD 88
Date: 5/1/2006

Figure
Boring Log
PGG-8

Blaser Die Casting
Remedial Investigation
JK0504.03

PGG

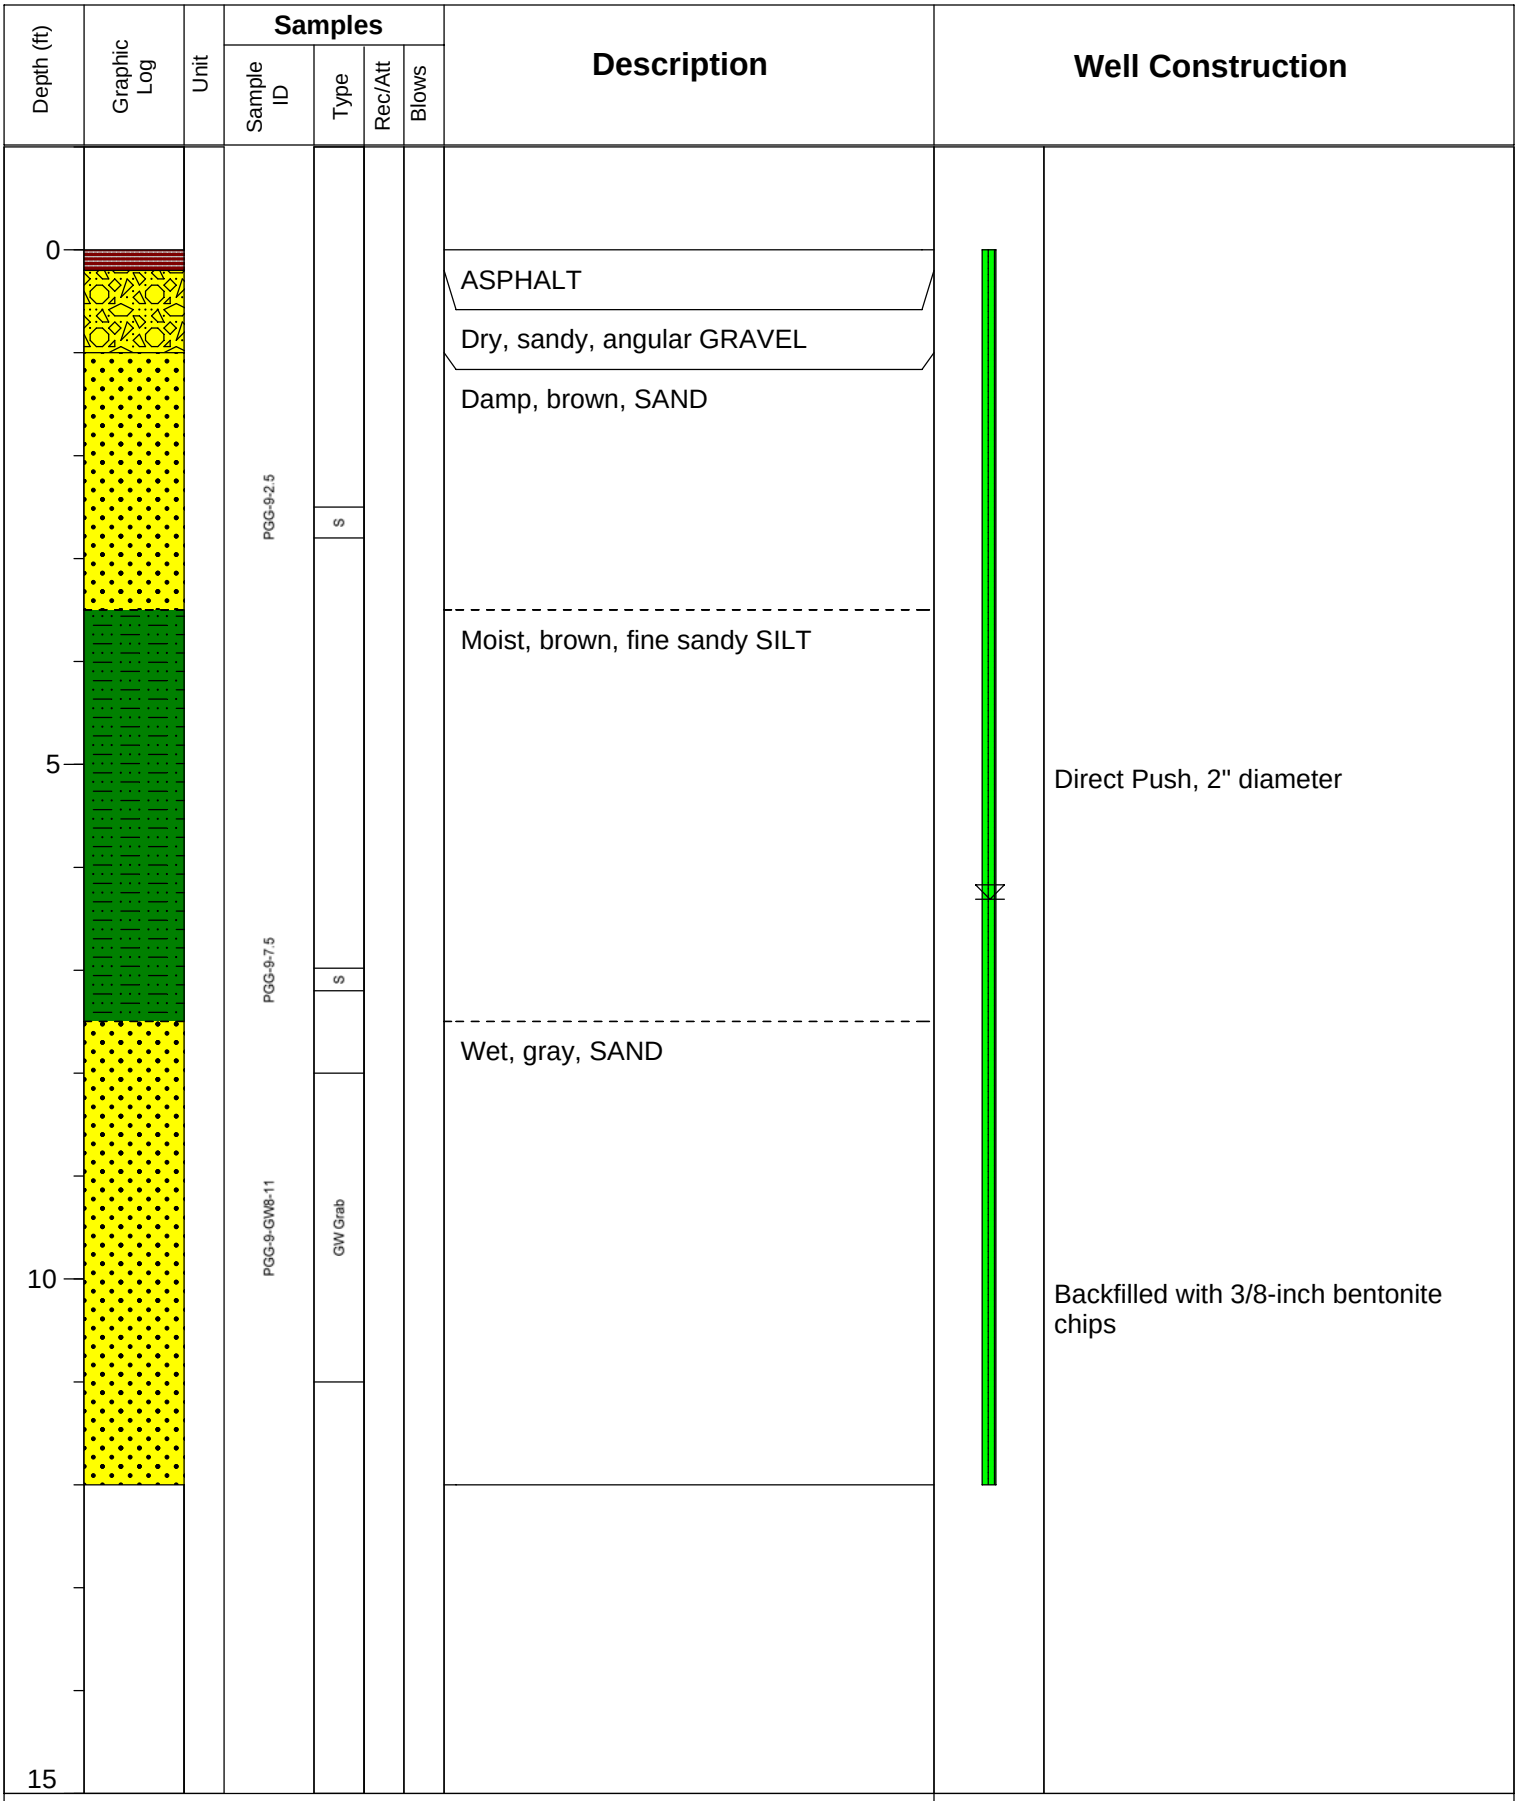


Address: 5700 3rd Ave S
City, State: Seattle, WA
Tax Parcel ID: 172280-1495
Location (TRS): T24N R4W S20; NE1/4 of SW1/4
Lat/Long: N 204751.2 ft, E 1270621 ft
Consulting Firm: Pacific Groundwater Group
Logged by: G. Wallace

Drilling Firm: ESN NW
Drilling Method: Direct Push
Ecology ID: NA
DTW: ~6.31 ft bmp
MP Elevation: ~13.3 ft
V. Datum: NAVD 88
Date: 5/1/2006

Figure
Boring Log
PGG-9

Blaser Die Casting
Remedial Investigation
JK0504.03

PGG

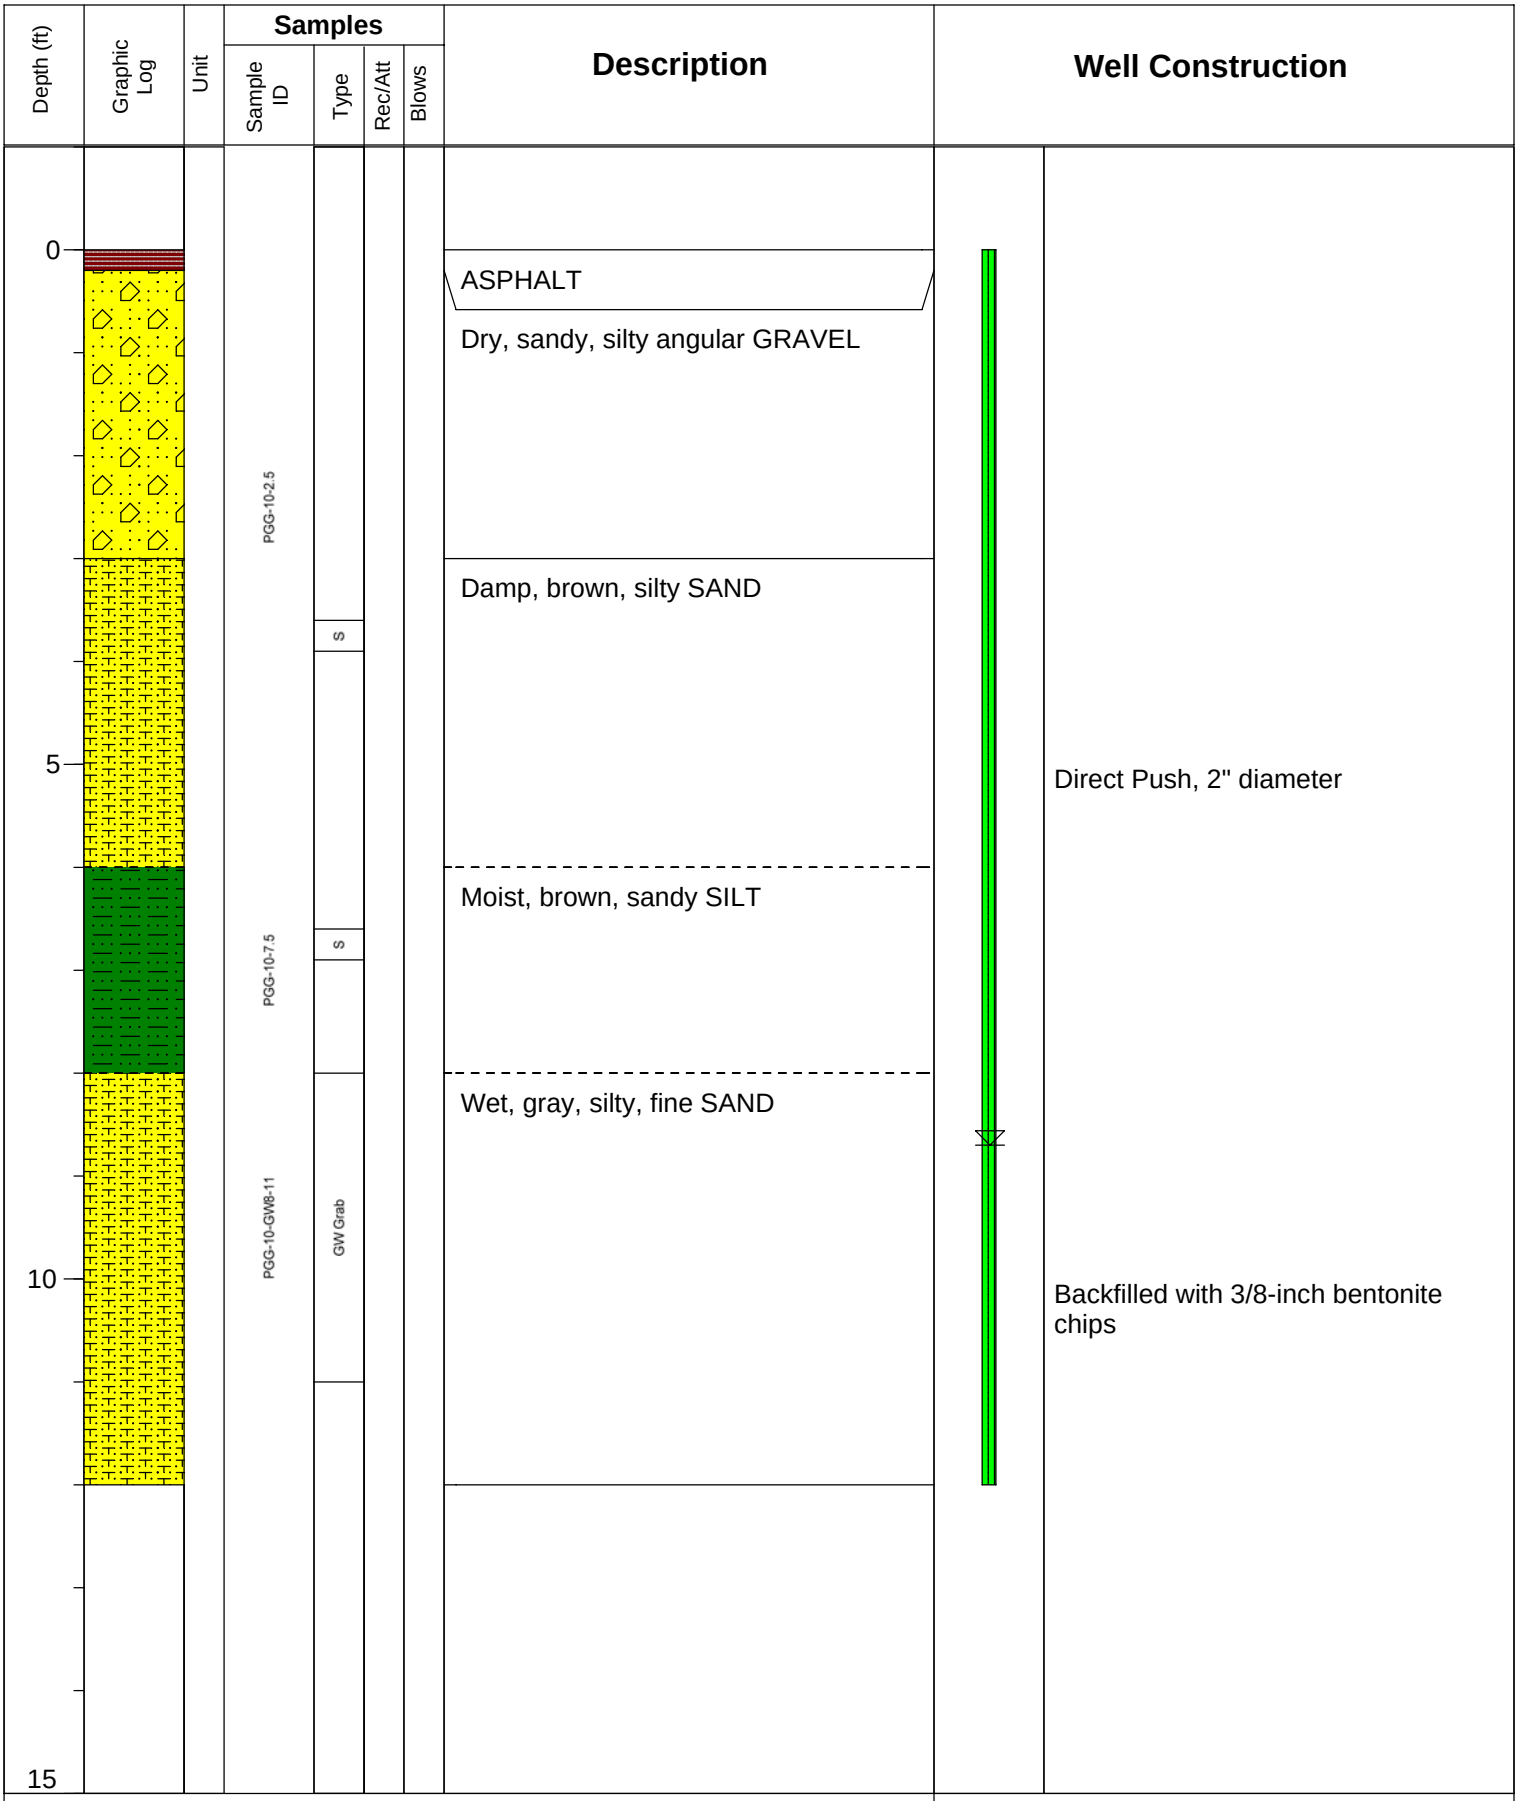


Address: 5700 3rd Ave S
City, State: Seattle, WA
Tax Parcel ID: 172280-1495
Location (TRS): T24N R4W S20; NE1/4 of SW1/4
Lat/Long: N 204768.6 ft, E 1270645 ft
Consulting Firm: Pacific Groundwater Group
Logged by: G. Wallace

Drilling Firm: ESN NW
Drilling Method: Direct Push
Ecology ID: NA
DTW: ~8.70 ft bmp
MP Elevation: ~16.75 ft
V. Datum: NAVD 88
Date: 5/1/2006

Figure
Boring Log
PGG-10

Blaser Die Casting
Remedial Investigation
JK0504.03

PgG

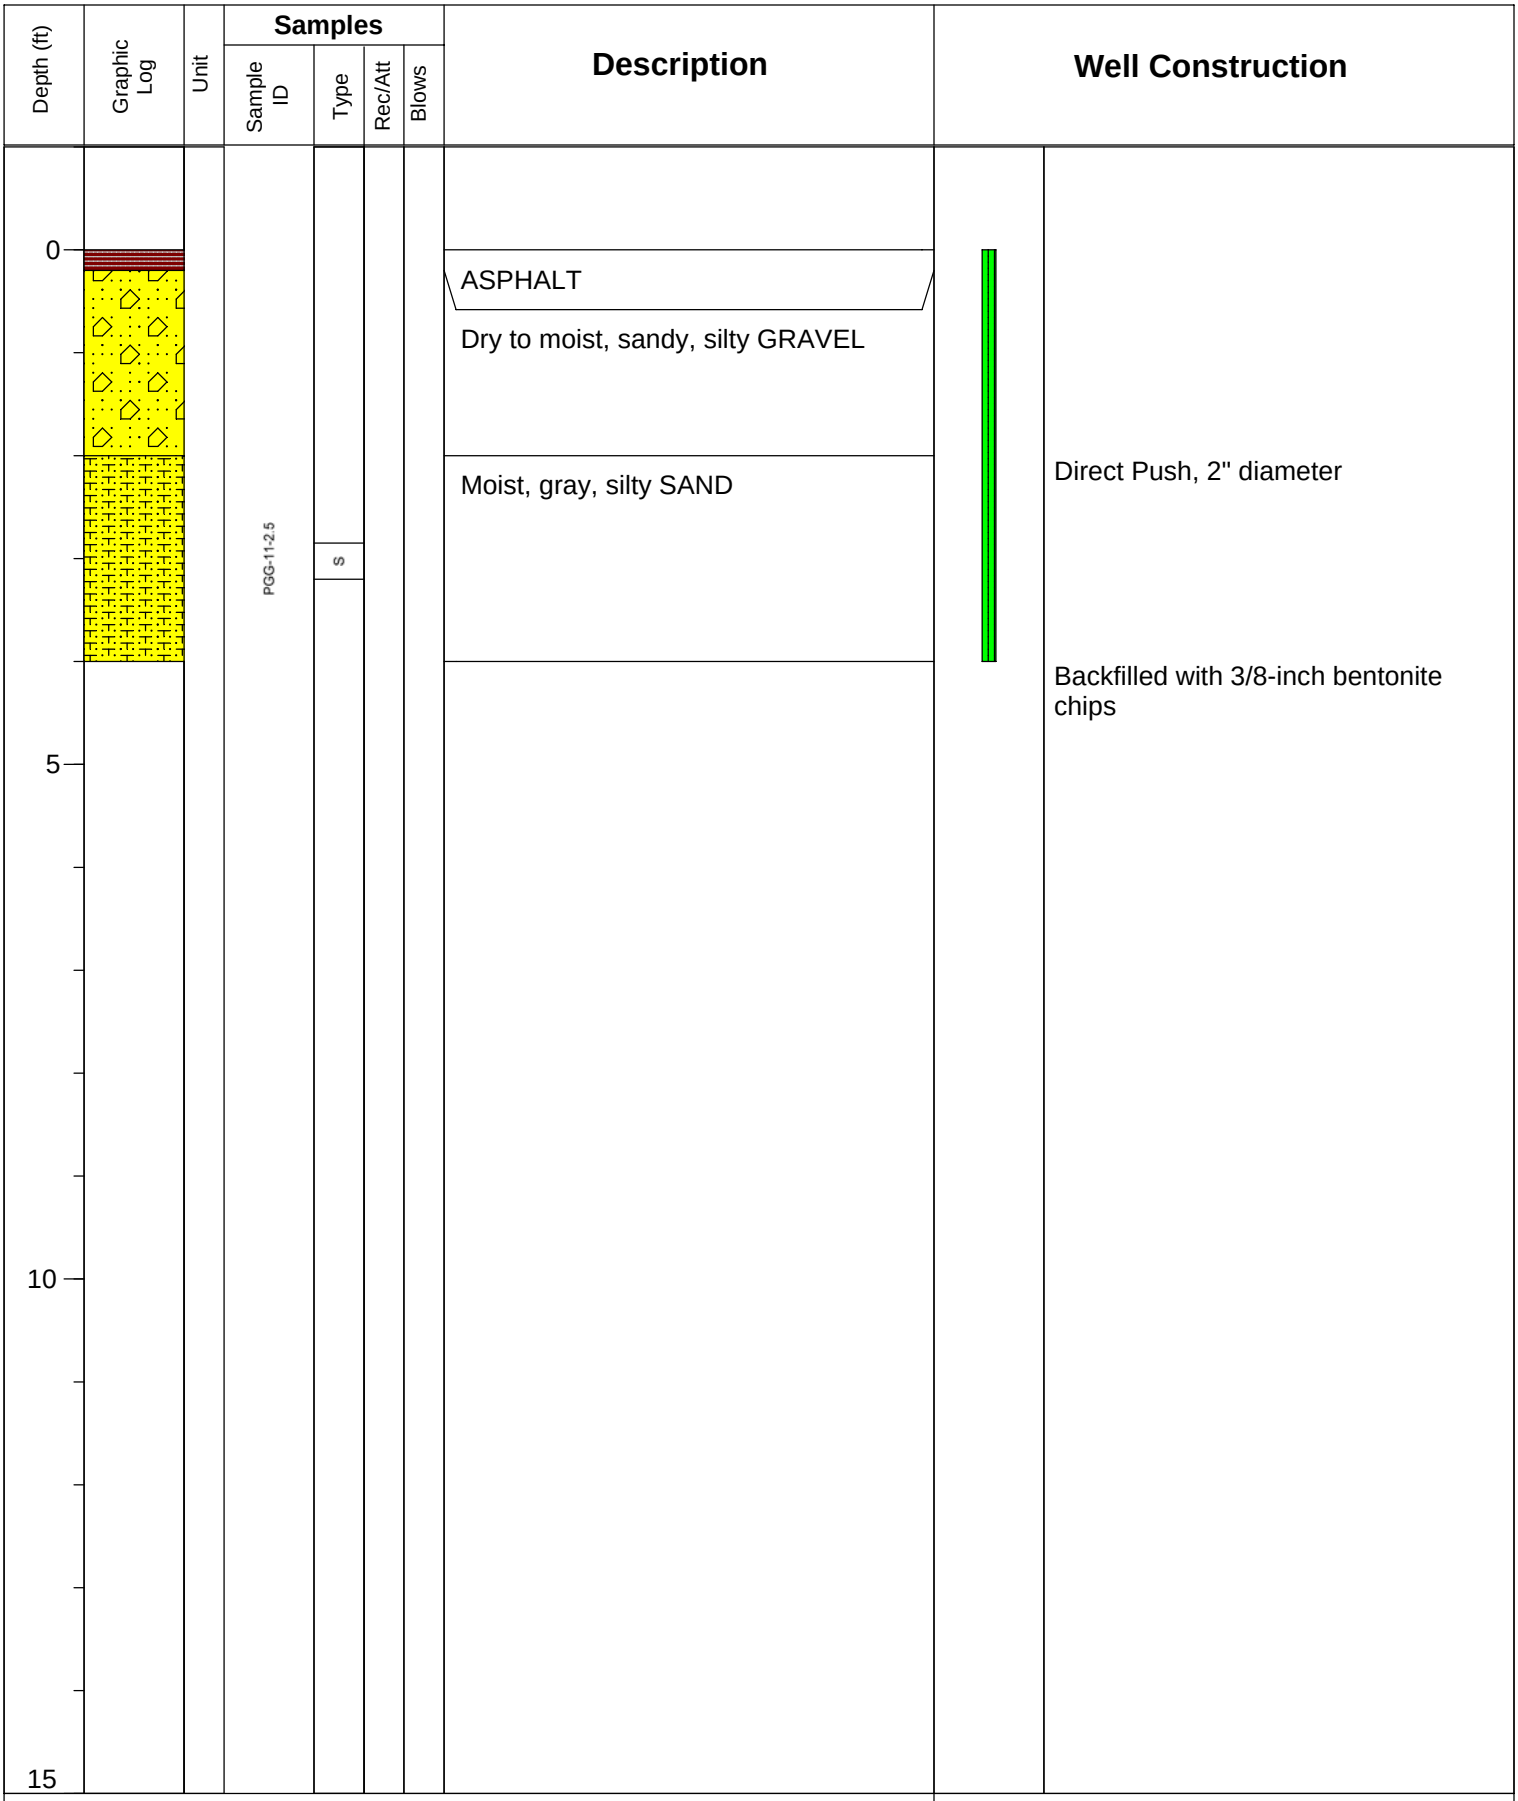


Address: 5700 3rd Ave S
City, State: Seattle, WA
Tax Parcel ID: 172280-1495
Location (TRS): T24N R4W S20; NE1/4 of SW1/4
Lat/Long: N 204774 ft, E 1270606 ft
Consulting Firm: Pacific Groundwater Group
Logged by: G. Wallace

Drilling Firm: ESN NW
Drilling Method: Direct Push
Ecology ID: NA
DTW: NA
MP Elevation: ft
V. Datum: NAVD 88
Date: 5/1/2006

Figure
Boring Log
PGG-11

Blaser Die Casting
Remedial Investigation
JK0504.03

PgG

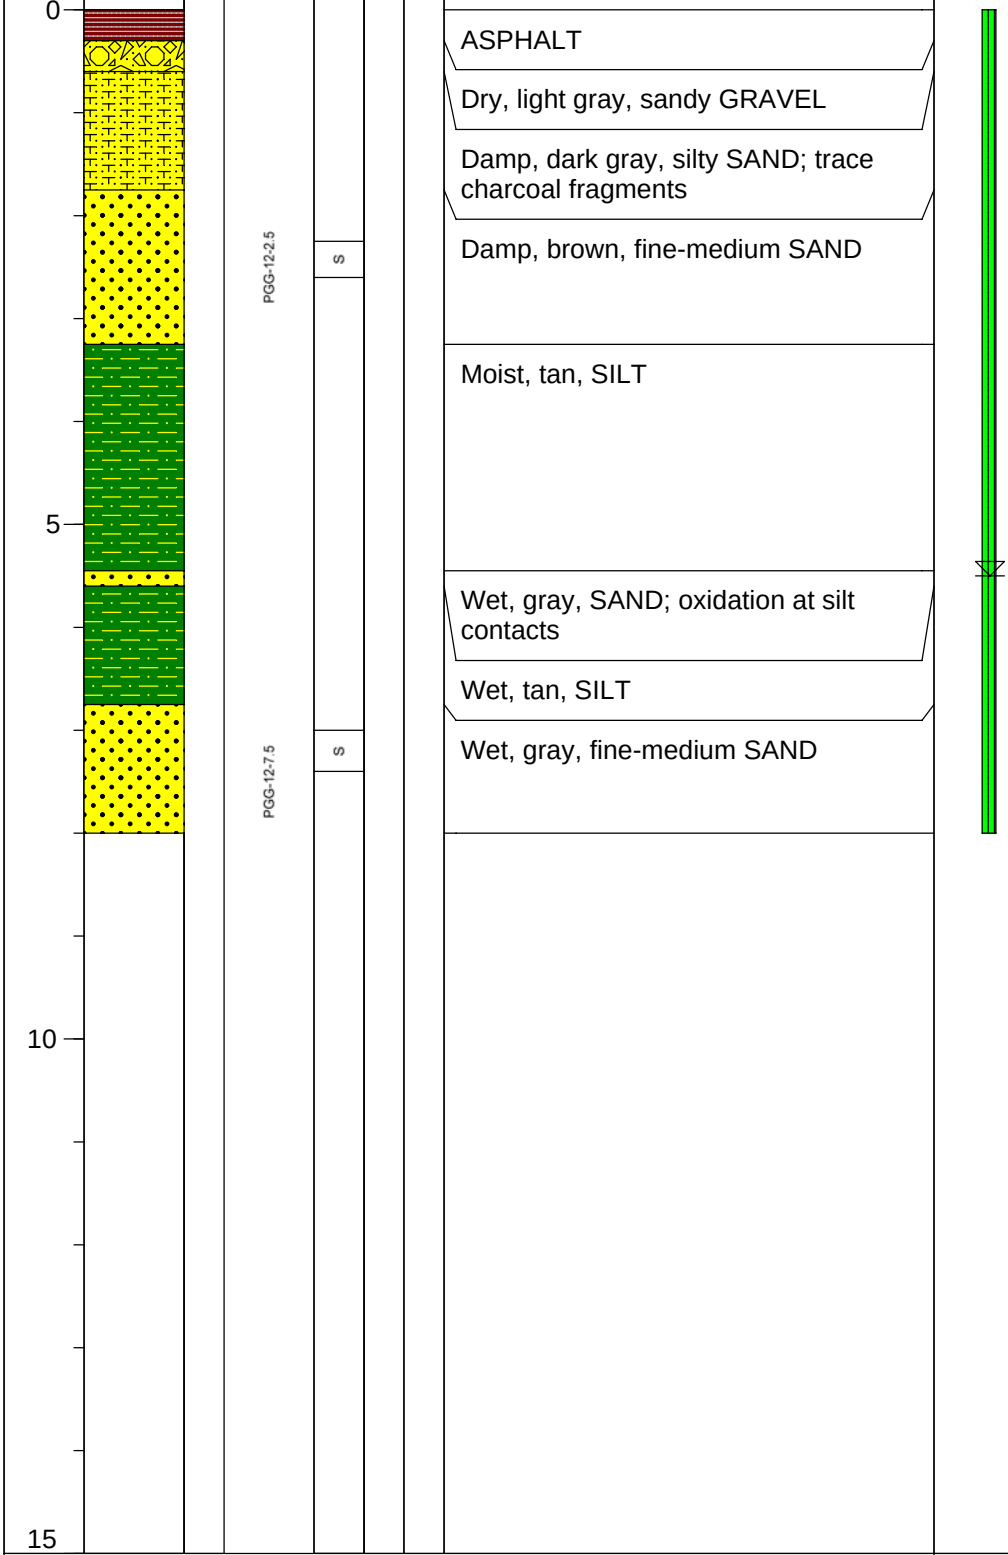


Address: 5700 3rd Ave S
City, State: Seattle, WA
Tax Parcel ID: 172280-1495
Location (TRS): T24N R4W S20; NE1/4 of SW1/4
Lat/Long: N 204758 ft, E 1270657 ft
Consulting Firm: Pacific Groundwater Group
Logged by: G. Wallace

Drilling Firm: ESN NW
Drilling Method: Direct Push
Ecology ID: NA
DTW: 5.5 ft bmp
MP Elevation: ft
V. Datum: NAVD 88
Date: 5/1/2006

Figure
Boring Log
PGG-12

Blaser Die Casting
Remedial Investigation
JK0504.03

PgG

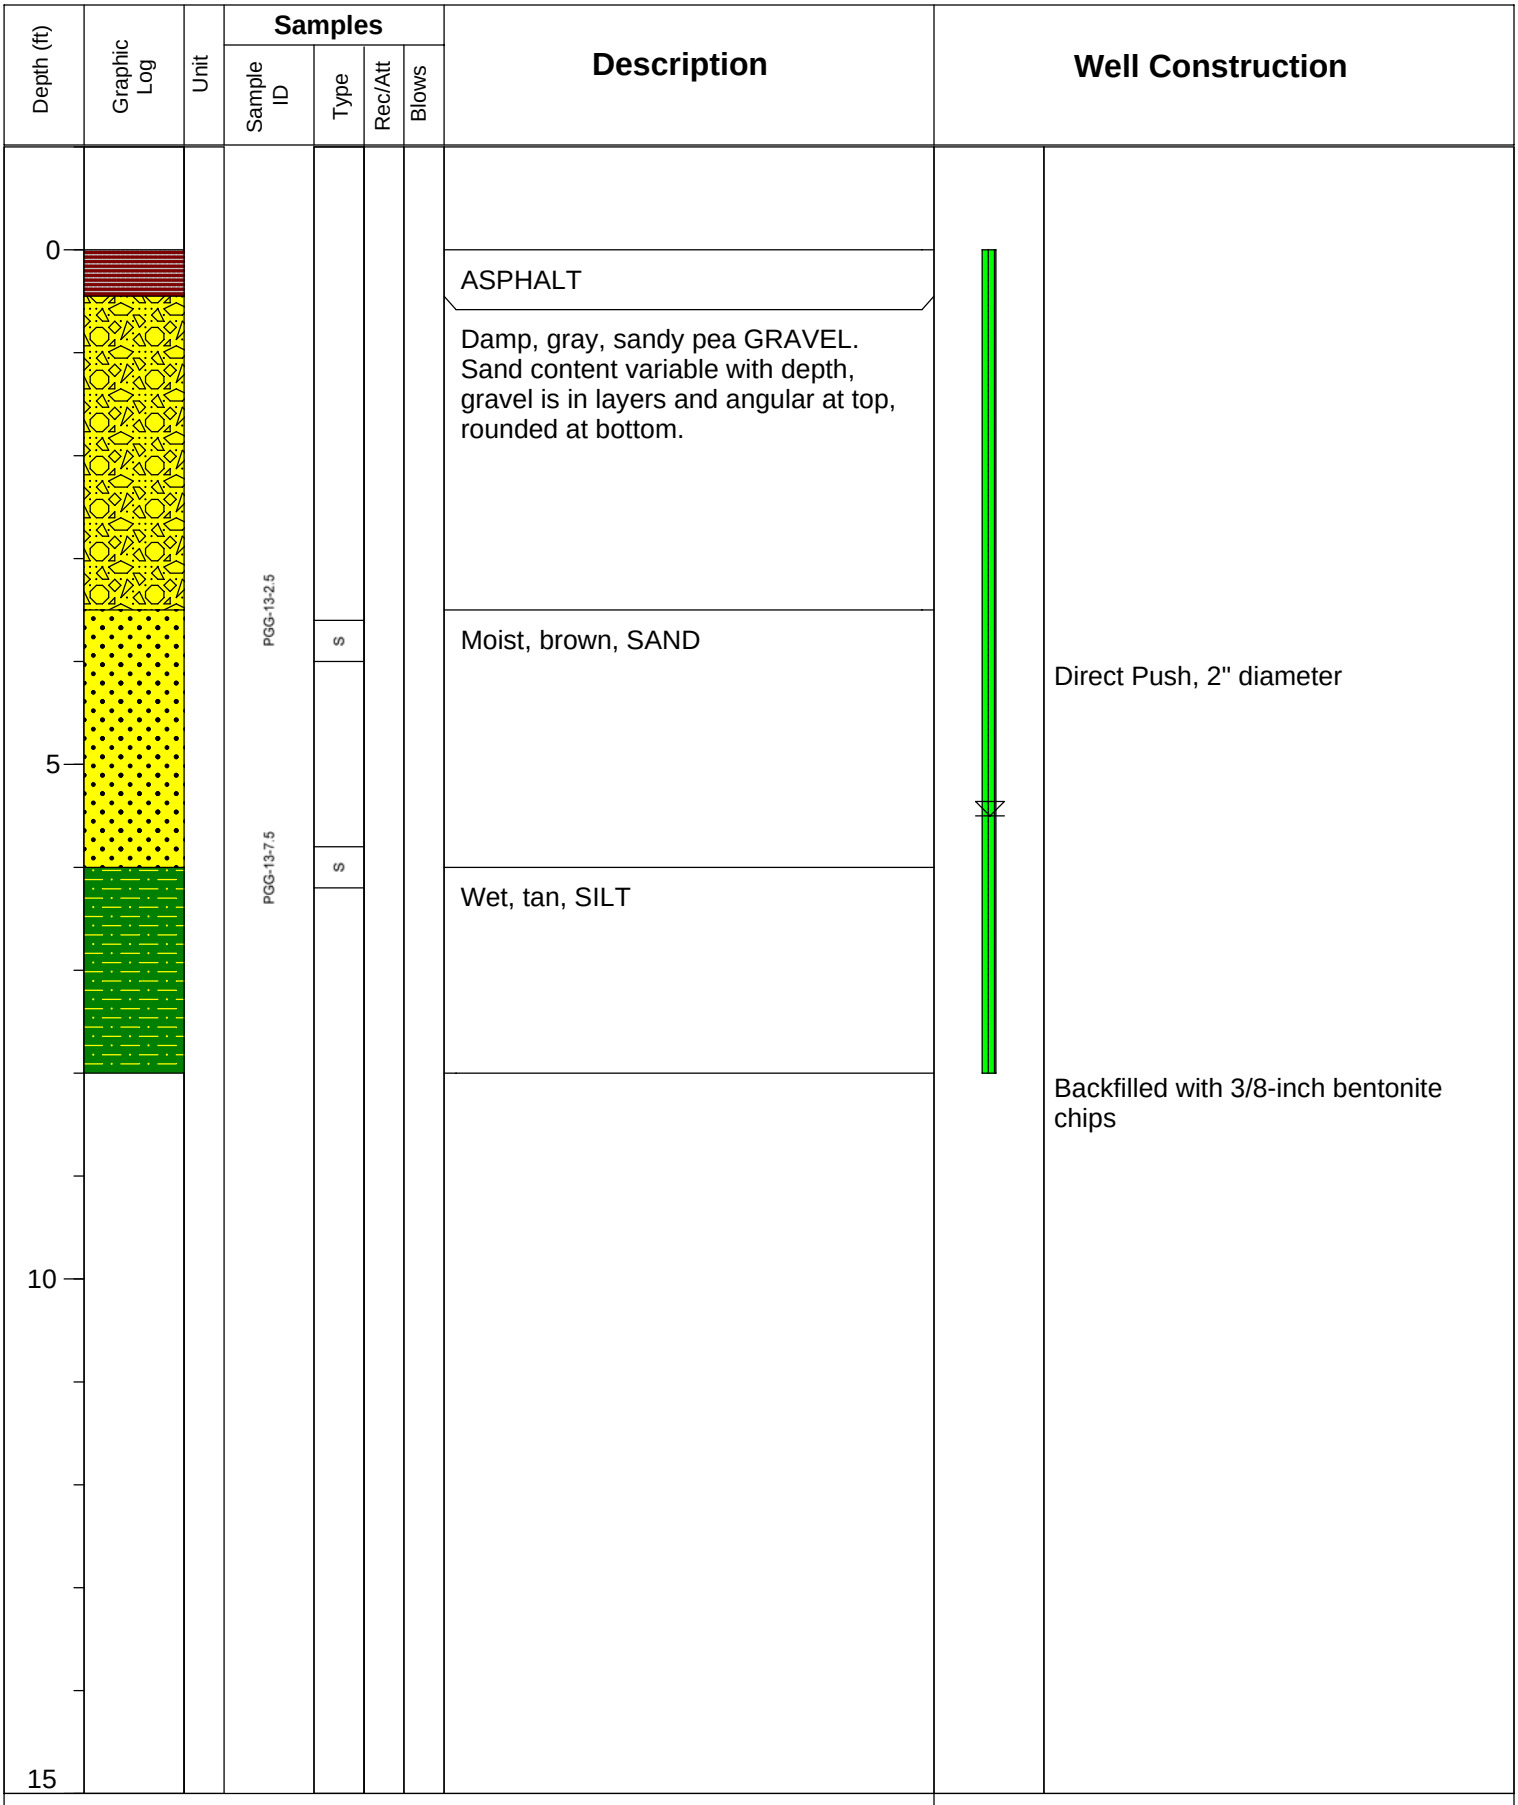


Address: 5700 3rd Ave S
City, State: Seattle, WA
Tax Parcel ID: 172280-1495
Location (TRS): T24N R4W S20; NE1/4 of SW1/4
Lat/Long: N 204797 ft, E 1270640 ft
Consulting Firm: Pacific Groundwater Group
Logged by: G. Wallace

Drilling Firm: ESN NW
Drilling Method: Direct Push
Ecology ID: NA
DTW: ~6 ft bmp
MP Elevation: ft
V. Datum: NAVD 88
Date: 5/1/2006

Figure
Boring Log
PGG-13

Blaser Die Casting
Remedial Investigation
JK0504.03

PgG

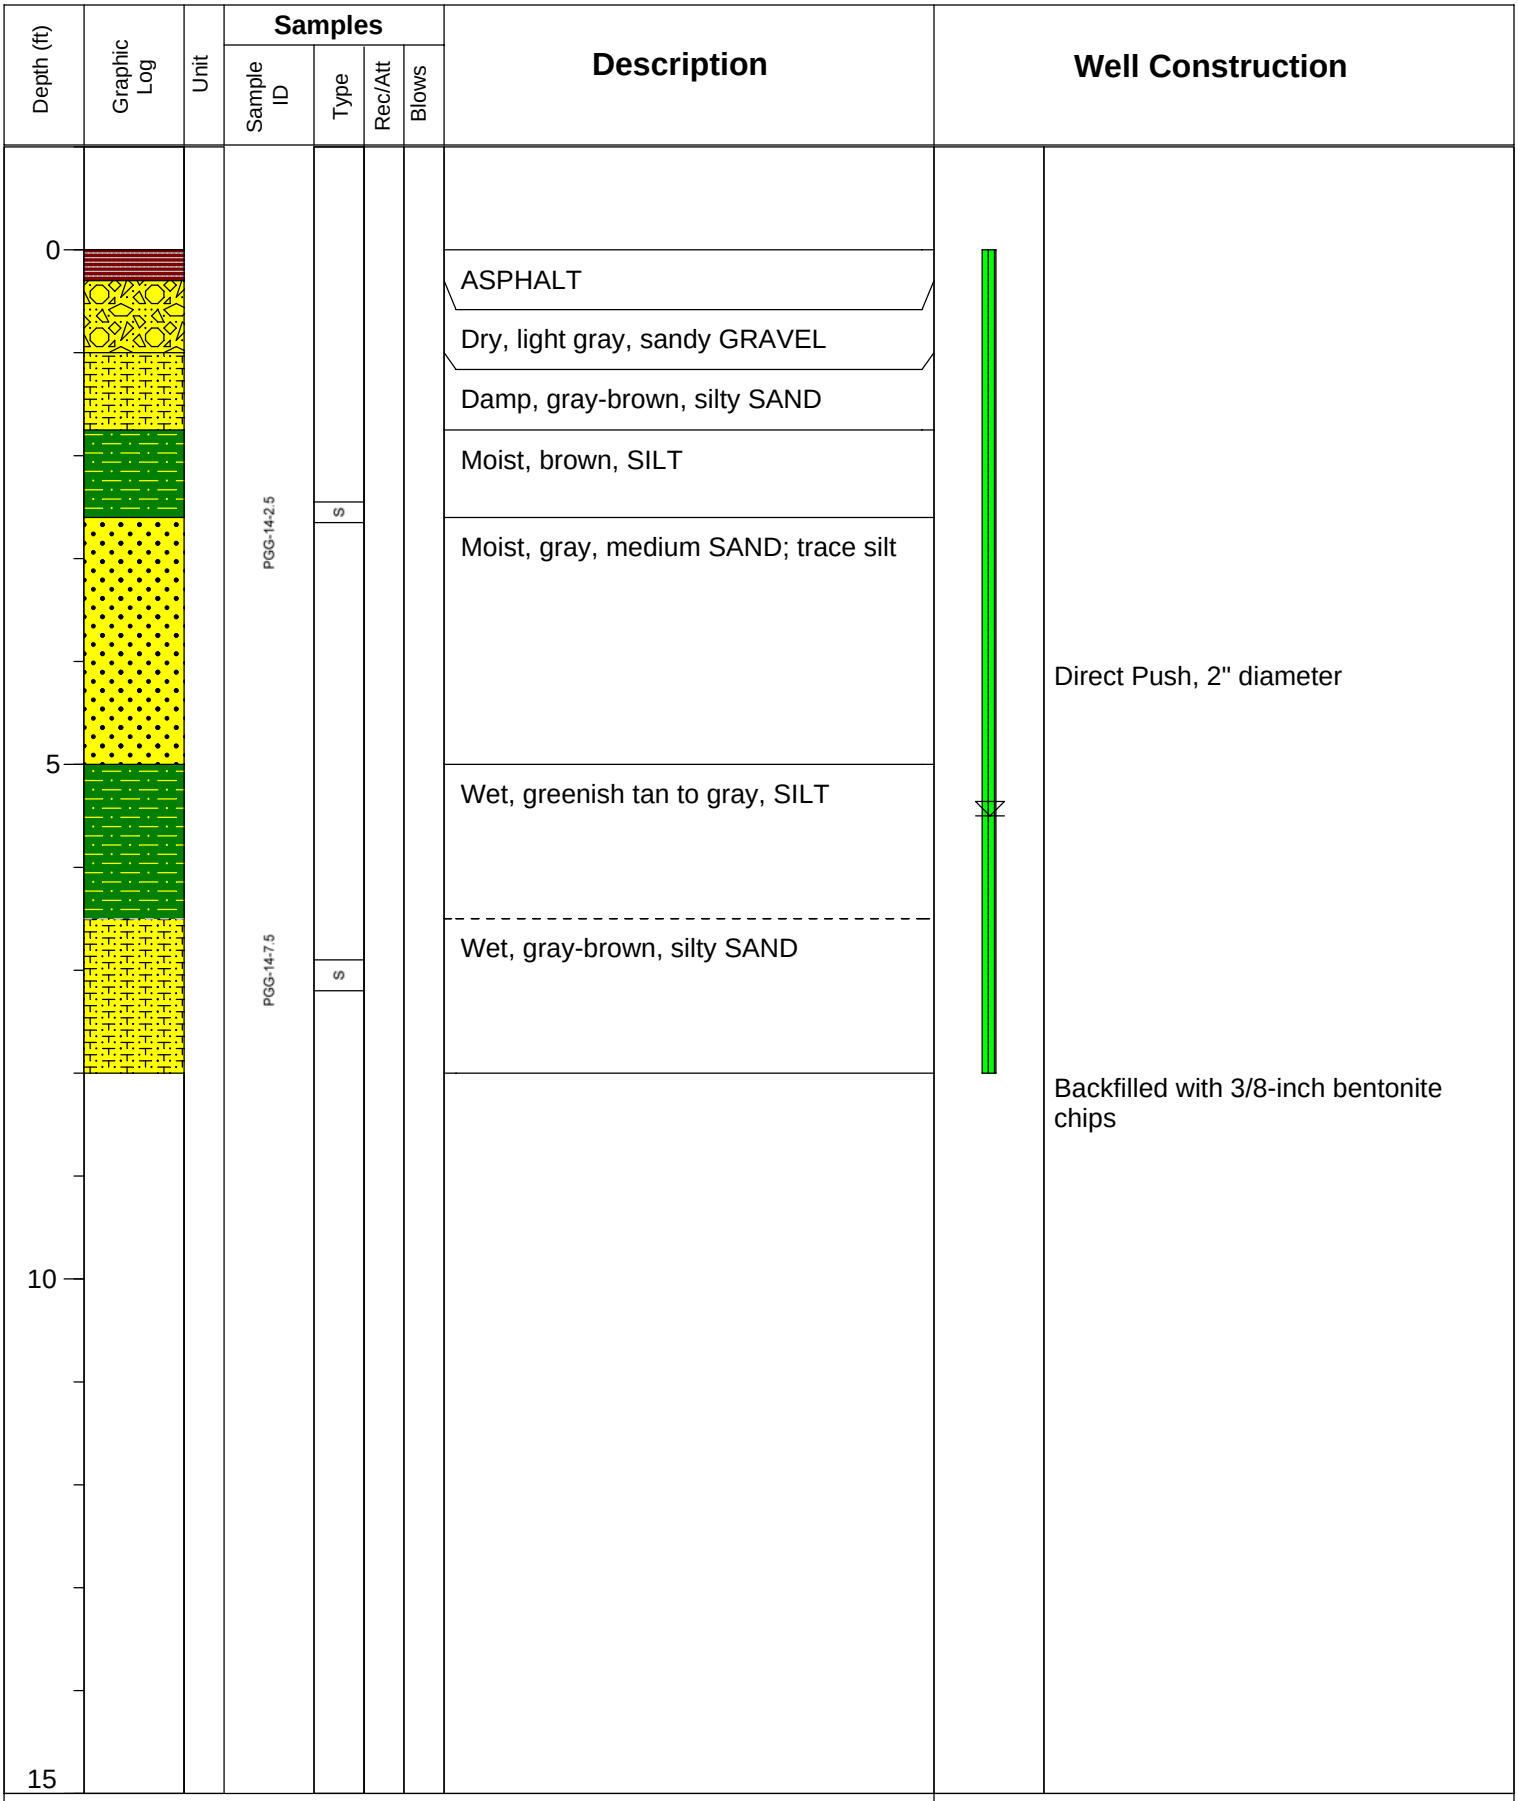


Address: 5700 3rd Ave S
City, State: Seattle, WA
Tax Parcel ID: 172280-1495
Location (TRS): T24N R4W S20; NE1/4 of SW1/4
Lat/Long: N 204796 ft, E 1270623 ft
Consulting Firm: Pacific Groundwater Group
Logged by: G. Wallace

Drilling Firm: ESN NW
Drilling Method: Direct Push
Ecology ID: NA
DTW: ~5.5 ft bmp
MP Elevation: ft
V. Datum: NAVD 88
Date: 5/1/2006

Figure
Boring Log
PGG-14

Blaser Die Casting
Remedial Investigation
JK0504.03

PGG

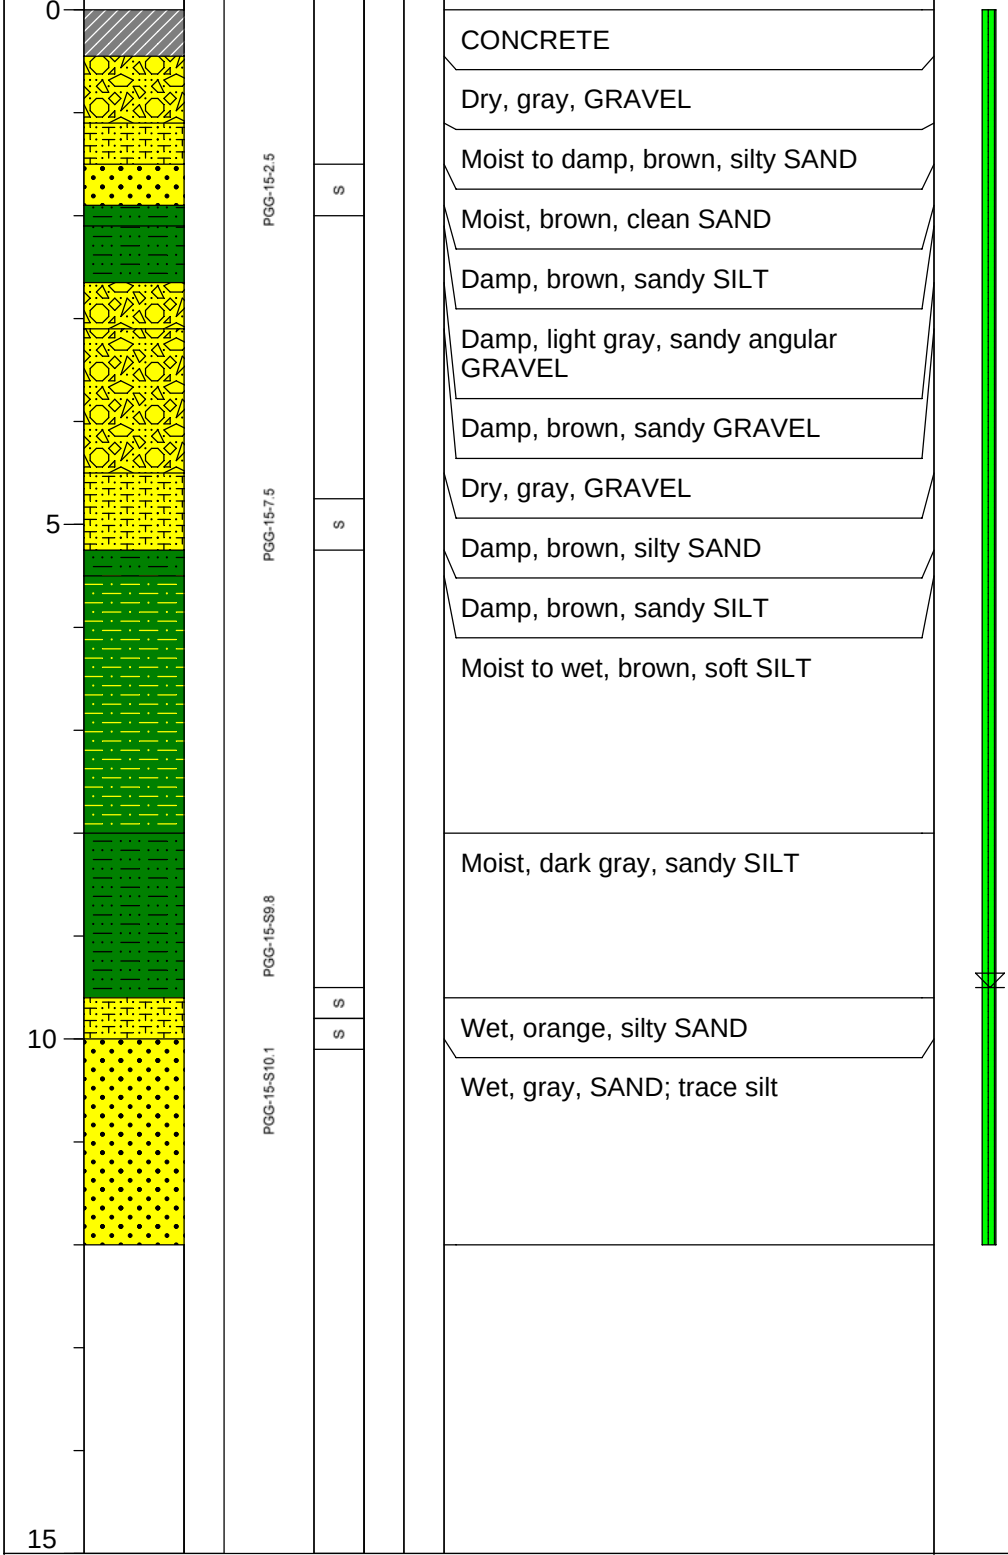


Address: 5700 3rd Ave S
City, State: Seattle, WA
Tax Parcel ID: 172280-1495
Location (TRS): T24N R4W S20; NE1/4 of SW1/4
Lat/Long: N 204821 ft, E 1270691 ft
Consulting Firm: Pacific Groundwater Group
Logged by: G. Wallace

Drilling Firm: ESN NW
Drilling Method: Direct Push
Ecology ID: NA
DTW: ~9.5 ft bmp
MP Elevation: ft
V. Datum: NAVD 88
Date: 5/1/2006

Figure
Boring Log
PGG-15

Blaser Die Casting
Remedial Investigation
JK0504.03

PGG

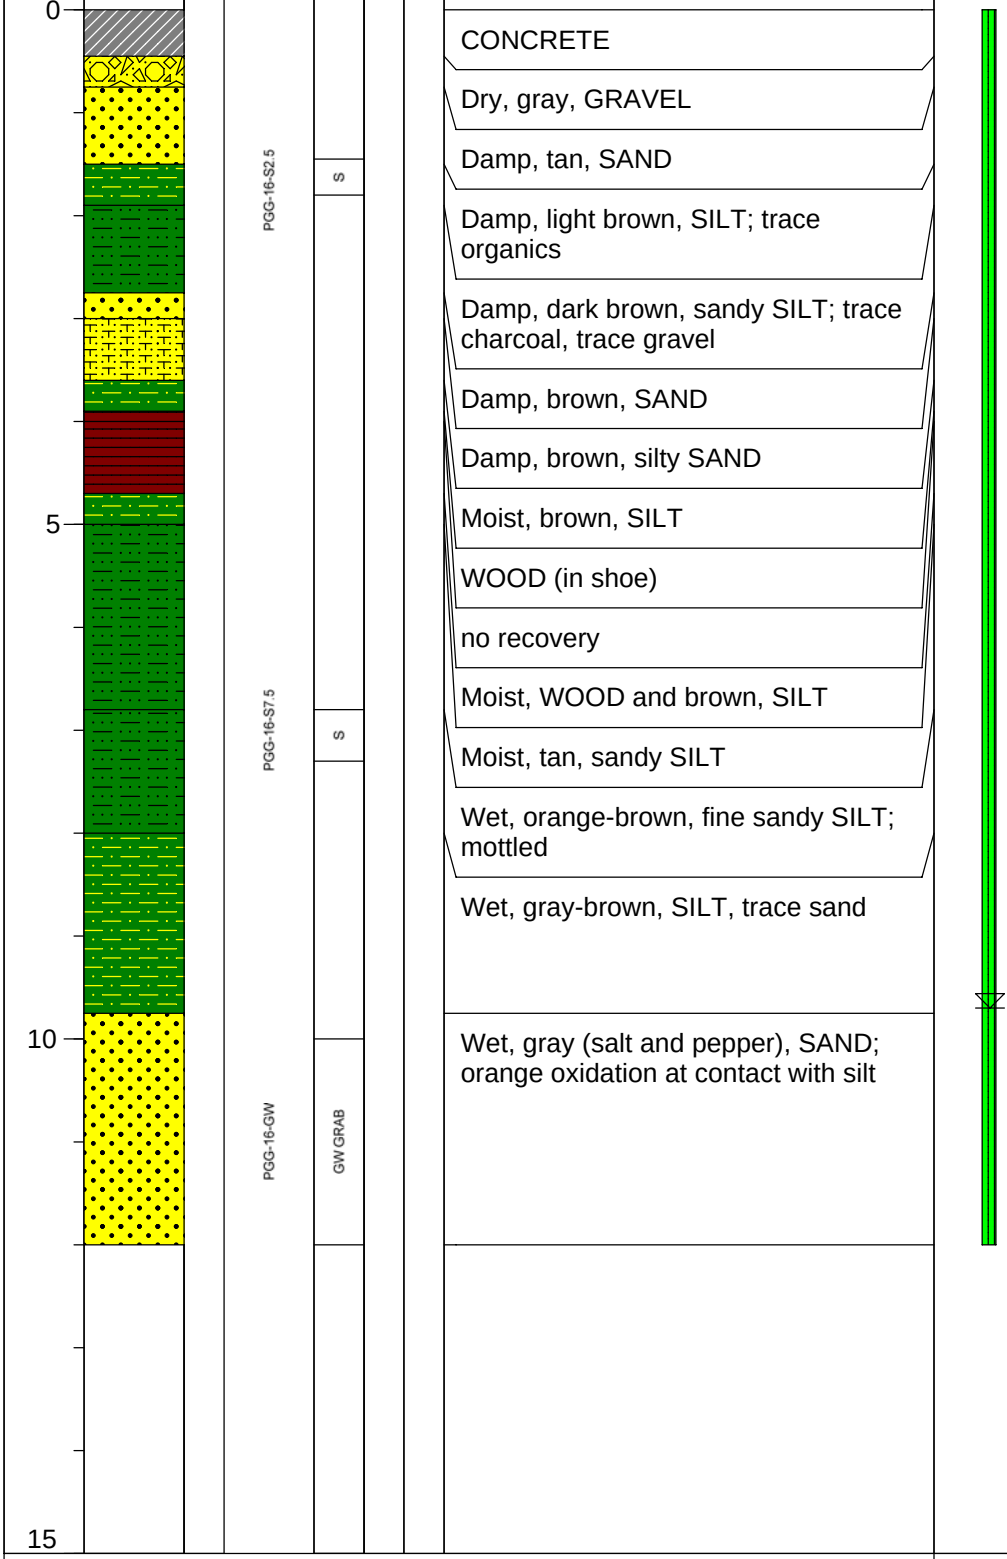


Address: 5700 3rd Ave S
City, State: Seattle, WA
Tax Parcel ID: 172280-1495
Location (TRS): T24N R4W S20; NE1/4 of SW1/4
Lat/Long: N 204843 ft, E 1270754 ft
Consulting Firm: Pacific Groundwater Group
Logged by: G. Wallace

Drilling Firm: ESN NW
Drilling Method: Direct Push
Ecology ID: NA
DTW: ~9.7 ft bmp
MP Elevation: ft
V. Datum: NAVD 88
Date: 5/1/2006

Figure
Boring Log
PGG-16

Blaser Die Casting
Remedial Investigation
JK0504.03

PGG

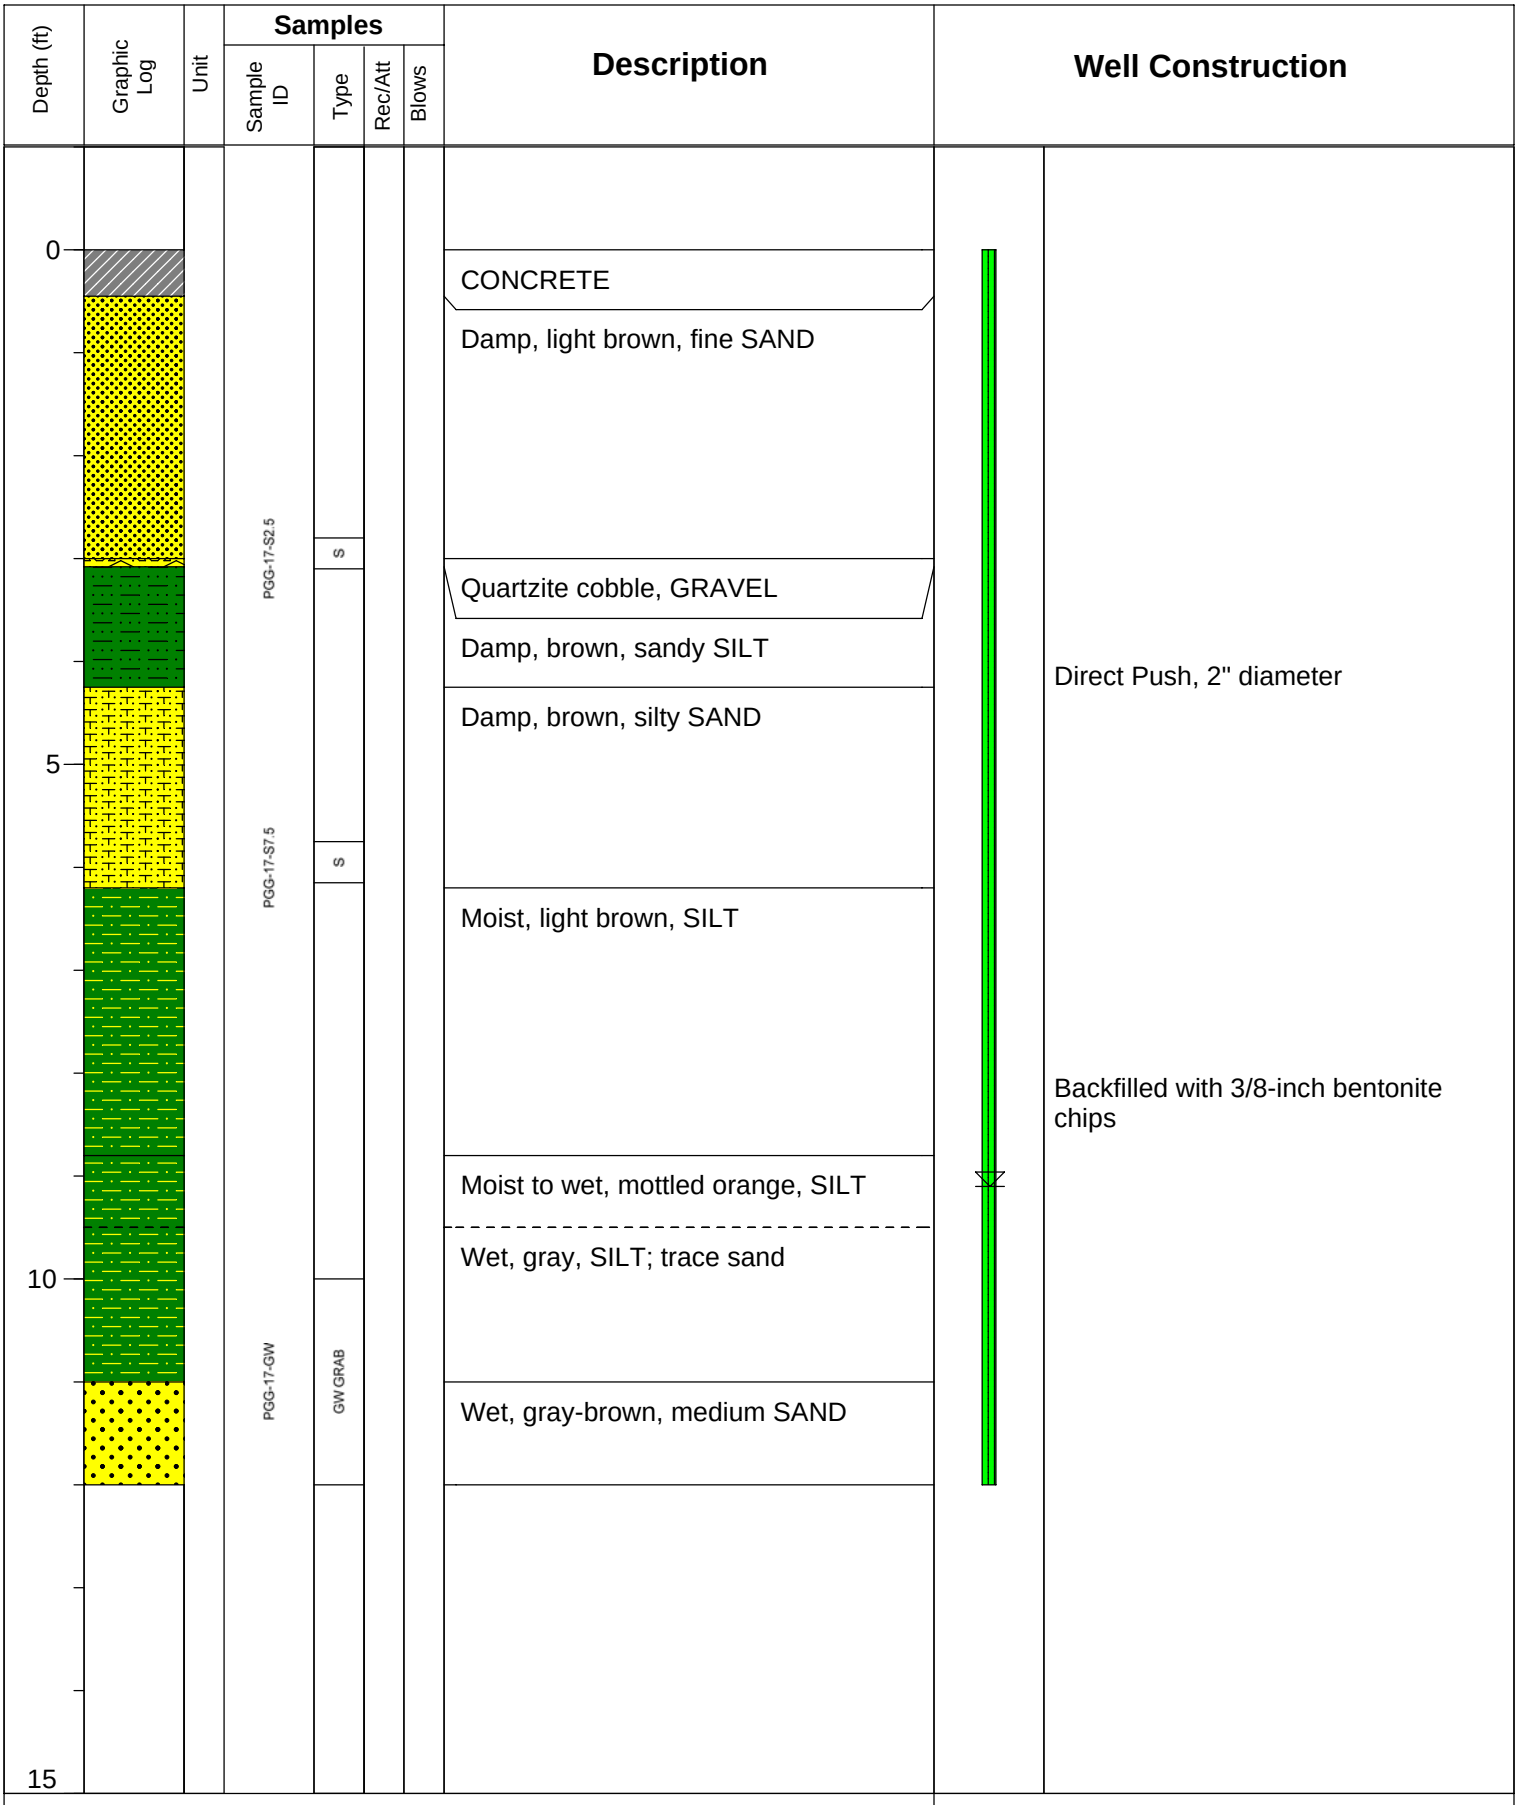


Address: 5700 3rd Ave S
City, State: Seattle, WA
Tax Parcel ID: 172280-1495
Location (TRS): T24N R4W S20; NE1/4 of SW1/4
Lat/Long: N 204795 ft, E 1270672 ft
Consulting Firm: Pacific Groundwater Group
Logged by: G. Wallace

Drilling Firm: ESN NW
Drilling Method: Direct Push
Ecology ID: NA
DTW: ~9.1 ft bmp
MP Elevation: ft
V. Datum: NAVD 88
Date: 5/1/2006

Figure
Boring Log
PGG-17

Blaser Die Casting
Remedial Investigation
JK0504.03

PGG

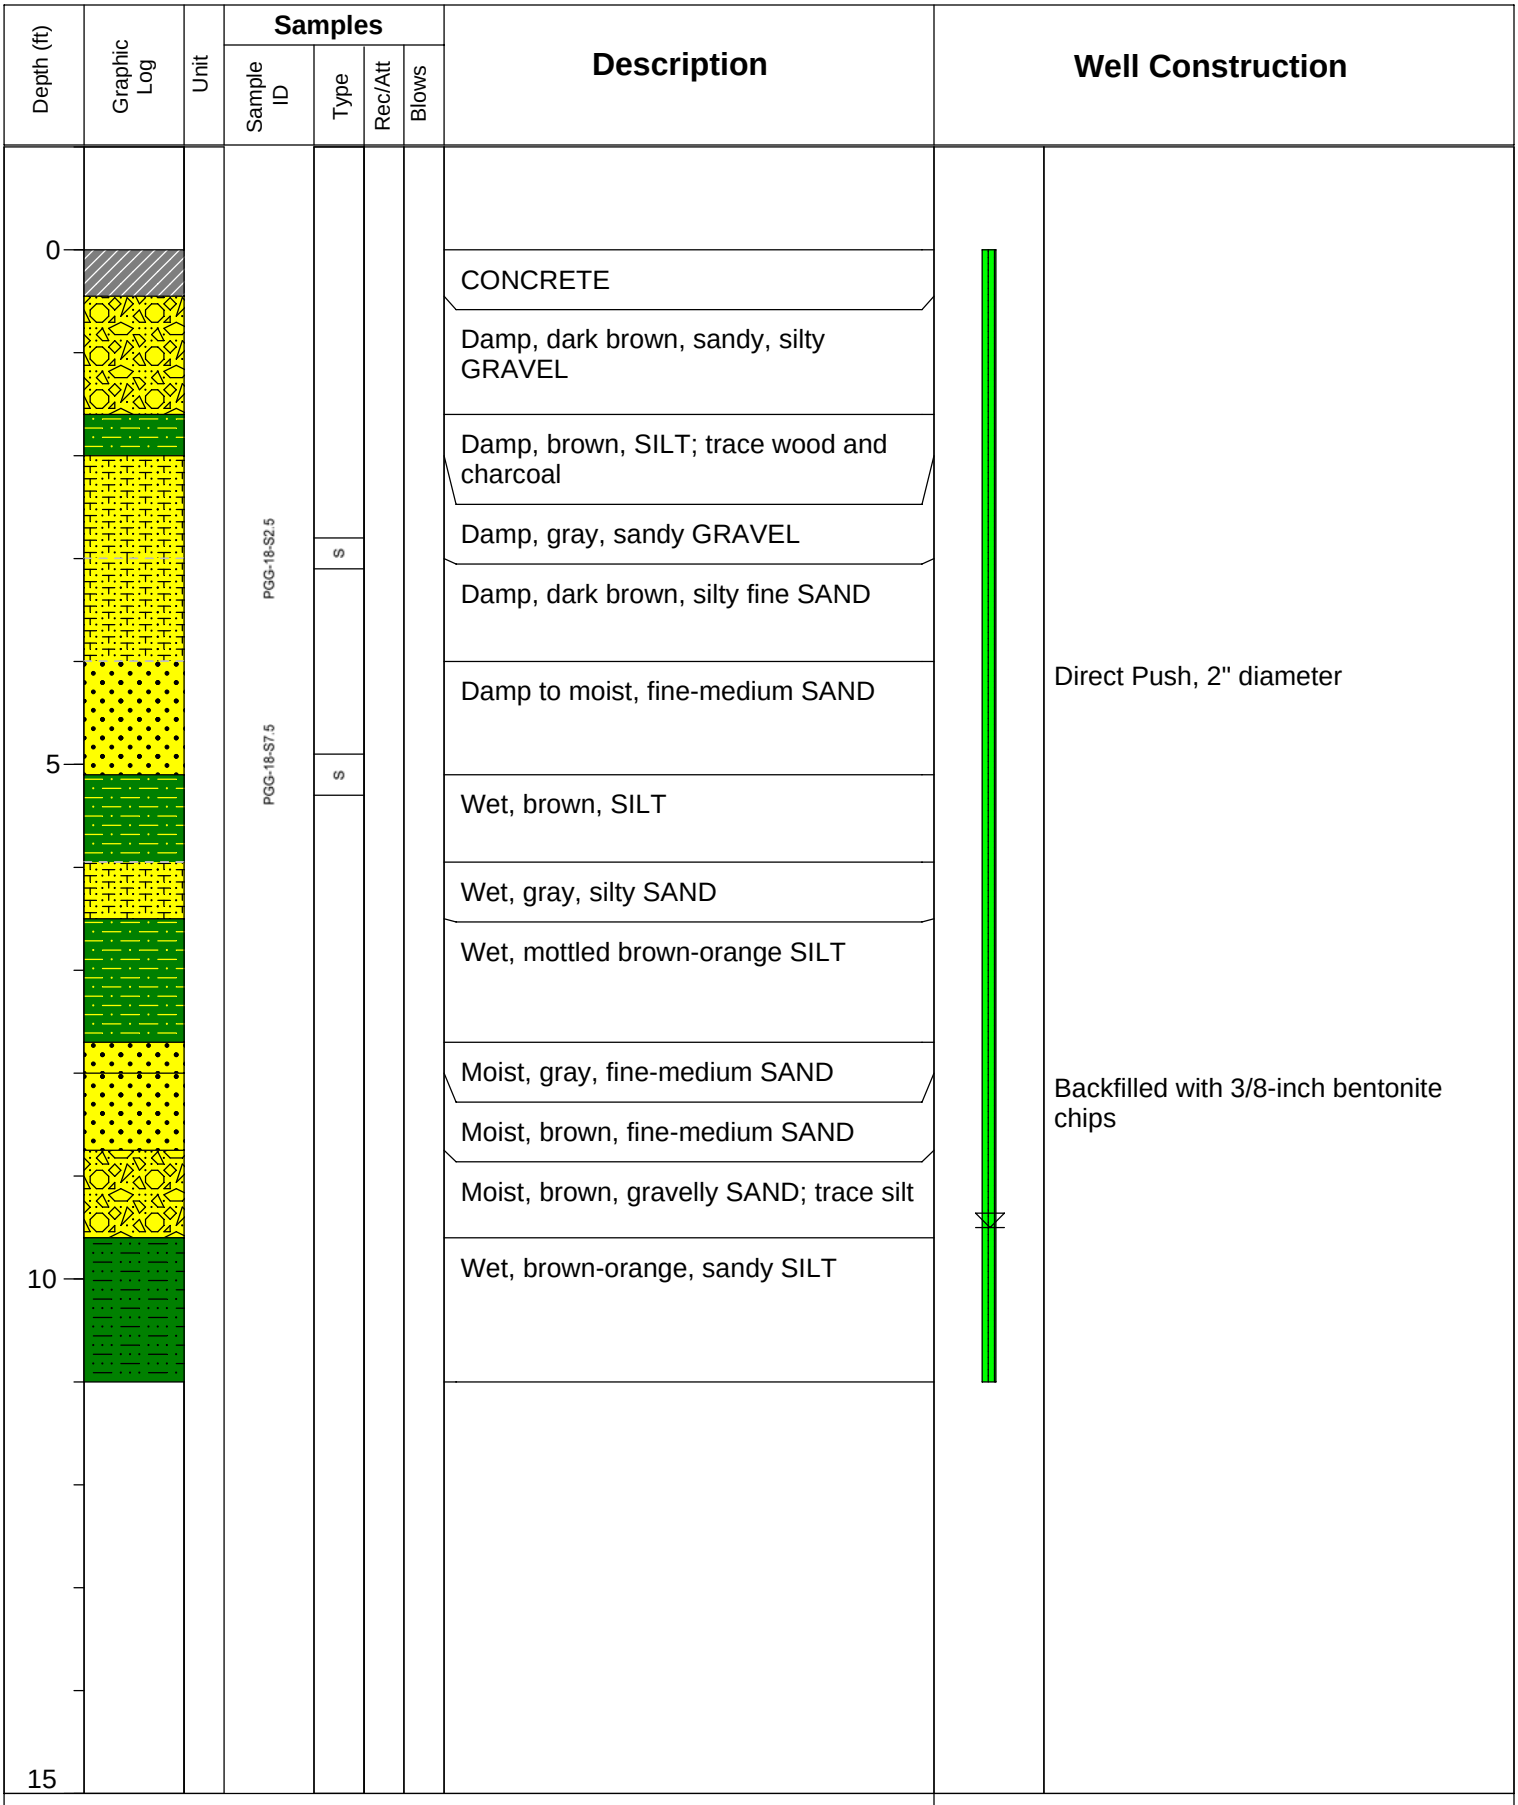


Address: 5700 3rd Ave S
City, State: Seattle, WA
Tax Parcel ID: 172280-1495
Location (TRS): T24N R4W S20; NE1/4 of SW1/4
Lat/Long: N 204769 ft, E 1270667 ft
Consulting Firm: Pacific Groundwater Group
Logged by: G. Wallace

Drilling Firm: ESN NW
Drilling Method: Direct Push
Ecology ID: NA
DTW: ~9.5 ft bmp
MP Elevation: ft
V. Datum: NAVD 88
Date: 5/1/2006

Figure
Boring Log
PGG-18

Blaser Die Casting
Remedial Investigation
JK0504.03

PGG

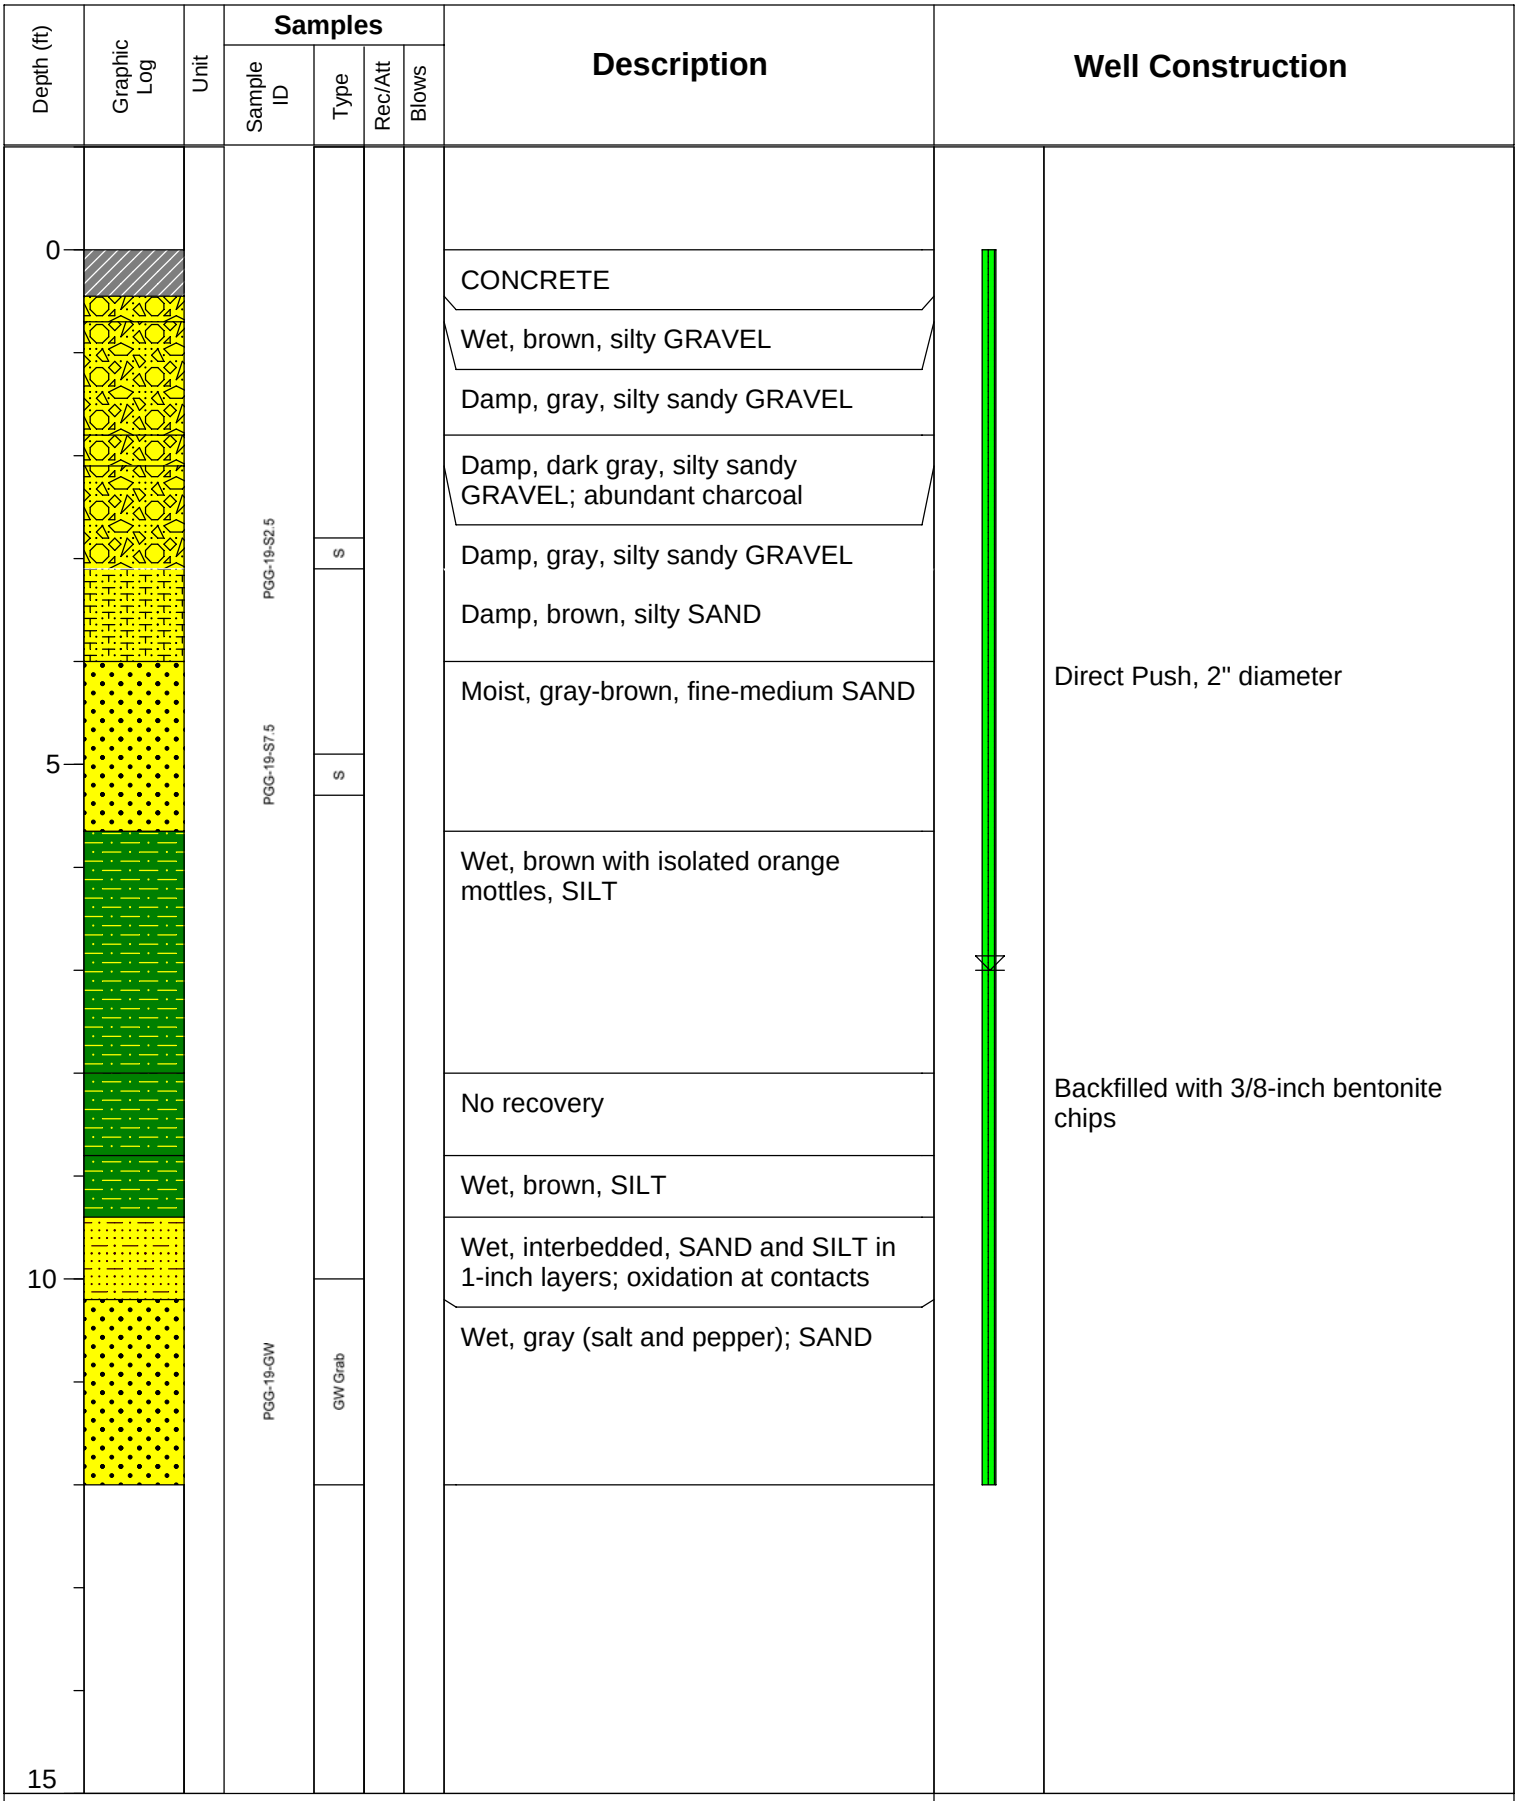


Address: 5700 3rd Ave S
City, State: Seattle, WA
Tax Parcel ID: 172280-1495
Location (TRS): T24N R4W S20; NE1/4 of SW1/4
Lat/Long: N 204768 ft, E 1270686 ft
Consulting Firm: Pacific Groundwater Group
Logged by: G. Wallace

Drilling Firm: ESN NW
Drilling Method: Direct Push
Ecology ID: NA
DTW: ~7 ft bmp
MP Elevation: ft
V. Datum: NAVD 88
Date: 5/1/2006

Figure
Boring Log
PGG-19

Blaser Die Casting
Remedial Investigation
JK0504.03

PGG

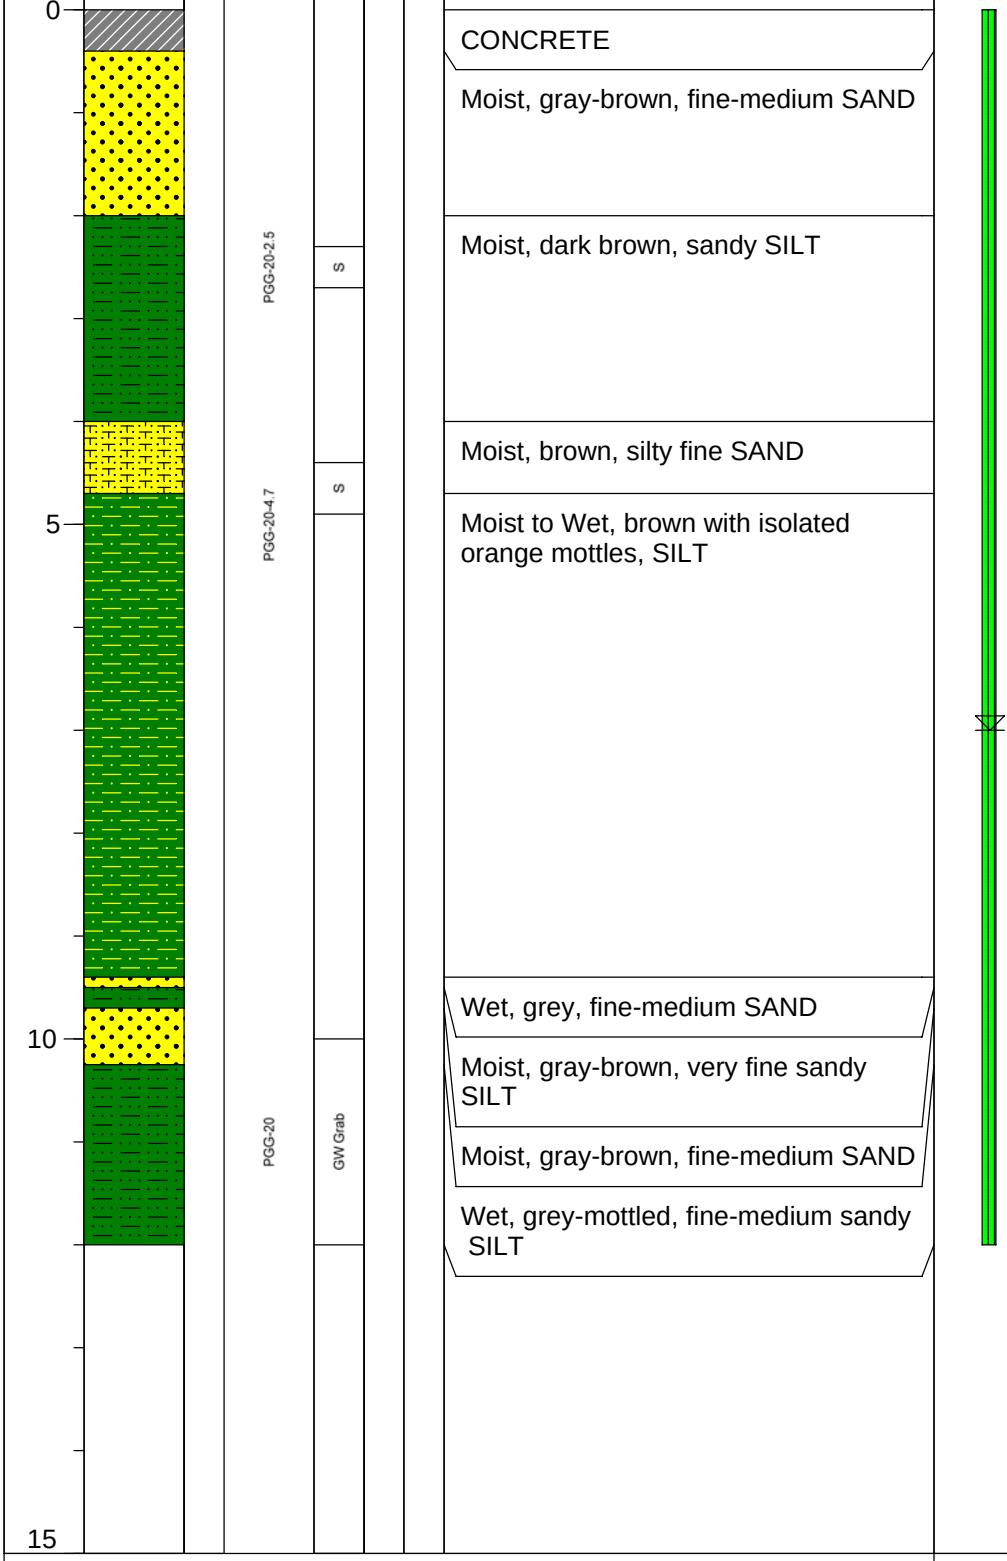


Address: 5700 3rd Ave S
City, State: Seattle, WA
Tax Parcel ID: 172280-1495
Location (TRS): T24N R4W S20; NE1/4 of SW1/4
Lat/Long: N 204806 ft, E 1270671 ft
Consulting Firm: Pacific Groundwater Group
Logged by: G. Mutti

Drilling Firm: ESN NW
Drilling Method: Direct Push
Ecology ID: NA
DTW: ~7 ft bmp
MP Elevation: ft
V. Datum: NAVD 88
Date: 8/3/2007

Figure
Boring Log
PGG-20

Blaser Die Casting
Remedial Investigation
JK0504.03

PGG

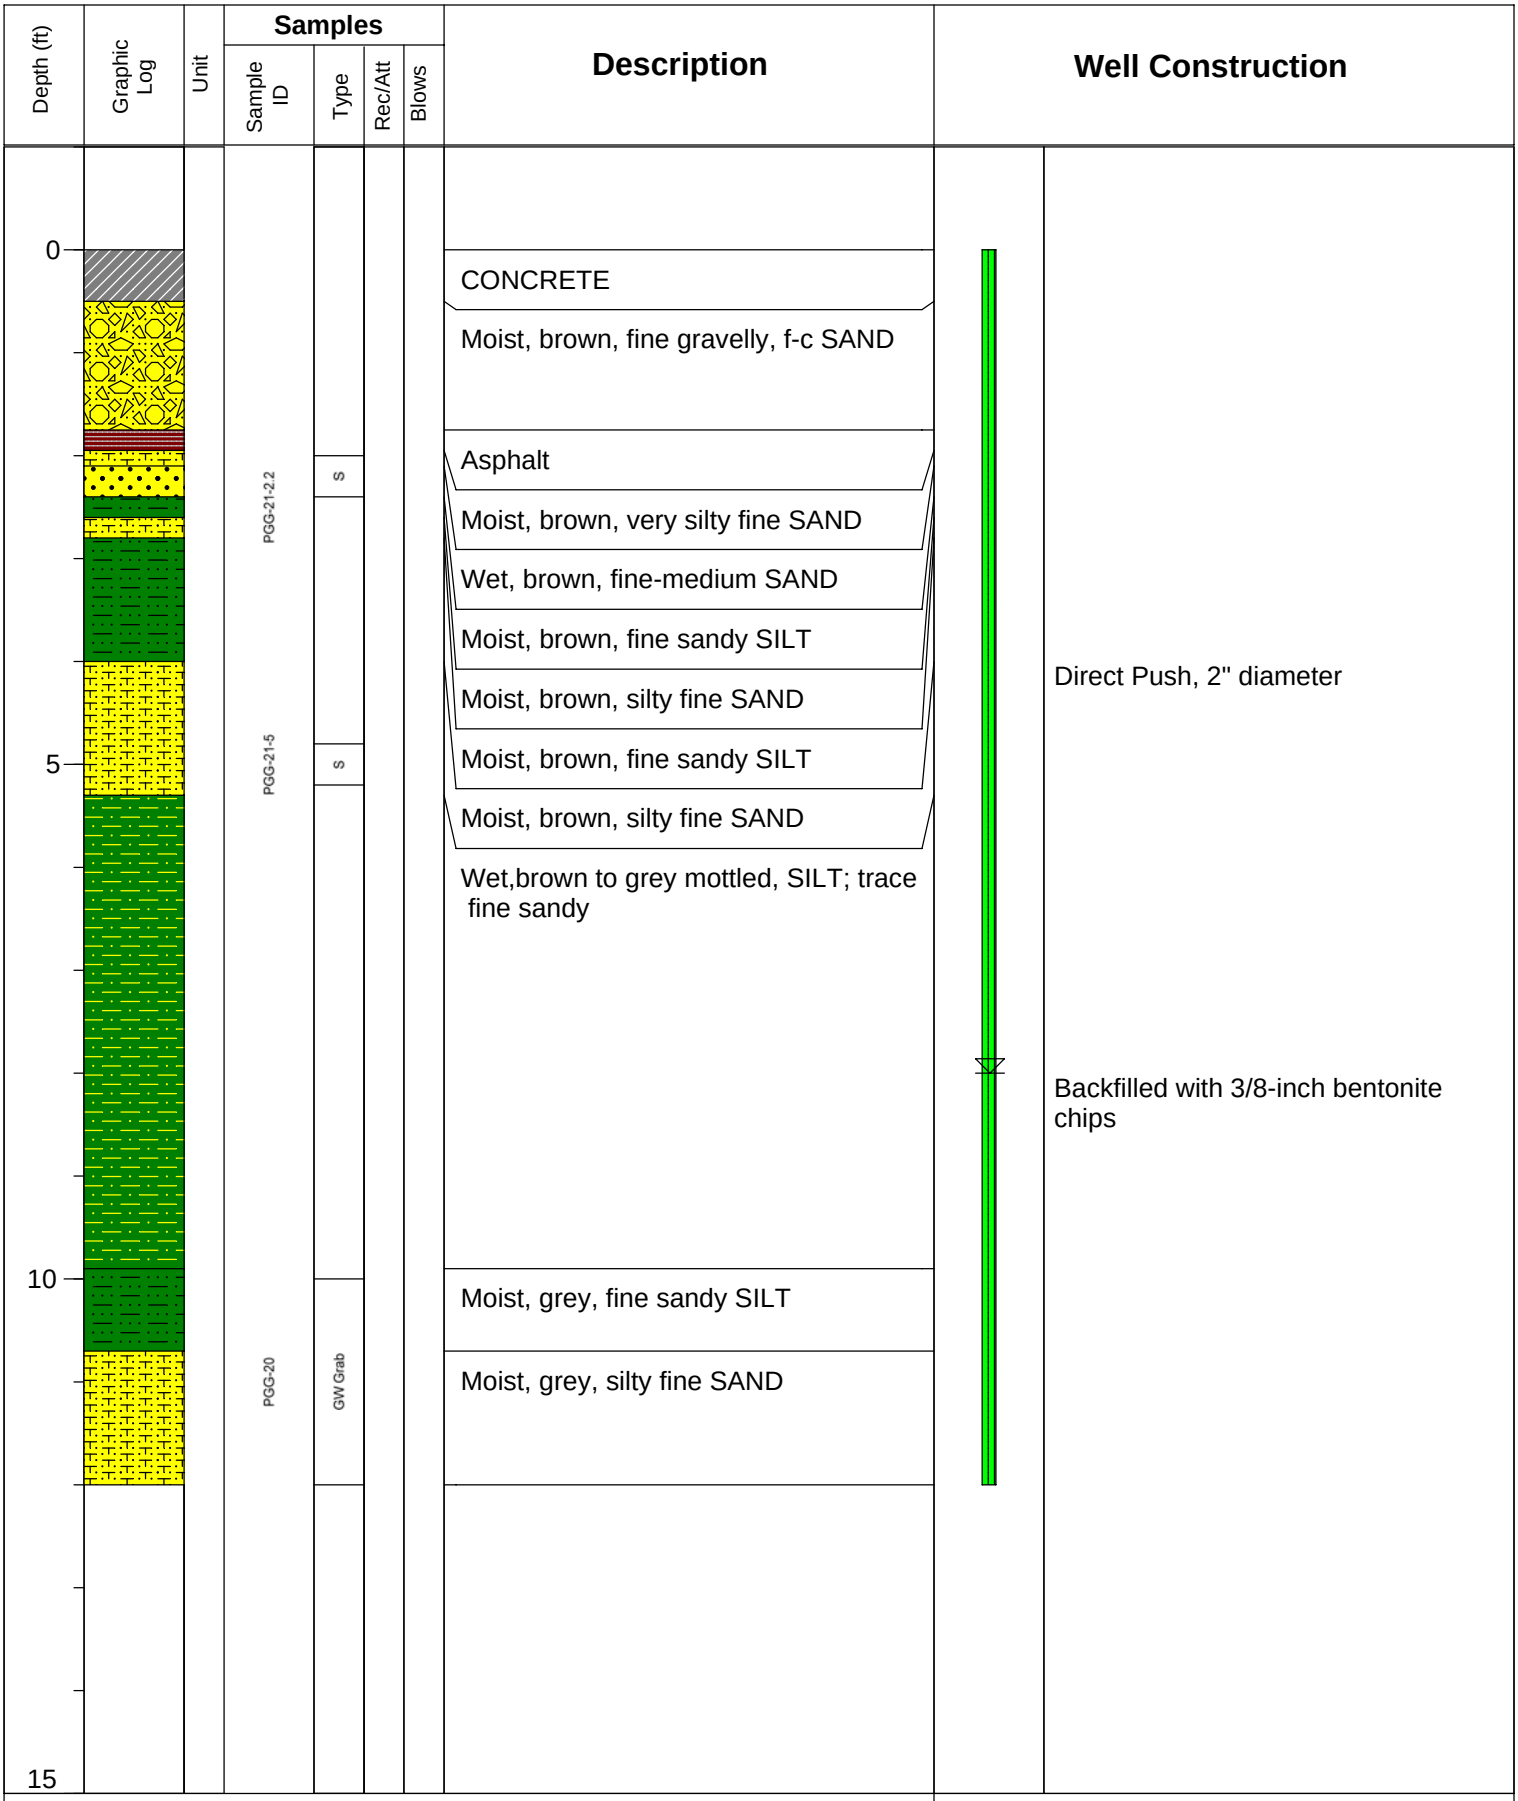


Address: 5700 3rd Ave S
City, State: Seattle, WA
Tax Parcel ID: 172280-1495
Location (TRS): T24N R4W S20; NE1/4 of SW1/4
Lat/Long: N 204799.5 ft, E 1270653 ft
Consulting Firm: Pacific Groundwater Group
Logged by: G. Mutti

Drilling Firm: ESN NW
Drilling Method: Direct Push
Ecology ID: NA
DTW: ~8 ft bmp
MP Elevation: ft
V. Datum: NAVD 88
Date: 8/3/2007

Figure
Boring Log
PGG-21

Blaser Die Casting
Remedial Investigation
JK0504.03

PGG

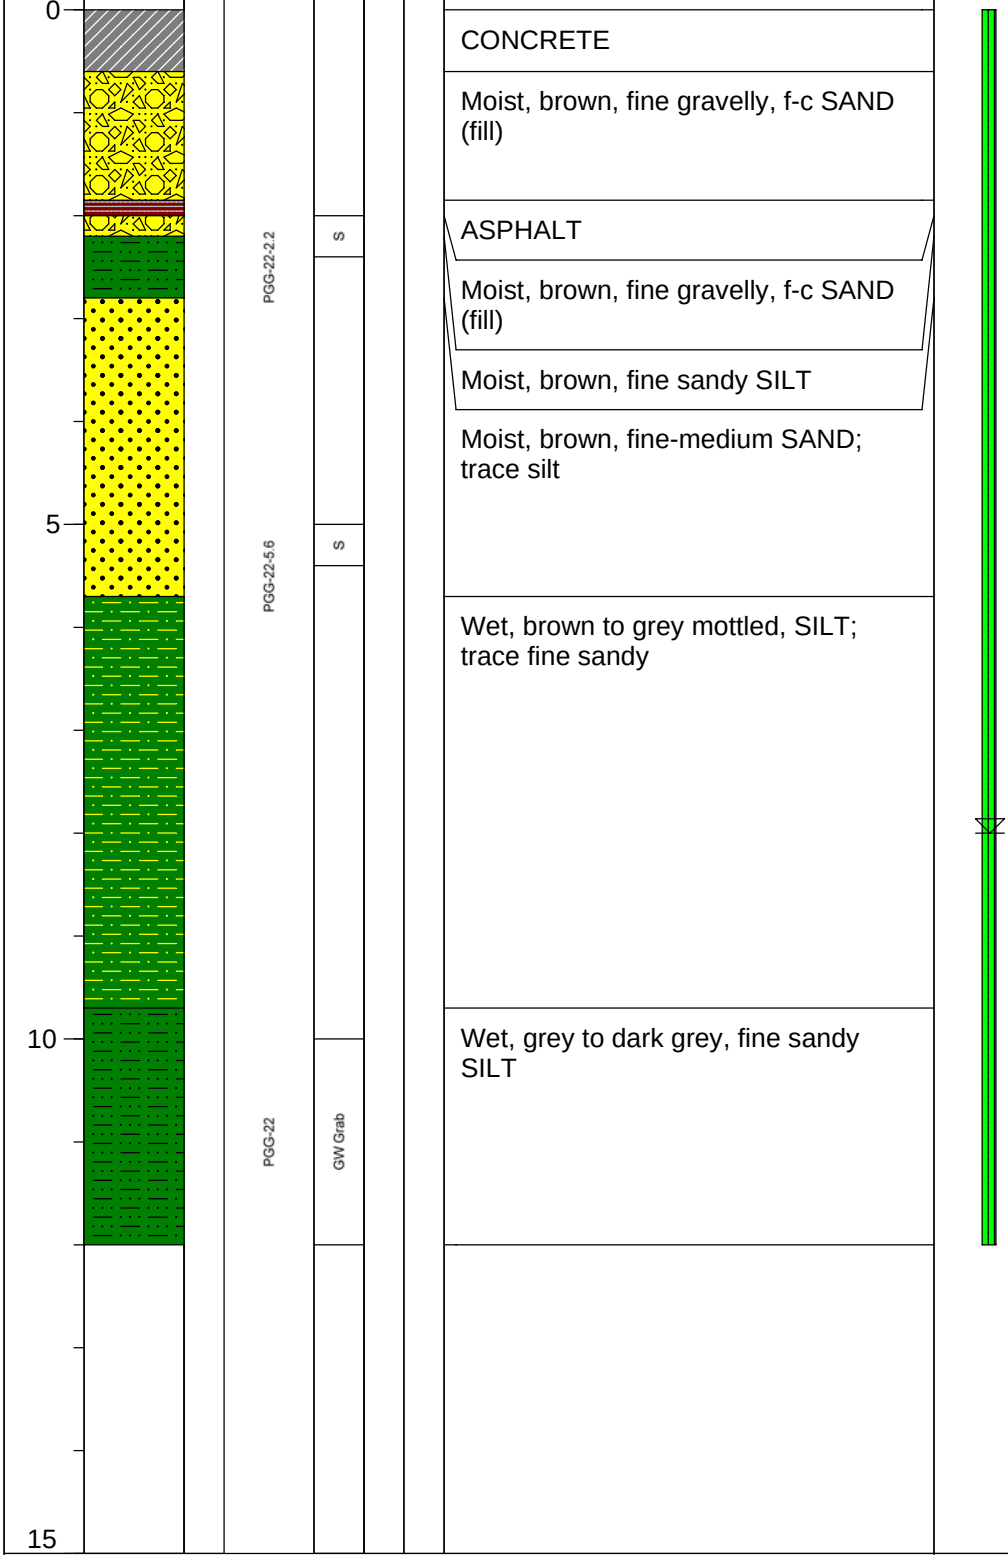


Address: 5700 3rd Ave S
City, State: Seattle, WA
Tax Parcel ID: 172280-1495
Location (TRS): T24N R4W S20; NE1/4 of SW1/4
Lat/Long: N 204791 ft, E 1270653 ft
Consulting Firm: Pacific Groundwater Group
Logged by: G. Mutti

Drilling Firm: ESN NW
Drilling Method: Direct Push
Ecology ID: NA
DTW: ~8 ft bmp
MP Elevation: ft
V. Datum: NAVD 88
Date: 8/3/2007

Figure
Boring Log
PGG-22

Blaser Die Casting
Remedial Investigation
JK0504.03

PGG

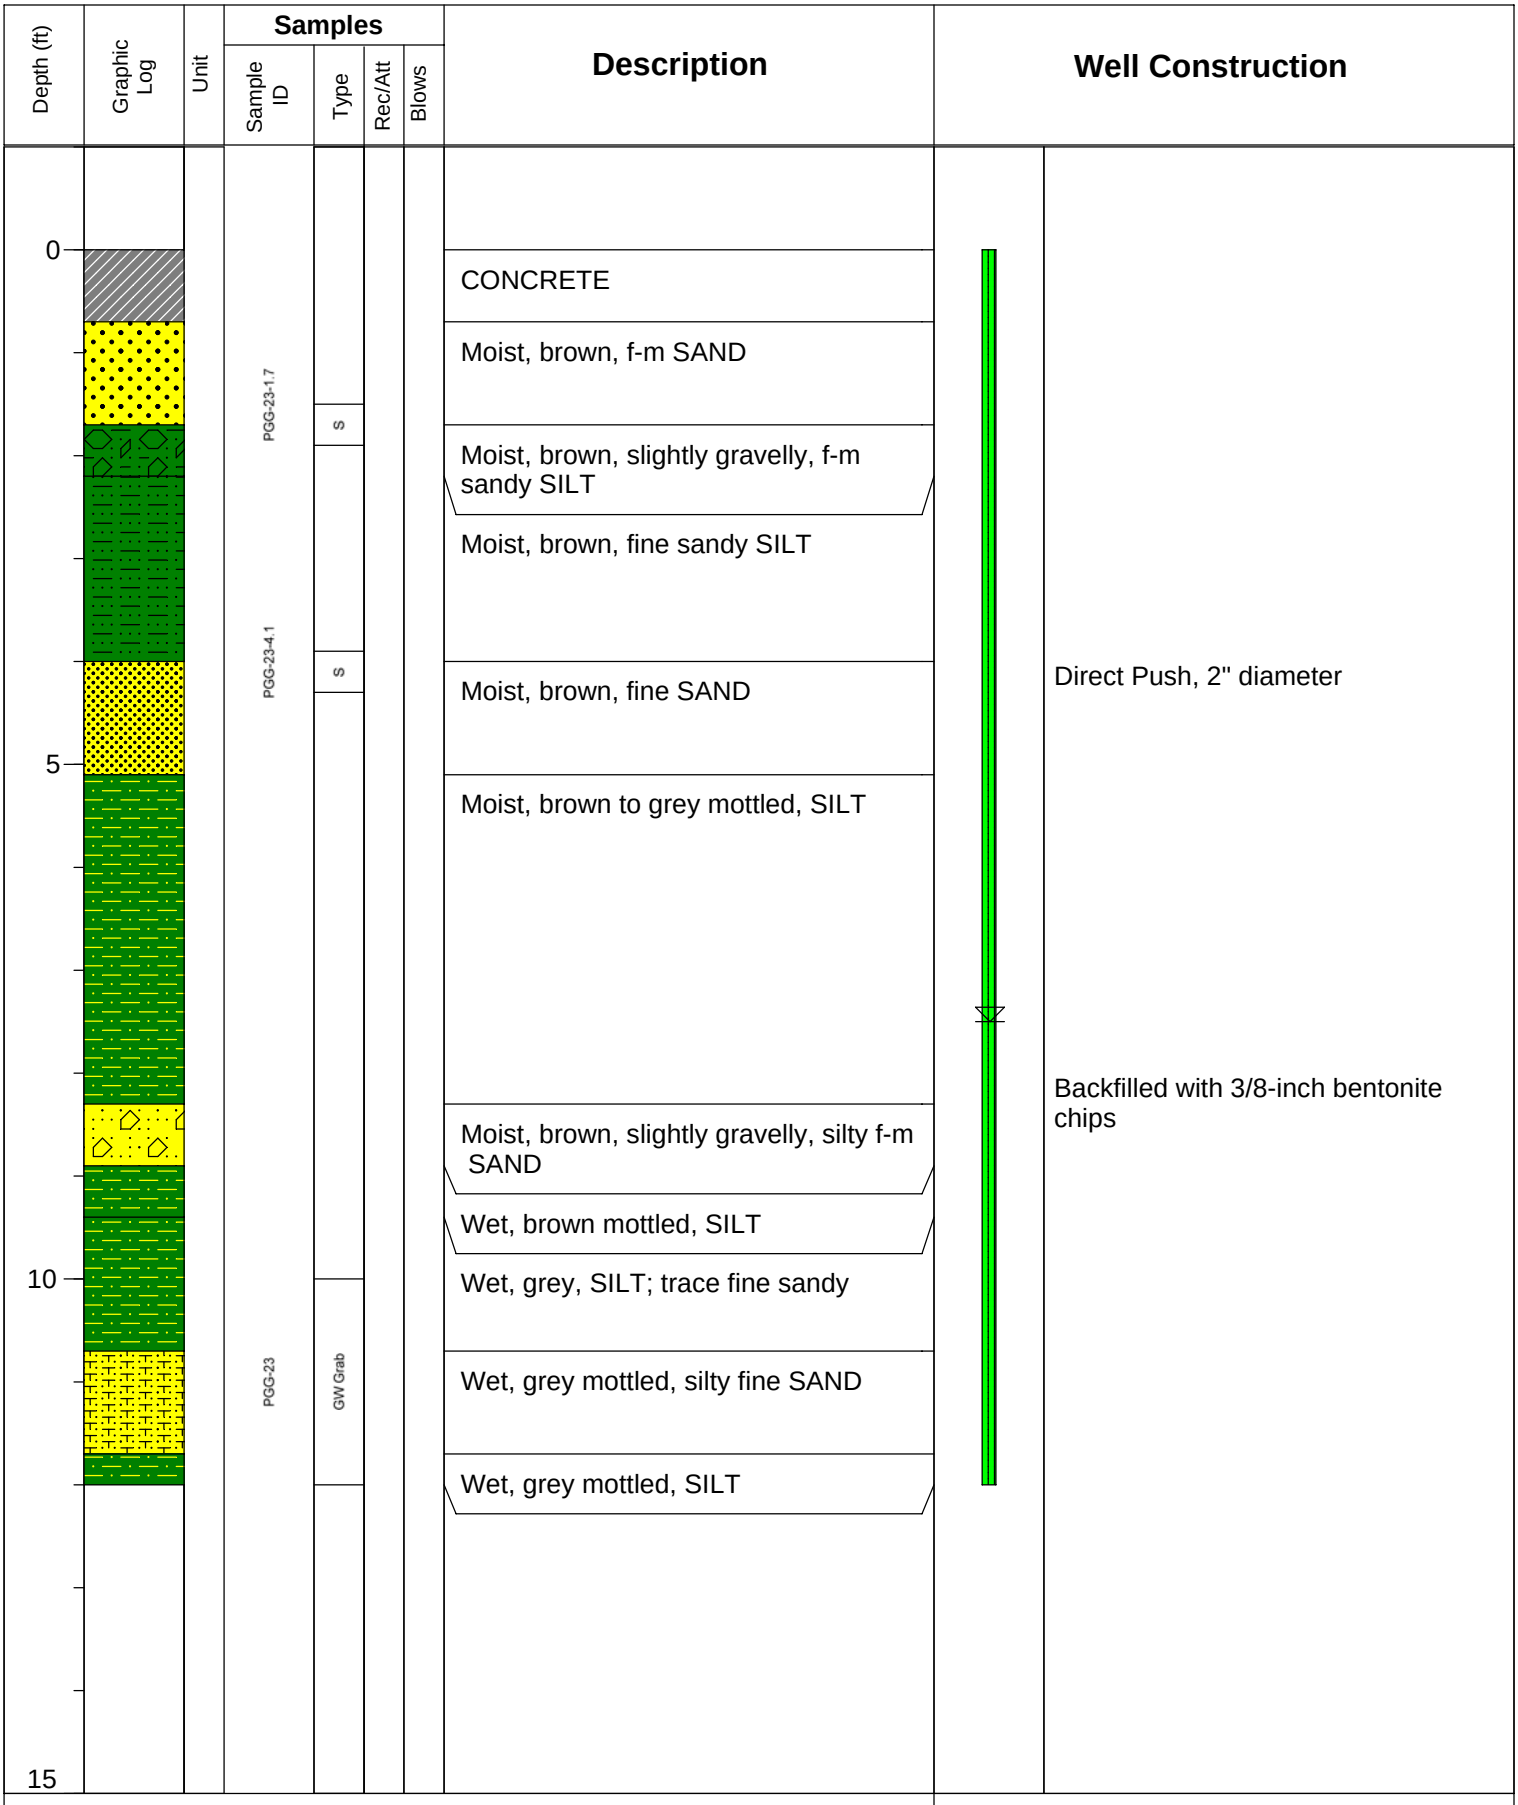


Address: 5700 3rd Ave S
City, State: Seattle, WA
Tax Parcel ID: 172280-1495
Location (TRS): T24N R4W S20; NE1/4 of SW1/4
Lat/Long: N 204791 ft, E 1270681 ft
Consulting Firm: Pacific Groundwater Group
Logged by: G. Mutti

Drilling Firm: ESN NW
Drilling Method: Direct Push
Ecology ID: NA
DTW: ~7.5 ft bmp
MP Elevation: ft
V. Datum: NAVD 88
Date: 8/3/2007

Figure
Boring Log
PGG-23

Blaser Die Casting
Remedial Investigation
JK0504.03

PGG

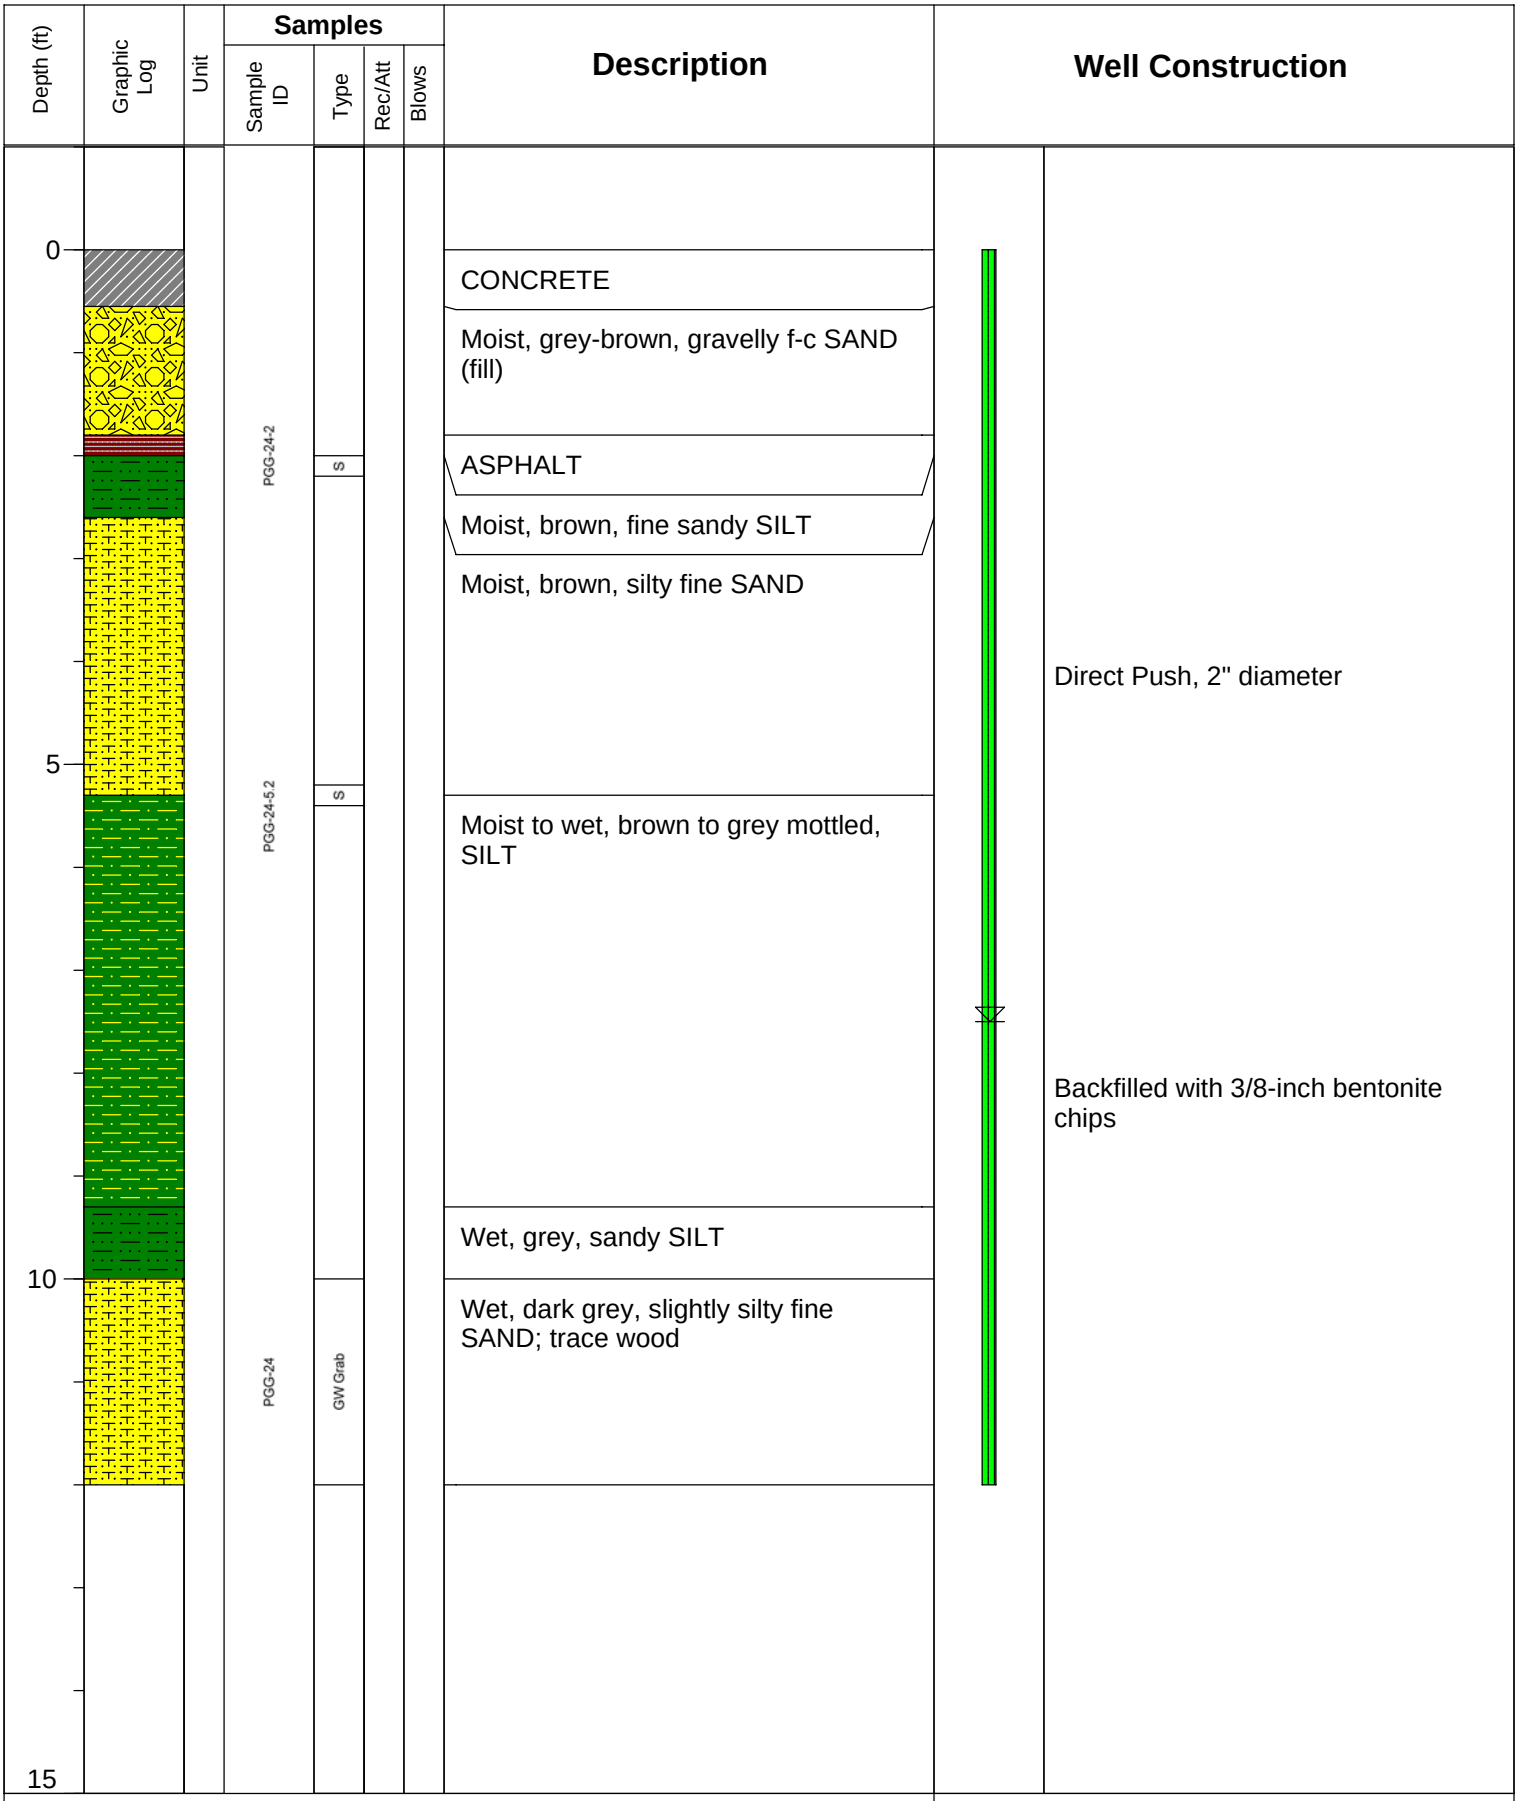


Address: 5700 3rd Ave S
City, State: Seattle, WA
Tax Parcel ID: 172280-1495
Location (TRS): T24N R4W S20; NE1/4 of SW1/4
Lat/Long: N 204775 ft, E 1270657 ft
Consulting Firm: Pacific Groundwater Group
Logged by: G. Mutti

Drilling Firm: ESN NW
Drilling Method: Direct Push
Ecology ID: NA
DTW: ~8 ft bmp
MP Elevation: ft
V. Datum: NAVD 88
Date: 8/3/2007

Figure
Boring Log
PGG-24

Blaser Die Casting
Remedial Investigation
JK0504.03

PGG

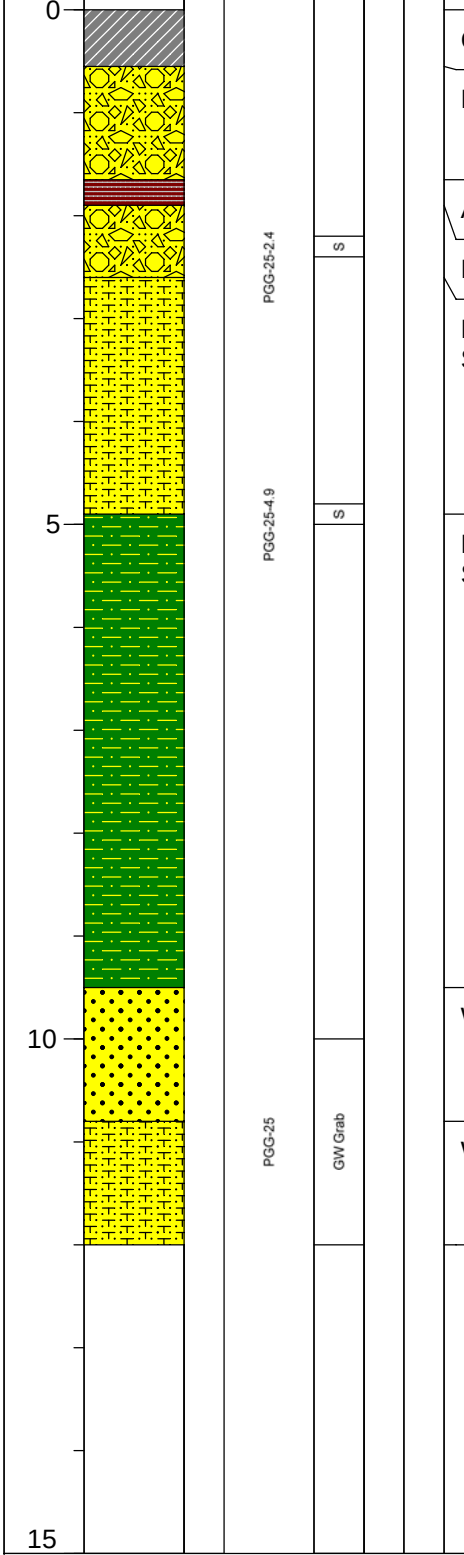

Description

CONCRETE

Moist, brown, gravelly f-c SAND (fill)

ASPHALT

Moist, brown, gravelly f-c SAND (fill)

Moist, brown, trace to slightly silty fine SAND

Moist to wet, brown to grey mottled, SILT

Wet, grey, fine to medium SAND

Wet, grey, slightly silty fine SAND

Well Construction



Direct Push, 2" diameter

Backfilled with 3/8-inch bentonite chips


Address: 5700 3rd Ave S
City, State: Seattle, WA
Tax Parcel ID: 172280-1495
Location (TRS): T24N R4W S20; NE1/4 of SW1/4
Lat/Long: N 204769 ft, E 1270677 ft
Consulting Firm: Pacific Groundwater Group
Logged by: G. Mutti

Drilling Firm: ESN NW
Drilling Method: Direct Push
Ecology ID: NA
DTW: ~8 ft bmp
MP Elevation: ft
V. Datum: NAVD 88
Date: 8/3/2007

Figure
Boring Log
PGG-25

Blaser Die Casting
Remedial Investigation
JK0504.03

PGG

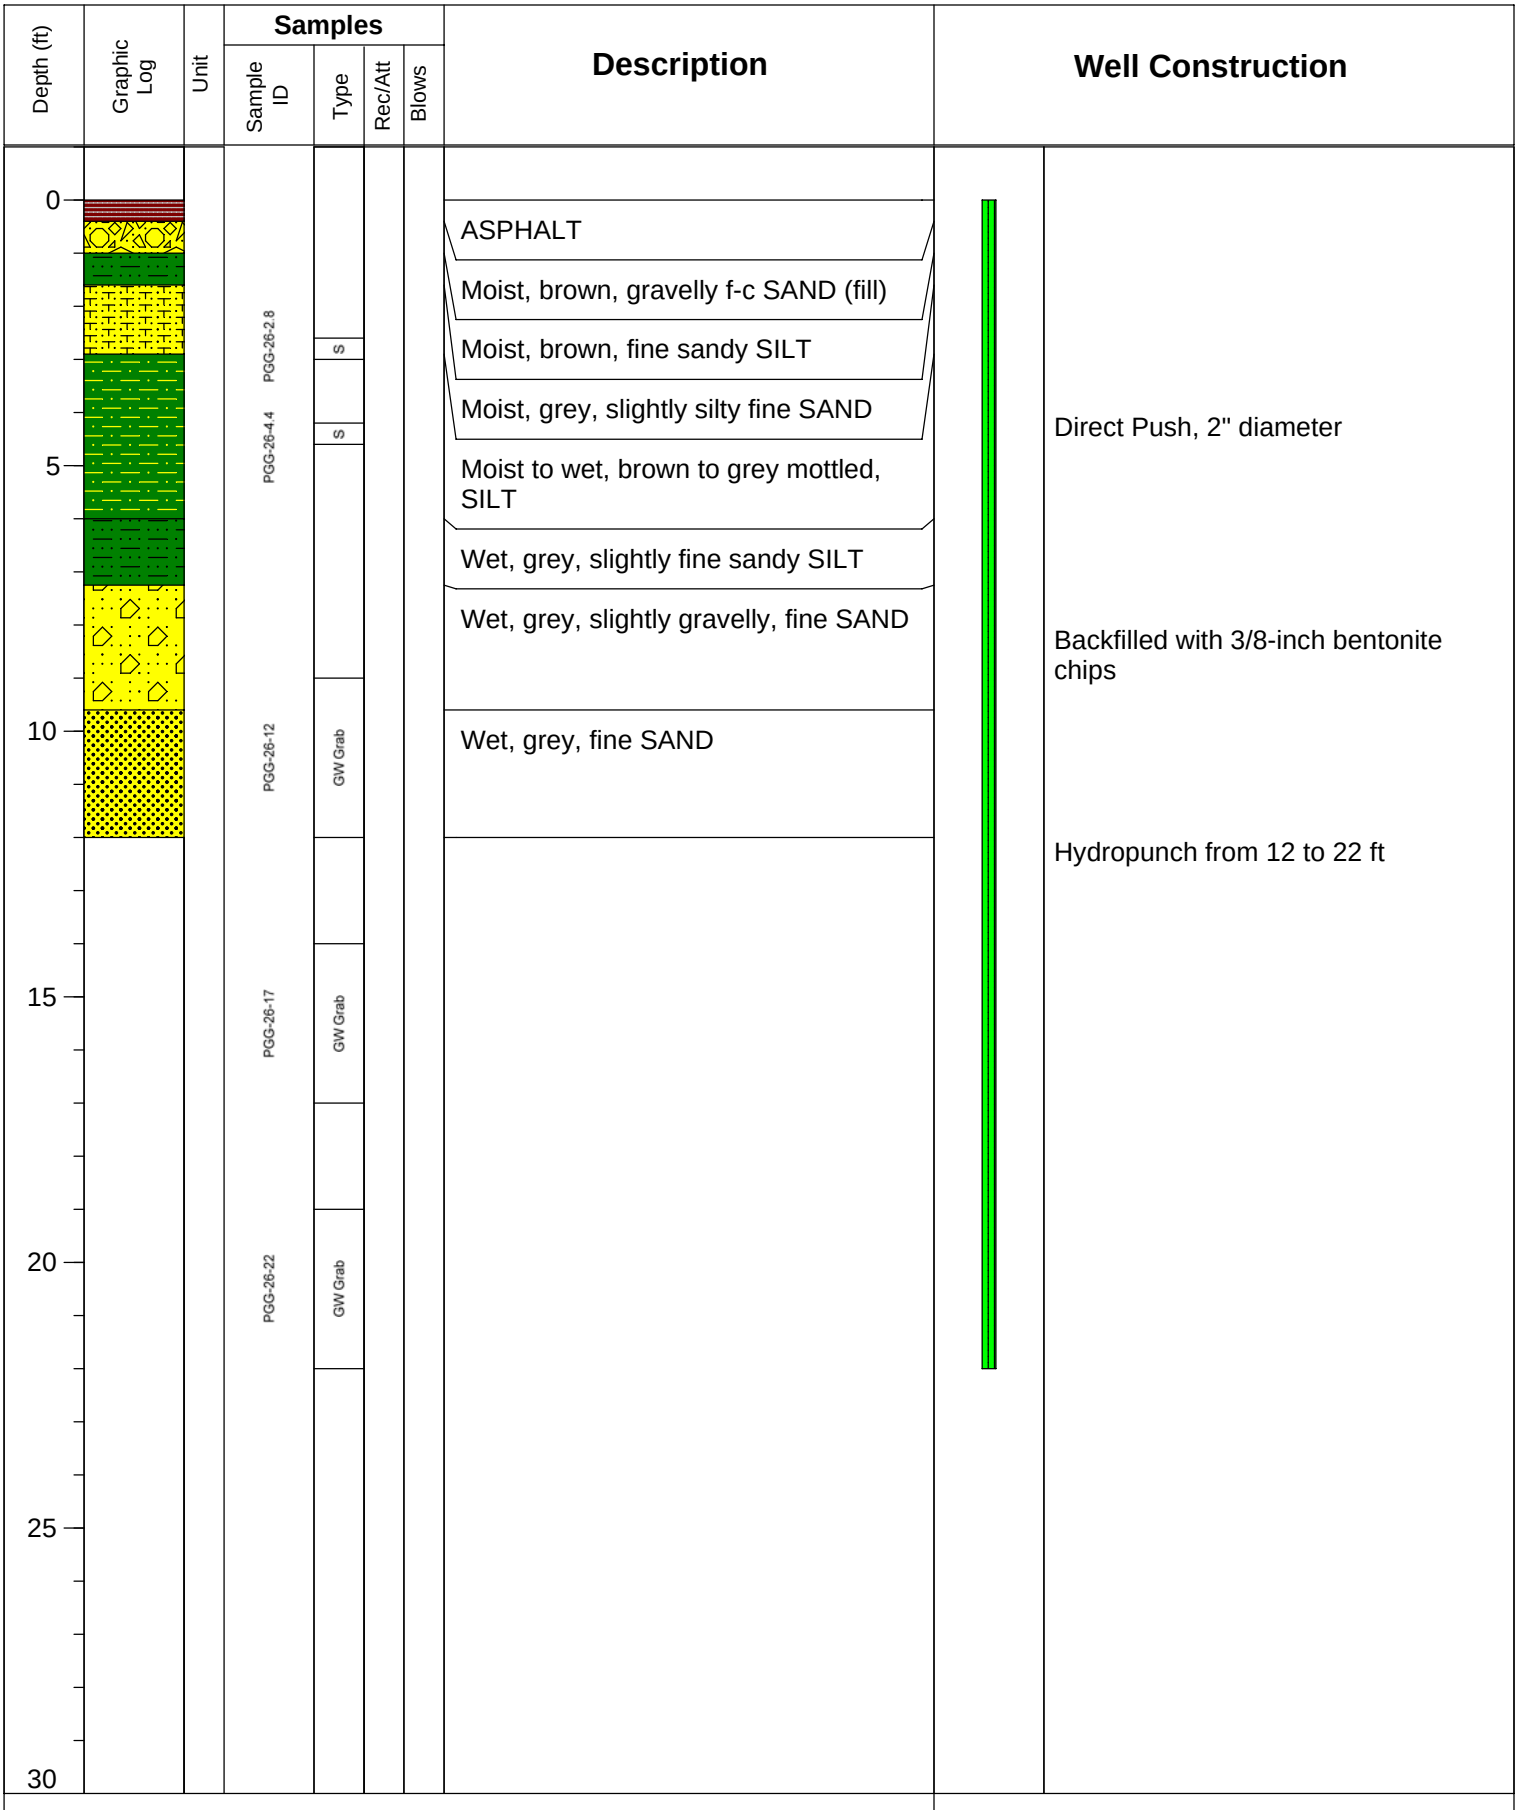

Address: 5700 3rd Ave S
City, State: Seattle, WA
Tax Parcel ID: 172280-1495
Location (TRS): T24N R4W S20; NE1/4 of SW1/4
Lat/Long: N 204753 ft, E 1270641 ft
Consulting Firm: Pacific Groundwater Group
Logged by: G. Mutti

Drilling Firm: ESN NW
Drilling Method: Direct Push
Ecology ID: NA
DTW: ft bmp
MP Elevation: ft
V. Datum: NAVD 88
Date: 8/3/2007

Figure
Boring Log
PGG-26

Blaser Die Casting
Remedial Investigation
JK0504.03

PGG

Depth (ft)	Graphic Log	Unit	Samples: Sample ID	Samples: Type	Samples: Rec/Att	Samples: Blows	Description	Well Construction
0								
5								Hydropunch, 2" diameter
10			PGG-27-10	GW Grab				Backfilled with 3/8-inch bentonite chips
15			PGG-27-15	GW Grab				
20			PGG-27-20	GW Grab				
25			PGG-27-25	GW Grab				
30			PGG-27-30	GW Grab				
35								Total Depth = 33 ft


Address: 202-228 S Mead St
City, State: Seattle, WA
Tax Parcel ID: 172280-1750
Location (TRS): T24N R4W S20; NE1/4 of SW1/4
Lat/Long: N 204678.1 ft, E 1270373 ft
Consulting Firm: Pacific Groundwater Group
Logged by: G. Wallace

Drilling Firm: ESN NW
Drilling Method: Direct Push
Ecology ID: NA
DTW: NA ft bmp
MP Elevation: 17.2 ft
V. Datum: NAVD 88
Date: 11/5/2007

Figure
Boring Log
PGG-27

Blaser Die Casting
Remedial Investigation
JK0504.03

PGG

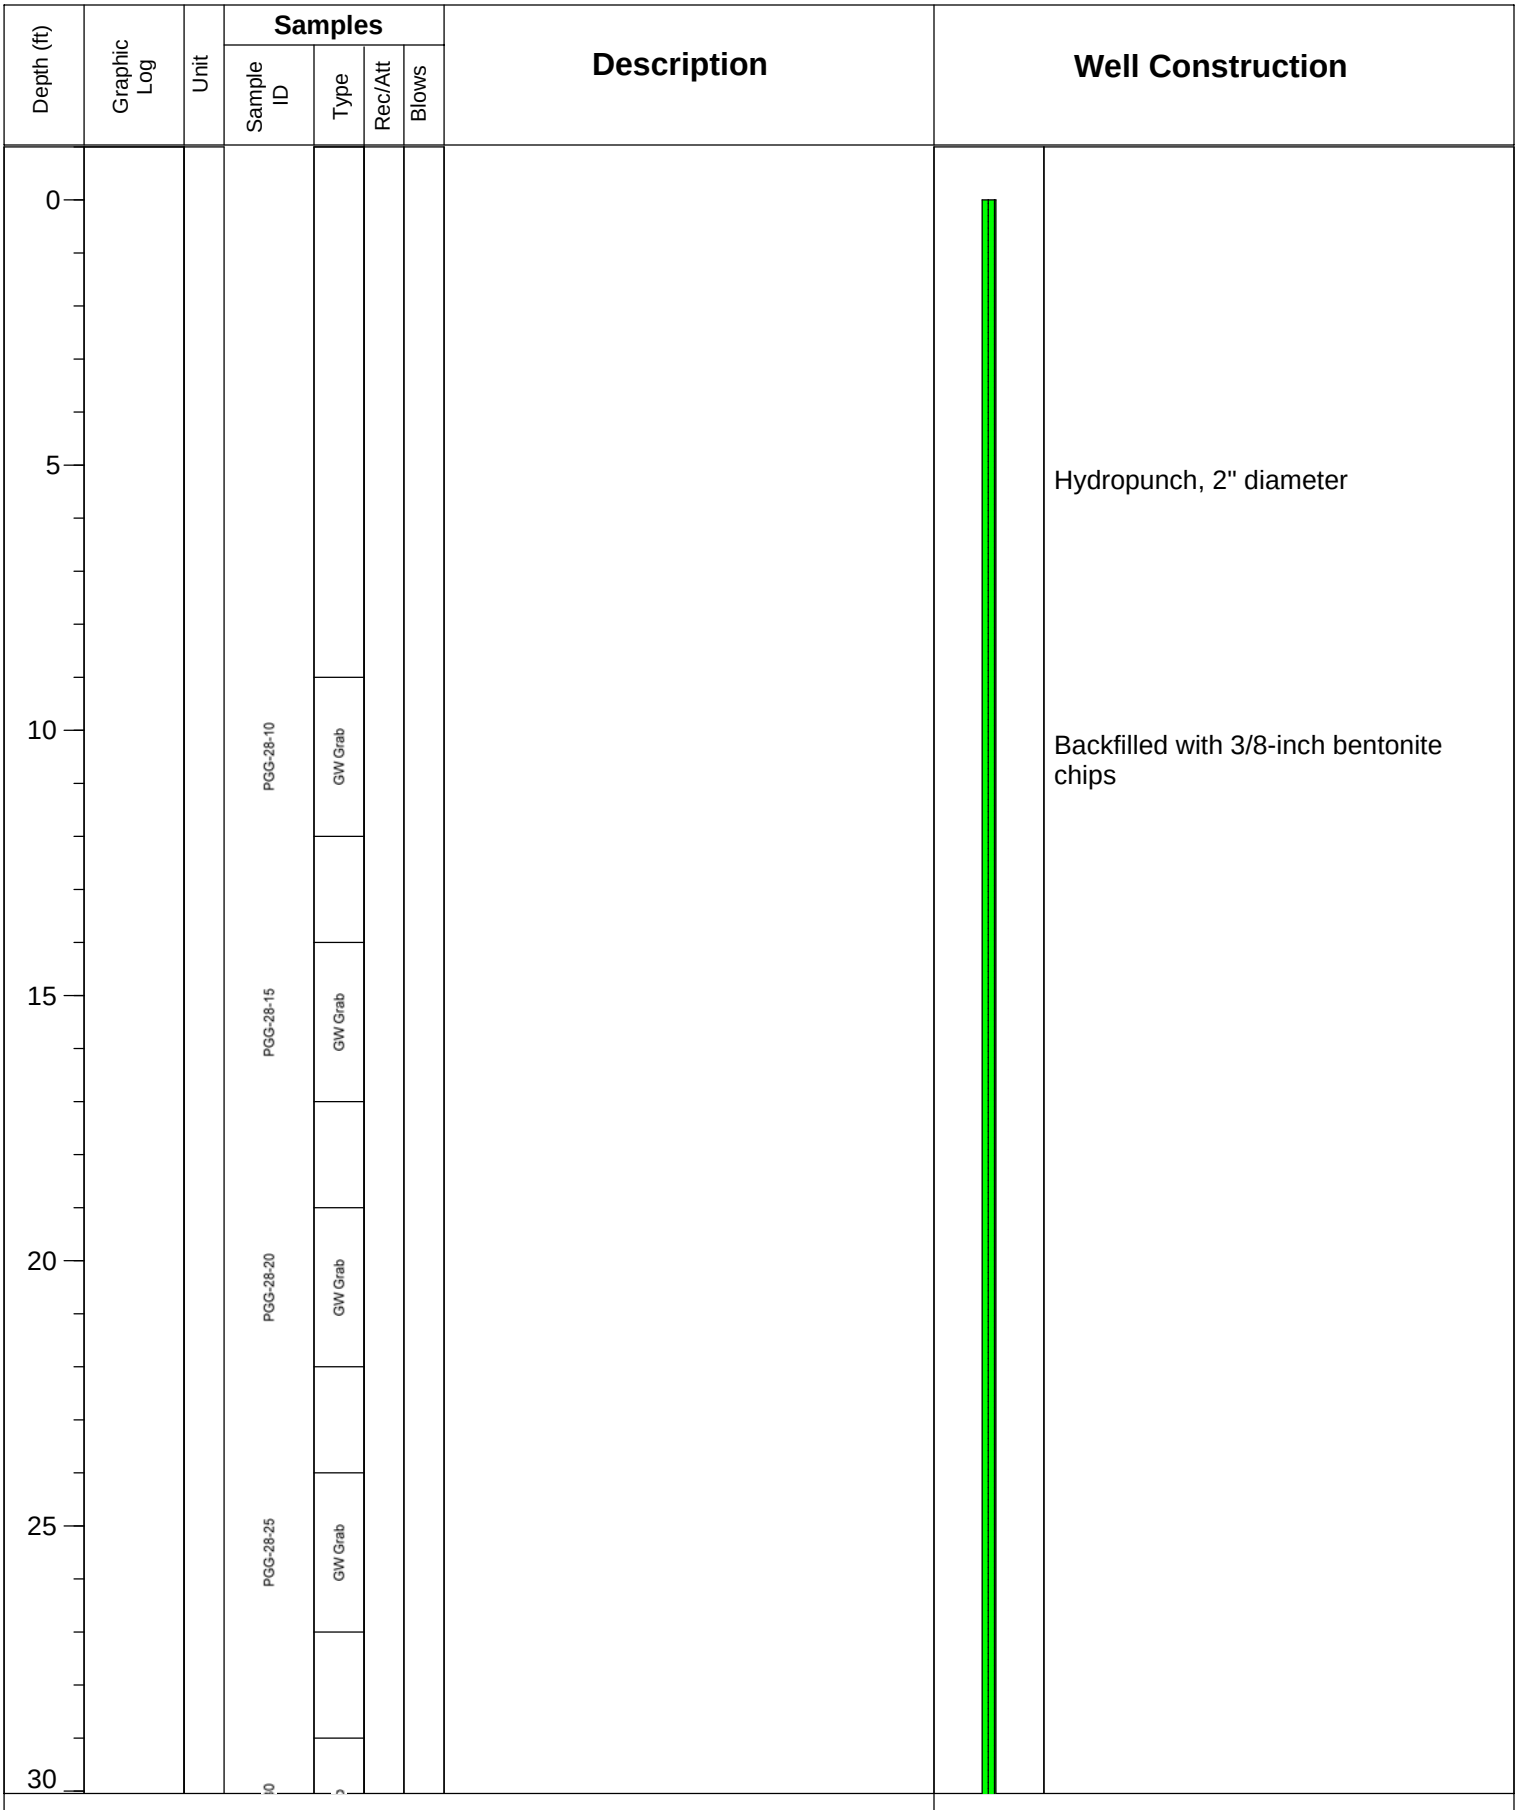

Address: 202-228 S Mead St
City, State: Seattle, WA
Tax Parcel ID: 172280-1750
Location (TRS): T24N R4W S20; NE1/4 of SW1/4
Lat/Long: N 204665.7 ft, E 1270412 ft
Consulting Firm: Pacific Groundwater Group
Logged by: G. Wallace

Drilling Firm: ESN NW
Drilling Method: Direct Push
Ecology ID: NA
DTW: NA ft bmp
MP Elevation: 17.2 ft
V. Datum: NAVD 88
Date: 11/5/2007

Figure
Boring Log
PGG-28

Blaser Die Casting
Remedial Investigation
JK0504.03

PGG

Depth (ft)	Graphic Log	Unit	Samples: Sample ID	Samples: Type	Samples: Rec/Att	Samples: Blows	Description	Well Construction
35			PGG-28-35	GW Grab				Hydropunch, 2" diameter
40			PGG-28-40	GW Grab				Backfilled with 3/8-inch bentonite chips Total Depth = 42 ft
45								
50								
55								
60								


Address: 202-228 S Mead St
City, State: Seattle, WA
Tax Parcel ID: 172280-1750
Location (TRS): T24N R4W S20; NE1/4 of SW1/4
Lat/Long: N 204665.7 ft, E 1270412 ft
Consulting Firm: Pacific Groundwater Group
Logged by: G. Wallace

Drilling Firm: ESN NW
Drilling Method: Direct Push
Ecology ID: NA
DTW: NA ft bmp
MP Elevation: 17.2 ft
V. Datum: NAVD 88
Date: 11/5/2007

Figure
Boring Log
PGG-28

Blaser Die Casting
Remedial Investigation
JK0504.03

PGG

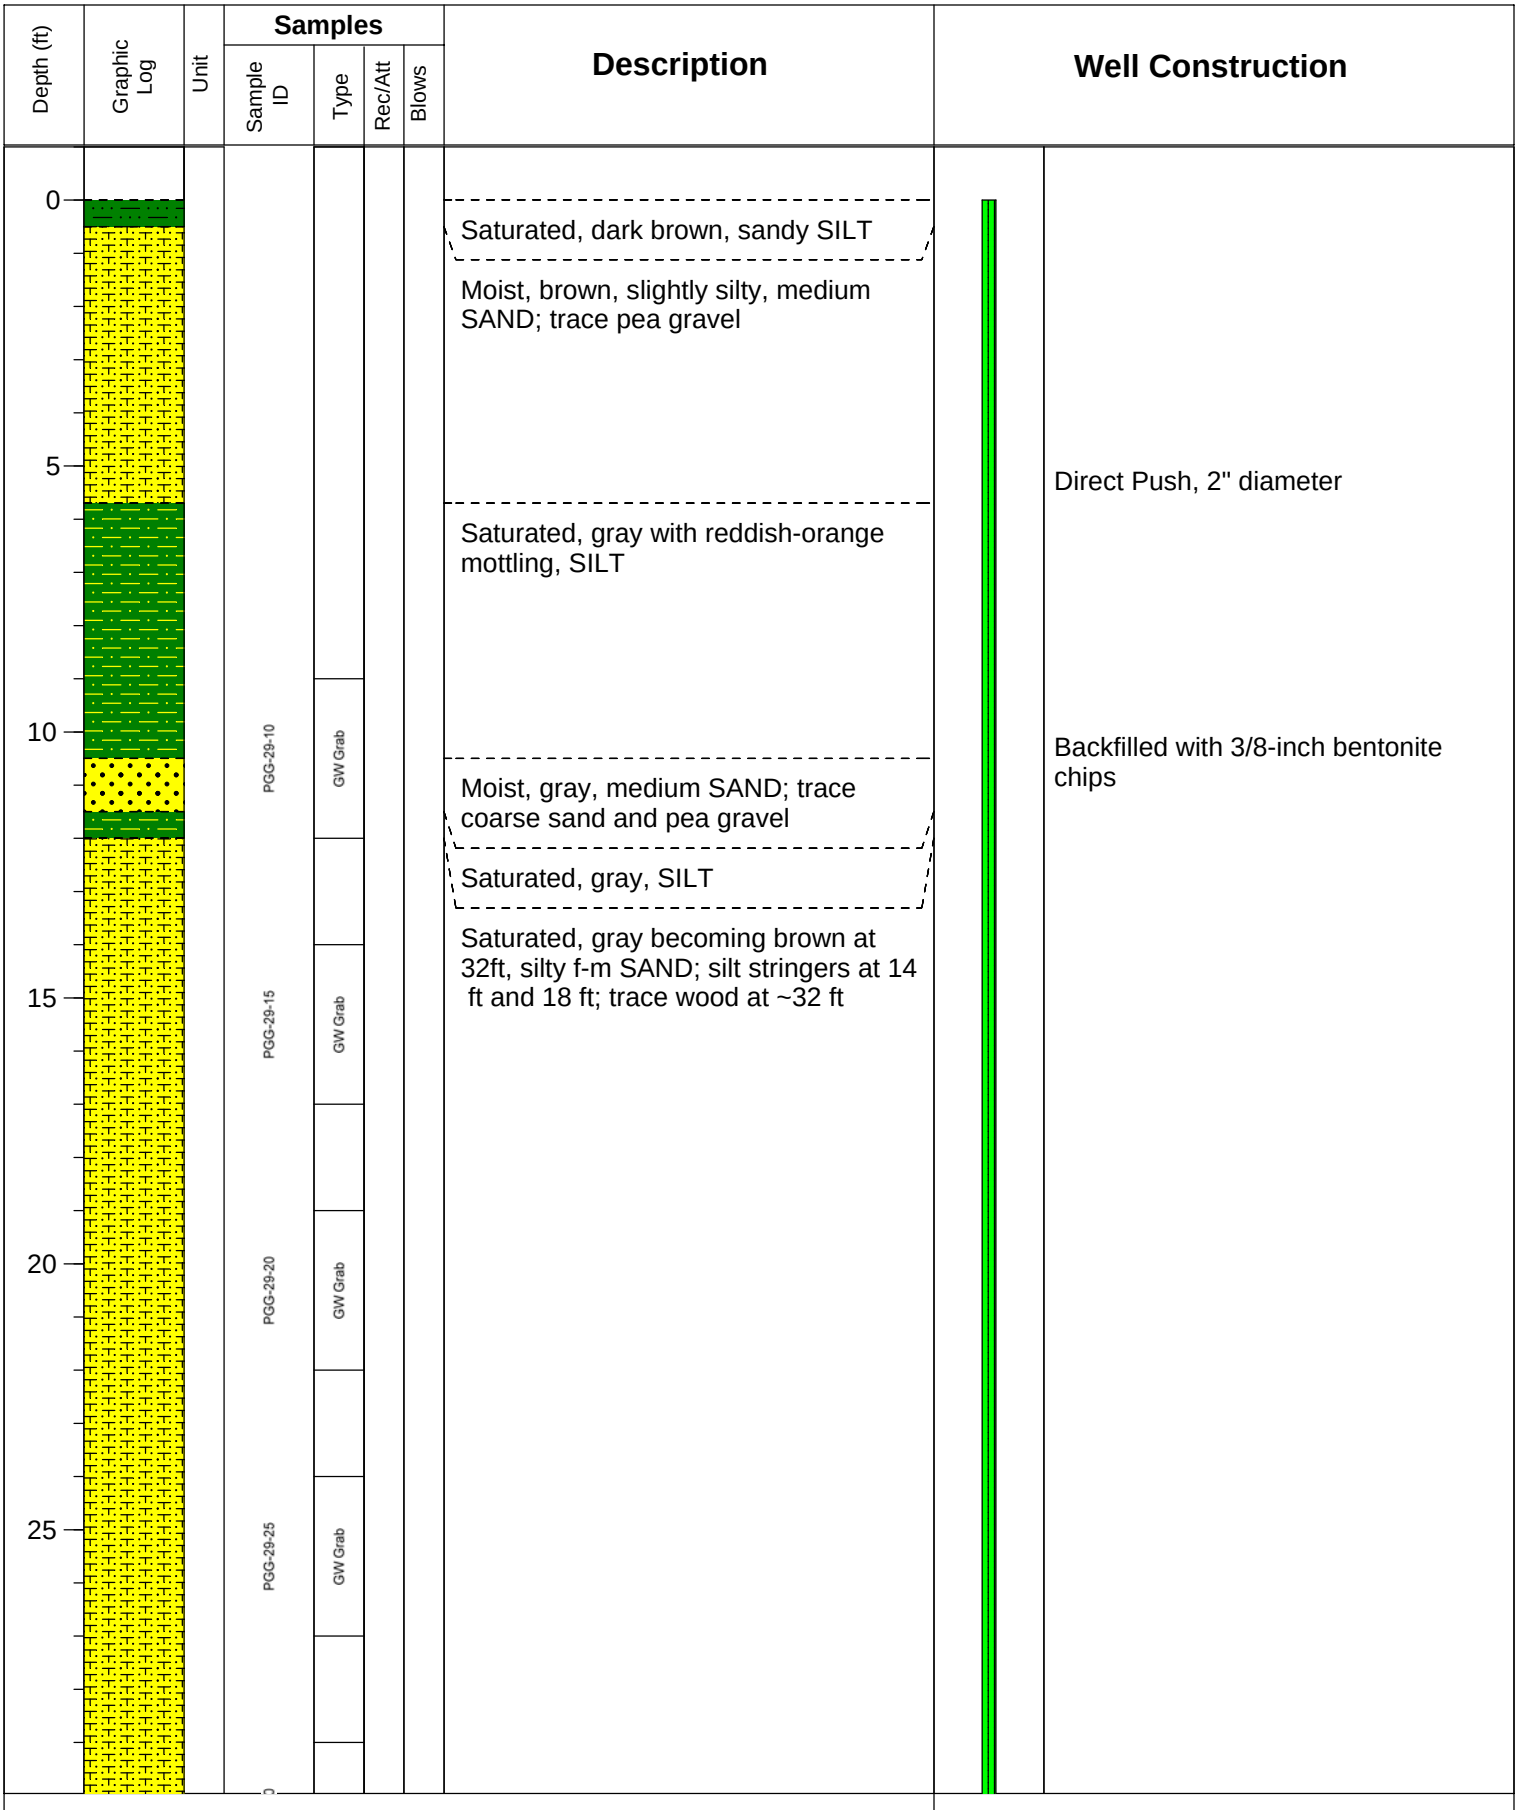


Address: 202-228 S Mead St
City, State: Seattle, WA
Tax Parcel ID: 172280-1750
Location (TRS): T24N R4W S20; NE1/4 of SW1/4
Lat/Long: N 204653.6 ft, E 1270453 ft
Consulting Firm: Pacific Groundwater Group
Logged by: G. Wallace

Drilling Firm: ESN NW
Drilling Method: Direct Push
Ecology ID: NA
DTW: NA ft bmp
MP Elevation: 17.2 ft
V. Datum: NAVD 88
Date: 11/6/2007

Figure
Boring Log
PGG-29

Blaser Die Casting
Remedial Investigation
JK0504.03

PGG

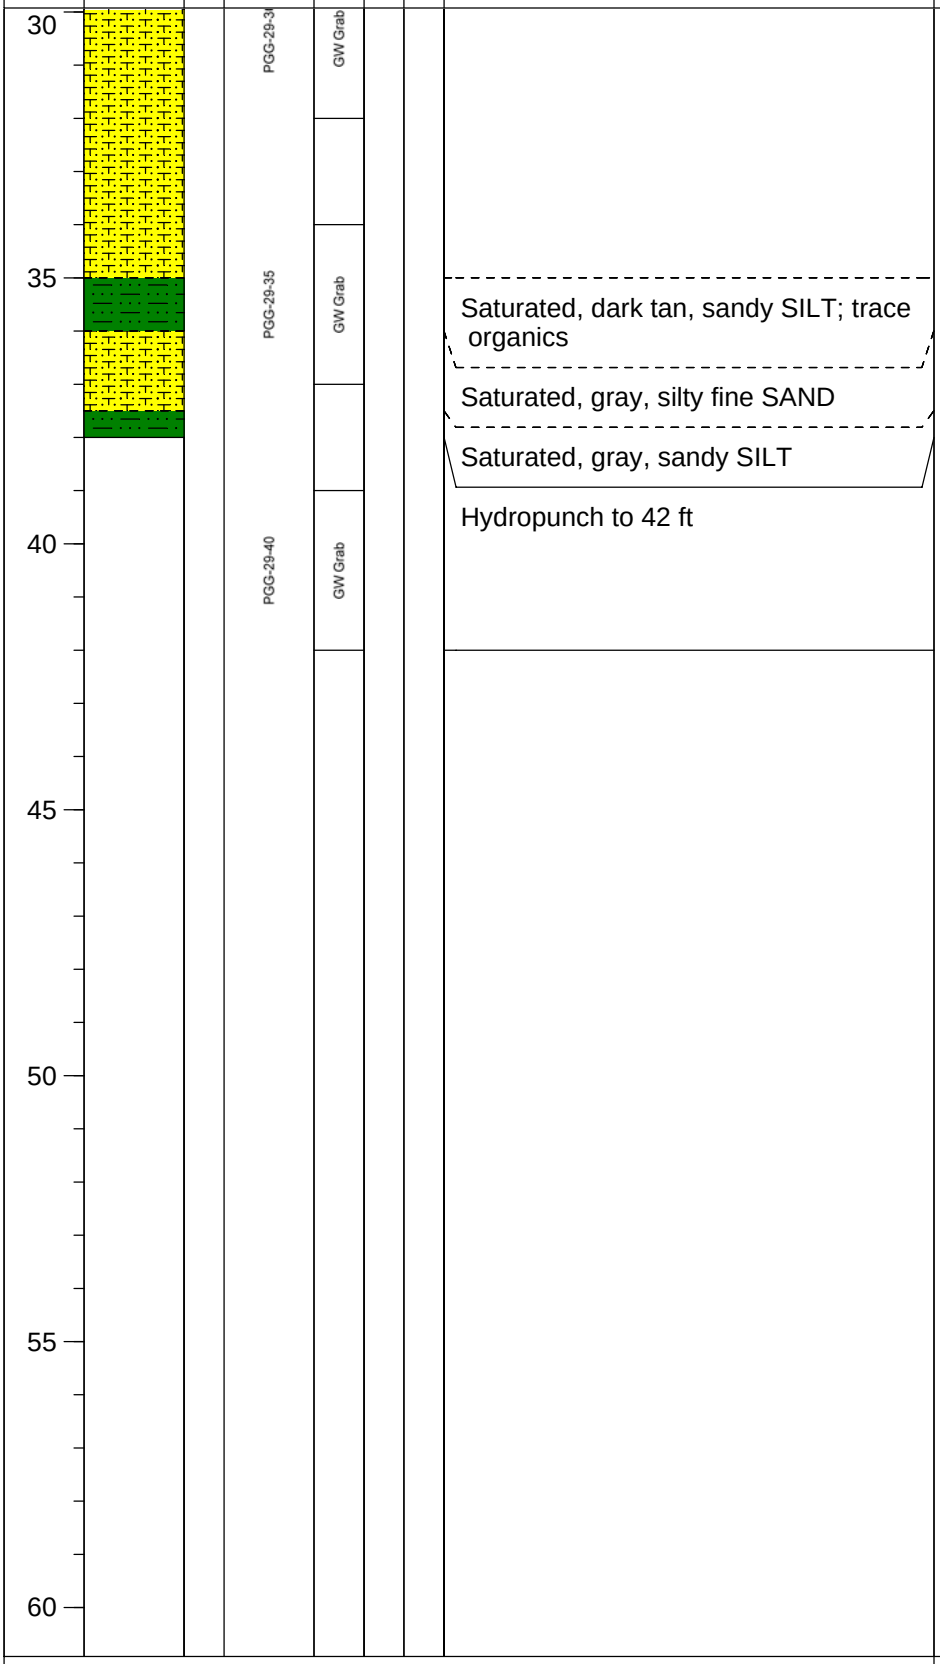

Address: 202-228 S Mead St
City, State: Seattle, WA
Tax Parcel ID: 172280-1750
Location (TRS): T24N R4W S20; NE1/4 of SW1/4
Lat/Long: N 204653.6 ft, E 1270453 ft
Consulting Firm: Pacific Groundwater Group
Logged by: G. Wallace


Drilling Firm: ESN NW
Drilling Method: Direct Push
Ecology ID: NA
DTW: NA ft bmp
MP Elevation: 17.2 ft
V. Datum: NAVD 88
Date: 11/6/2007

Figure
Boring Log
PGG-29

Blaser Die Casting
Remedial Investigation
JK0504.03

PGG

Depth (ft)	Graphic Log	Unit	Samples: Sample ID	Samples: Type	Samples: Rec/Att	Samples: Blows	Description	Well Construction
0								
5								Hydropunch, 2" diameter
10			PGG-30-10	GW Grab				Backfilled with 3/8-inch bentonite chips
15			PGG-30-15	GW Grab				
20			PGG-30-20	GW Grab				
25			PGG-30-25	GW Grab				



Address: 202-228 S Mead St
City, State: Seattle, WA
Tax Parcel ID: 172280-1750
Location (TRS): T24N R4W S20; NE1/4 of SW1/4
Lat/Long: N 204646.7 ft, E 1270504 ft
Consulting Firm: Pacific Groundwater Group
Logged by: G. Wallace

Drilling Firm: ESN NW
Drilling Method: Direct Push
Ecology ID: NA
DTW: NA ft bmp
MP Elevation: 16.8 ft
V. Datum: NAVD 88
Date: 11/7/2007

Figure
Boring Log
PGG-30

Blaser Die Casting
Remedial Investigation
JK0504.03

PGG

Depth (ft)	Graphic Log	Unit	Samples: Sample ID	Samples: Type	Samples: Rec/Att	Samples: Blows	Description	Well Construction
30			PGG-30-30	GW Grab				
35			PGG-30-35	GW Grab				Hydropunch, 2" diameter
40			PGG-30-40	GW Grab				Backfilled with 3/8-inch bentonite chips Total Depth = 42 ft
45								
50								
55								
60								

Address: 202-228 S Mead St
City, State: Seattle, WA
Tax Parcel ID: 172280-1750
Location (TRS): T24N R4W S20; NE1/4 of SW1/4
Lat/Long: N 204646.7 ft, E 1270504 ft
Consulting Firm: Pacific Groundwater Group
Logged by: G. Wallace

Drilling Firm: ESN NW
Drilling Method: Direct Push
Ecology ID: NA
DTW: NA ft bmp
MP Elevation: 16.8 ft
V. Datum: NAVD 88
Date: 11/7/2007

Figure
Boring Log
PGG-30

Blaser Die Casting
Remedial Investigation
JK0504.03

PGG

Depth (ft)	Graphic Log	Unit	Samples: Sample ID	Samples: Type	Samples: Rec/Att	Samples: Blows	Description	Well Construction
0			PGG-31-WT	GW Grab				Hydropunch, 2" diameter
5								Backfilled with 3/8-inch bentonite chips
10								
15								Total Depth = 15 ft
20								
25								
30								

Address: 202-228 S Mead St
City, State: Seattle, WA
Tax Parcel ID: 172280-1750
Location (TRS): T24N R4W S20; NE1/4 of SW1/4
Lat/Long: N 204760.4 ft, E 1270481 ft
Consulting Firm: Pacific Groundwater Group
Logged by: G. Wallace

Drilling Firm: ESN NW
Drilling Method: Direct Push
Ecology ID: NA
DTW: NA ft bmp
MP Elevation: 15.3 ft
V. Datum: NAVD 88
Date: 11/6/2007

Figure
Boring Log
PGG-31

Blaser Die Casting
Remedial Investigation
JK0504.03

PgG

Depth (ft)	Graphic Log	Unit	Samples: Sample ID	Samples: Type	Samples: Rec/Att	Samples: Blows	Description	Well Construction
0								
5								Hydropunch, 2" diameter
10			PGG-32-WT	GW Grab				Backfilled with 3/8-inch bentonite chips
15								Total Depth = 15 ft
20								
25								
30								

Address: 202-228 S Mead St
City, State: Seattle, WA
Tax Parcel ID: 172280-1750
Location (TRS): T24N R4W S20; NE1/4 of SW1/4
Lat/Long: N 204760.5 ft, E 1270356 ft
Consulting Firm: Pacific Groundwater Group
Logged by: G. Wallace


Drilling Firm: ESN NW
Drilling Method: Direct Push
Ecology ID: NA
DTW: NA ft bmp
MP Elevation: 15.2 ft
V. Datum: NAVD 88
Date: 11/6/2007

Figure
Boring Log
PGG-32

Blaser Die Casting
Remedial Investigation
JK0504.03

PgG

Depth (ft)	Graphic Log	Unit	Samples: Sample ID	Samples: Type	Samples: Rec/Att	Samples: Blows	Description	Well Construction
0								
5								Hydropunch, 2" diameter
10			PGG-33B-10	GW Grab				Backfilled with 3/8-inch bentonite chips
15			PGG-33B-15	GW Grab				
20			PGG-33B-19	GW Grab				
25			PGG-33B-24	GW Grab				



Address: 5700 3rd Ave S
City, State: Seattle, WA
Tax Parcel ID: 172280-1495
Location (TRS): T24N R4W S20; NE1/4 of SW1/4
Lat/Long: N 204856.3 ft, E 1270917 ft
Consulting Firm: Pacific Groundwater Group
Logged by: G. Wallace

Drilling Firm: ESN NW
Drilling Method: Direct Push
Ecology ID: NA
DTW: NA ft bmp
MP Elevation: ~12 ft
V. Datum: NAVD 88
Date: 9/9/2008

Figure
Boring Log
PGG-33B

Blaser Die Casting
Remedial Investigation
JK0504.03

PgG

Depth (ft)	Graphic Log	Unit	Samples: Sample ID	Samples: Type	Samples: Rec/Att	Samples: Blows	Description	Well Construction
30			PGG-33B-30	GW Grab				
35			PGG-33B-34	GW Grab				
			PGG-33B-37	GW Grab				
40								Hydropunch, 2" diameter
			PGG-33B-42	GW Grab				
45								Backfilled with 3/8-inch bentonite chips
			PGG-33B-46	GW Grab				
50			PGG-33B-50	GW Grab				
55			PGG-33B-54	GW Grab				
			PGG-33B-57	GW Grab				
60								

Address: 5700 3rd Ave S
City, State: Seattle, WA
Tax Parcel ID: 172280-1495
Location (TRS): T24N R4W S20; NE1/4 of SW1/4
Lat/Long: N 204856.3 ft, E 1270917 ft
Consulting Firm: Pacific Groundwater Group
Logged by: G. Wallace


Drilling Firm: ESN NW
Drilling Method: Direct Push
Ecology ID: NA
DTW: NA ft bmp
MP Elevation: ~12 ft
V. Datum: NAVD 88
Date: 9/9/2008

Figure
Boring Log
PGG-33B

Blaser Die Casting
Remedial Investigation
JK0504.03

PGG

Depth (ft)	Graphic Log	Unit	Samples: Sample ID	Samples: Type	Samples: Rec/Att	Samples: Blows	Description	Well Construction
0								
5								Hydropunch, 2" diameter
10			PGG-37-10	GW Grab				Backfilled with 3/8-inch bentonite chips
15			PGG-37-15	GW Grab				
20			PGG-37-19	GW Grab				
25			PGG-37-24	GW Grab				



Address: 5700 3rd Ave S
City, State: Seattle, WA
Tax Parcel ID: 172280-1495
Location (TRS): T24N R4W S20; NE1/4 of SW1/4
Lat/Long: N 204755 ft, E 1270625 ft
Consulting Firm: Pacific Groundwater Group
Logged by: G. Wallace

Drilling Firm: ESN NW
Drilling Method: Direct Push
Ecology ID: NA
DTW: NA ft bmp
MP Elevation: ~12 ft
V. Datum: NAVD 88
Date: 9/8/2008

Figure
Boring Log
PGG-37

Blaser Die Casting
Remedial Investigation
JK0504.03

PGG

Depth (ft)	Graphic Log	Unit	Samples: Sample ID	Samples: Type	Samples: Rec/Att	Samples: Blows	Description	Well Construction
30			PGG-37-30	GW Grab				
35			PGG-37-34	GW Grab				
			PGG-37-37	GW Grab				
40								Hydropunch, 2" diameter
			PGG-37-42	GW Grab				
45								Backfilled with 3/8-inch bentonite chips
			PGG-37-46	GW Grab				
50			PGG-37-50	GW Grab				
55			PGG-37-54	GW Grab				
			PGG-37-57	GW Grab				
60								


Address: 5700 3rd Ave S
City, State: Seattle, WA
Tax Parcel ID: 172280-1495
Location (TRS): T24N R4W S20; NE1/4 of SW1/4
Lat/Long: N 204755 ft, E 1270625 ft
Consulting Firm: Pacific Groundwater Group
Logged by: G. Wallace

Drilling Firm: ESN NW
Drilling Method: Direct Push
Ecology ID: NA
DTW: NA ft bmp
MP Elevation: ~12 ft
V. Datum: NAVD 88
Date: 9/8/2008

Figure
Boring Log
PGG-37

Blaser Die Casting
Remedial Investigation
JK0504.03

PGG

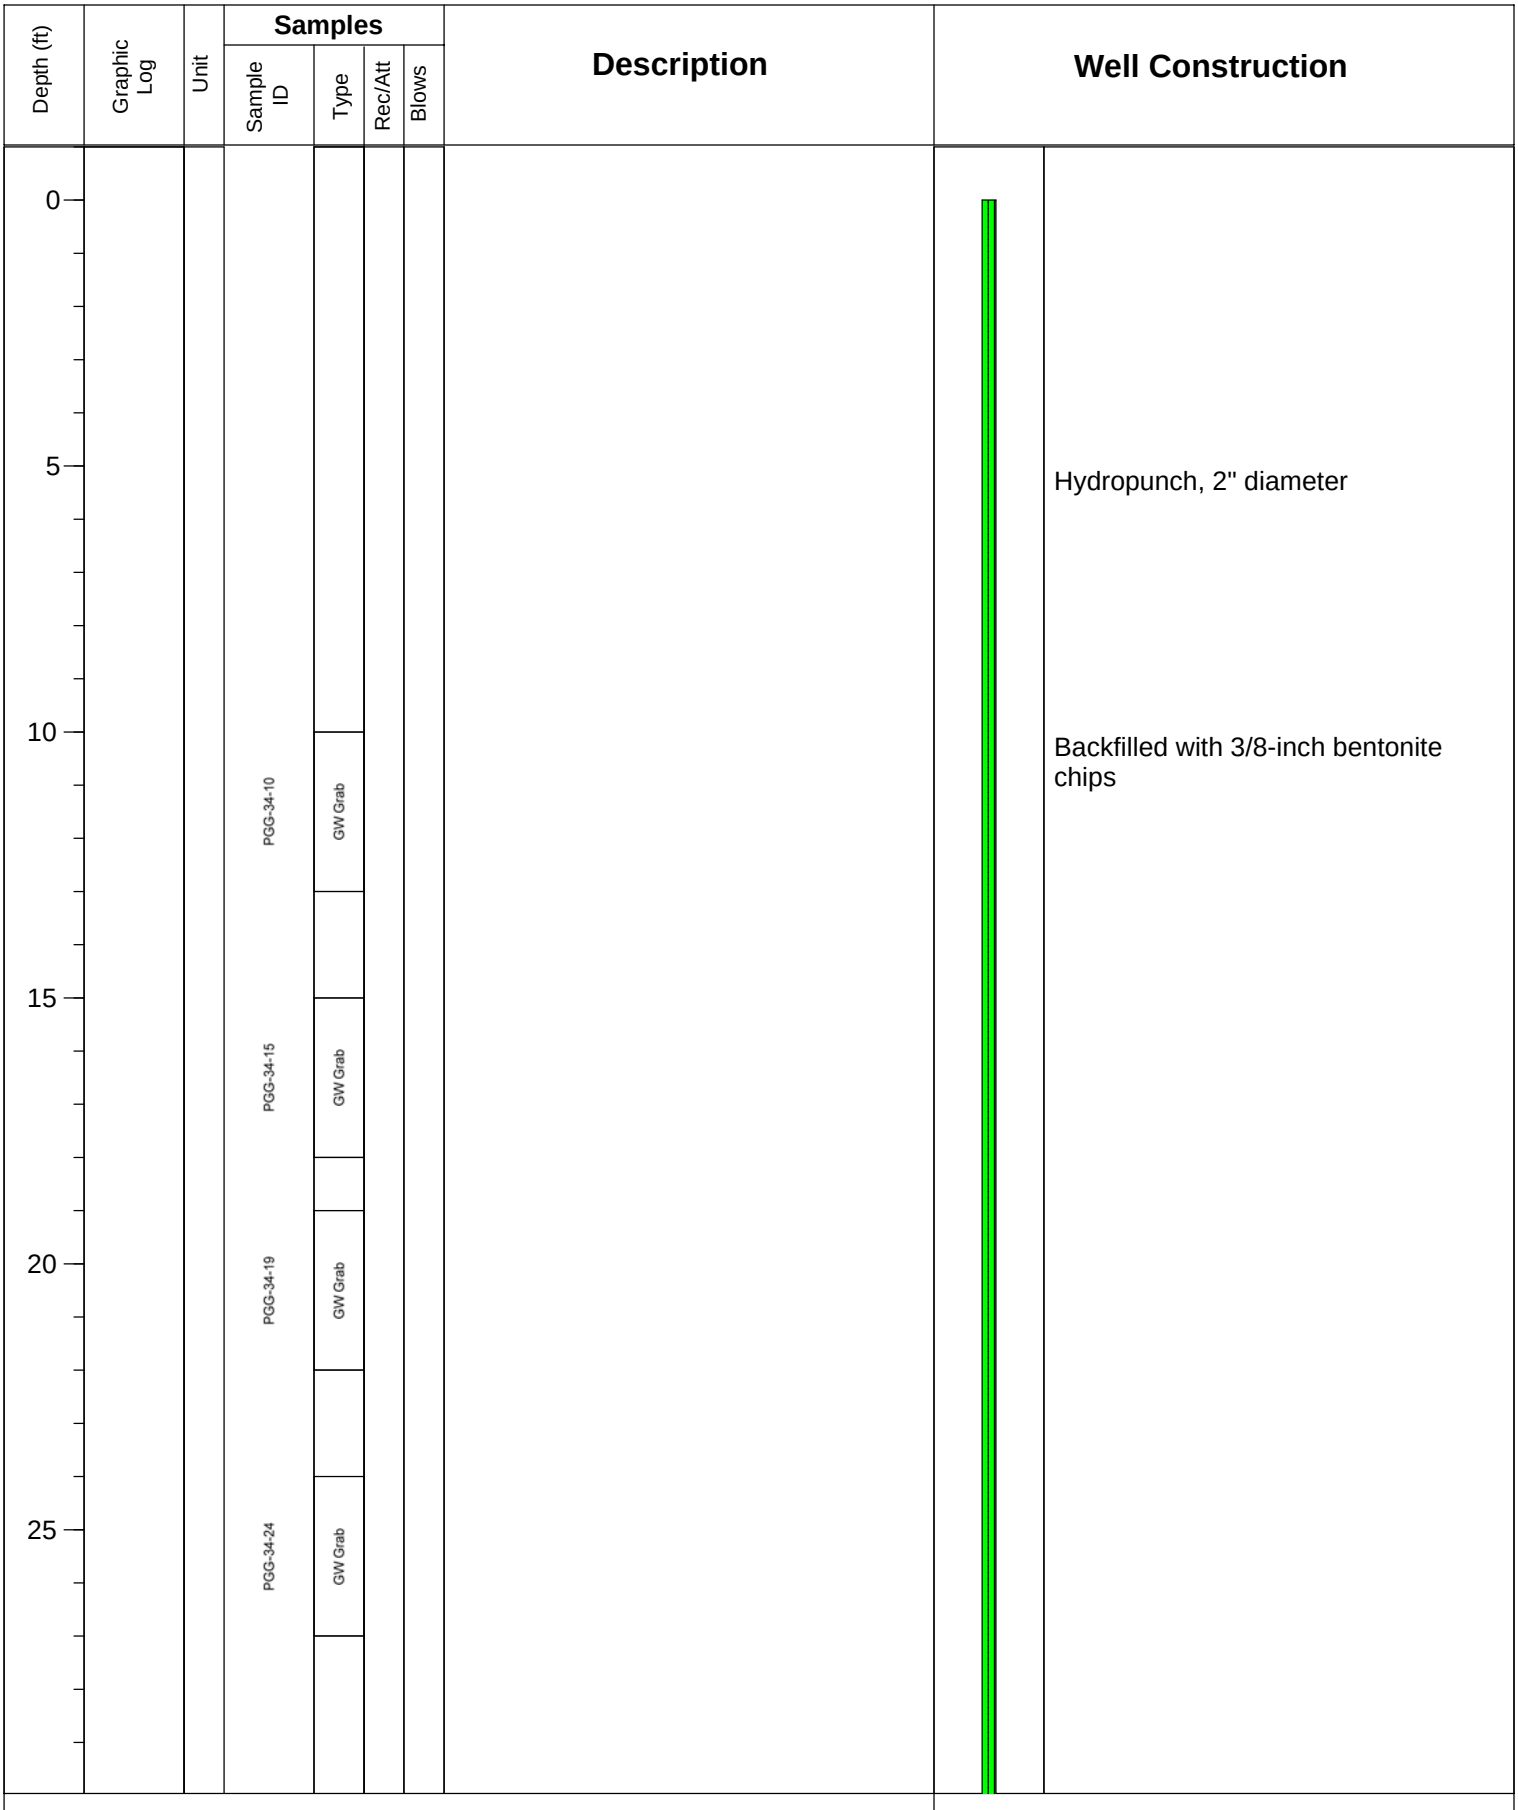

Address: 5700 3rd Ave S
City, State: Seattle, WA
Tax Parcel ID: 172280-1495
Location (TRS): T24N R4W S20; NE1/4 of SW1/4
Lat/Long: N 204795.8 ft, E 1270917 ft
Consulting Firm: Pacific Groundwater Group
Logged by: G. Wallace

Drilling Firm: ESN NW
Drilling Method: Direct Push
Ecology ID: NA
DTW: NA ft bmp
MP Elevation: ~12 ft
V. Datum: NAVD 88
Date: 9/9/2008

Figure
Boring Log
PGG-34

Blaser Die Casting
Remedial Investigation
JK0504.03

PGG

Depth (ft)	Graphic Log	Unit	Samples: Sample ID	Samples: Type	Samples: Rec/Att	Samples: Blows	Description	Well Construction
30			PGG-34-30	GW Grab				
35			PGG-34-34	GW Grab				
			PGG-34-37	GW Grab				
40								Hydropunch, 2" diameter
			PGG-34-42	GW Grab				
45								Backfilled with 3/8-inch bentonite chips
			PGG-34-46	GW Grab				
50			PGG-34-50	GW Grab				
55			PGG-34-54	GW Grab				
			PGG-34-57	GW Grab				
60								


Address: 5700 3rd Ave S
City, State: Seattle, WA
Tax Parcel ID: 172280-1495
Location (TRS): T24N R4W S20; NE1/4 of SW1/4
Lat/Long: N 204795.8 ft, E 1270917 ft
Consulting Firm: Pacific Groundwater Group
Logged by: G. Wallace

Drilling Firm: ESN NW
Drilling Method: Direct Push
Ecology ID: NA
DTW: NA ft bmp
MP Elevation: ~12 ft
V. Datum: NAVD 88
Date: 9/9/2008

Figure
Boring Log
PGG-34

Blaser Die Casting
Remedial Investigation
JK0504.03

PgG

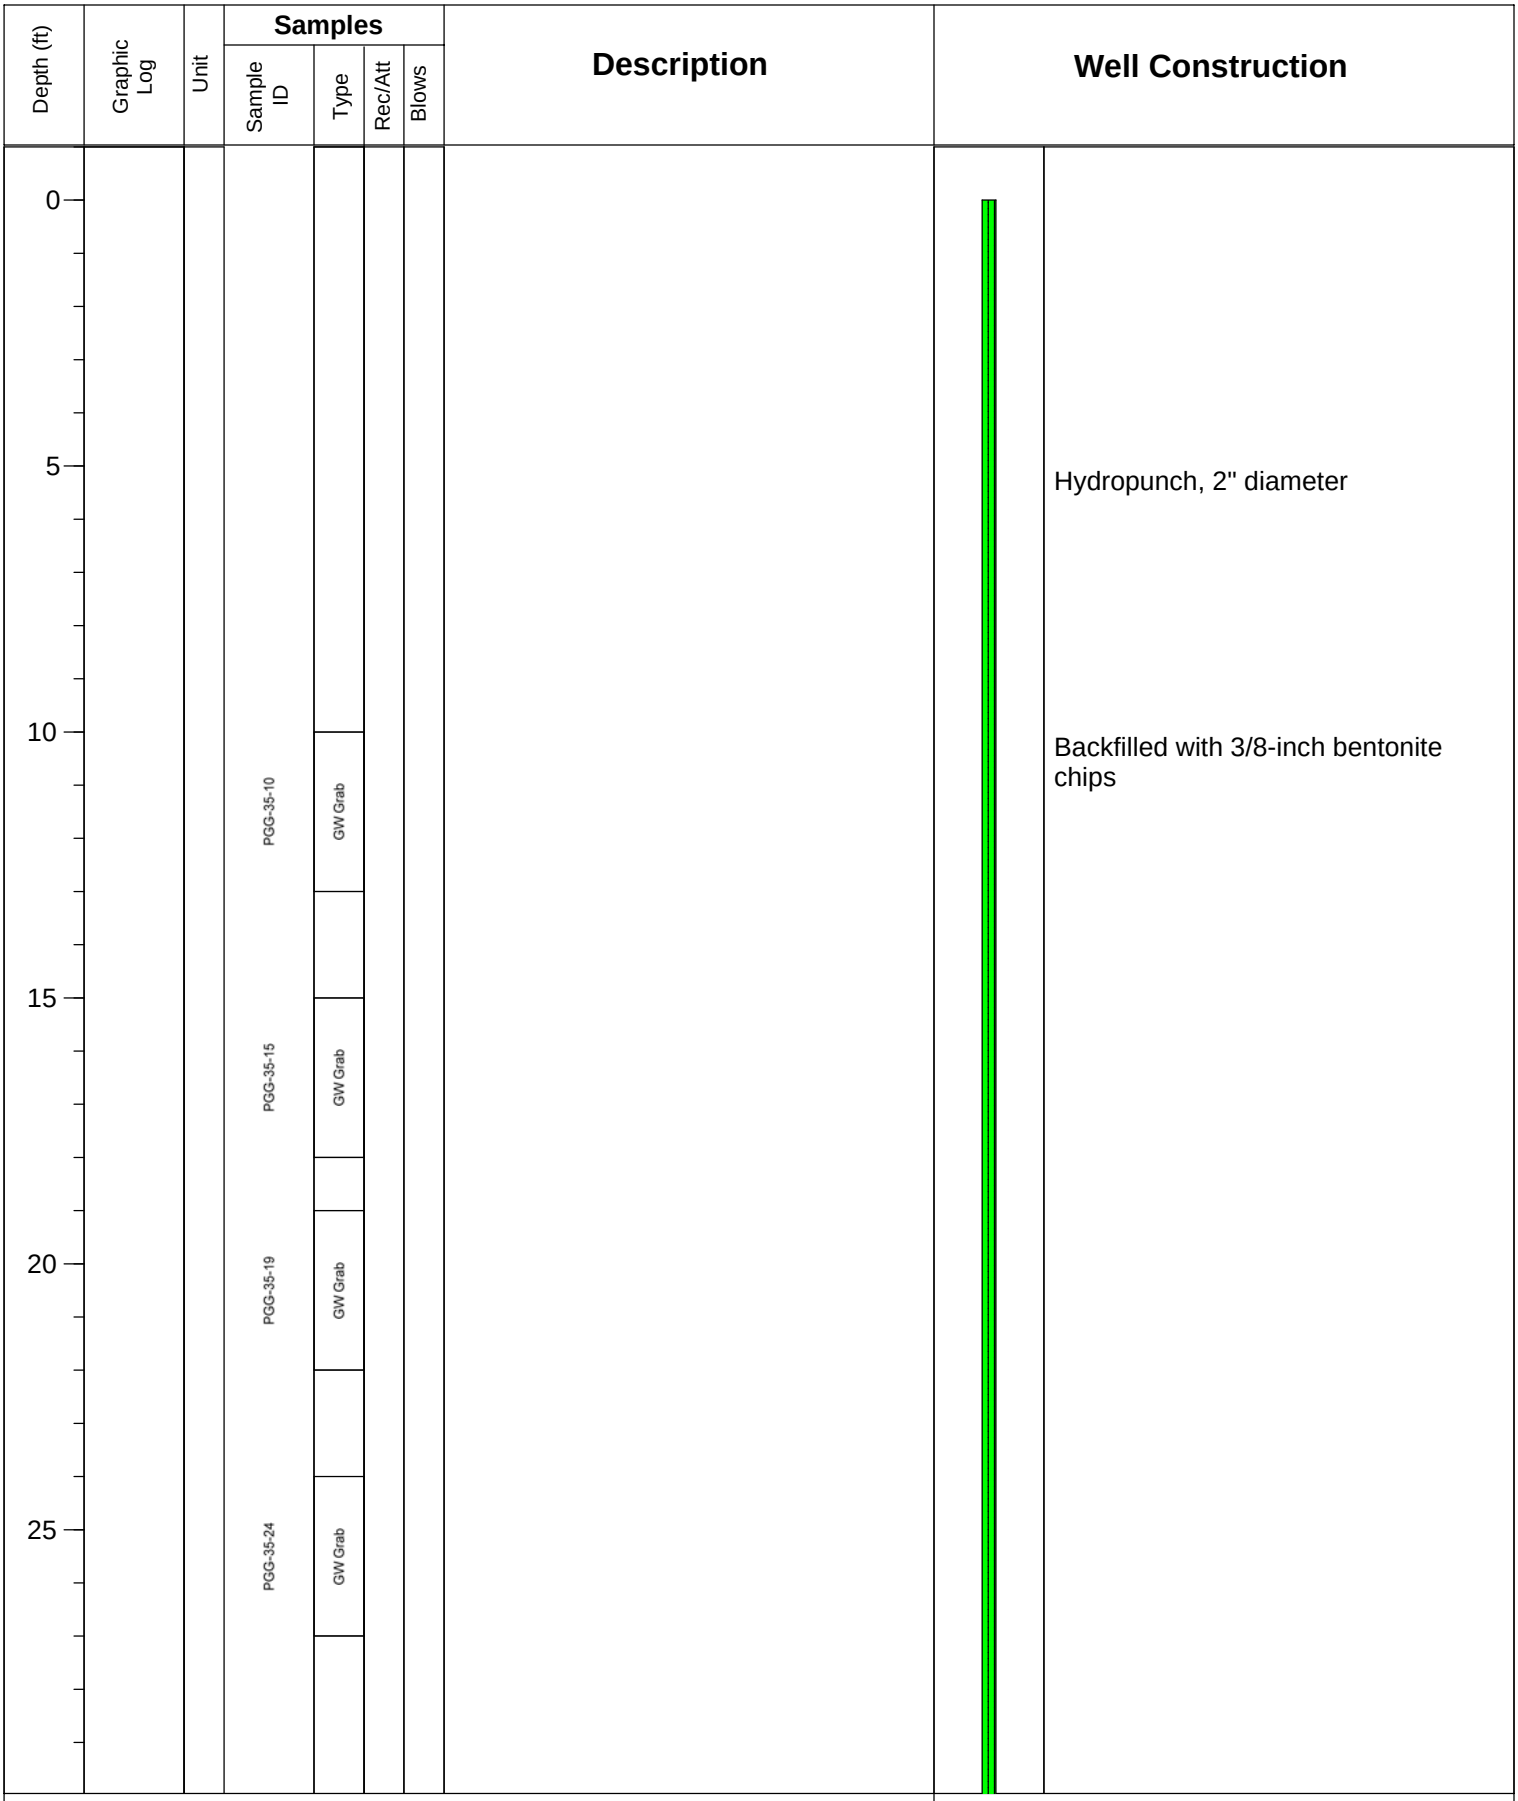

Address: 5700 3rd Ave S
City, State: Seattle, WA
Tax Parcel ID: 172280-1495
Location (TRS): T24N R4W S20; NE1/4 of SW1/4
Lat/Long: N 204737.9 ft, E 1270945 ft
Consulting Firm: Pacific Groundwater Group
Logged by: G. Wallace

Drilling Firm: ESN NW
Drilling Method: Direct Push
Ecology ID: NA
DTW: NA ft bmp
MP Elevation: ~12 ft
V. Datum: NAVD 88
Date: 9/9/2008

Figure
Boring Log
PGG-35

Blaser Die Casting
Remedial Investigation
JK0504.03

PGG

Depth (ft)	Graphic Log	Unit	Samples: Sample ID	Samples: Type	Samples: Rec/Att	Samples: Blows	Description	Well Construction
30			PGG-35-30	GW Grab				
35			PGG-35-34	GW Grab				
			PGG-35-37	GW Grab				
40								Hydropunch, 2" diameter
			PGG-35-42	GW Grab				
45								Backfilled with 3/8-inch bentonite chips
			PGG-35-46	GW Grab				
50			PGG-35-50	GW Grab				
55			PGG-35-54	GW Grab				
			PGG-35-57	GW Grab				
60								

Address: 5700 3rd Ave S
City, State: Seattle, WA
Tax Parcel ID: 172280-1495
Location (TRS): T24N R4W S20; NE1/4 of SW1/4
Lat/Long: N 204737.9 ft, E 1270945 ft
Consulting Firm: Pacific Groundwater Group
Logged by: G. Wallace

Drilling Firm: ESN NW
Drilling Method: Direct Push
Ecology ID: NA
DTW: NA ft bmp
MP Elevation: ~12 ft
V. Datum: NAVD 88
Date: 9/9/2008

Figure
Boring Log
PGG-35

Blaser Die Casting
Remedial Investigation
JK0504.03

PGG

Depth (ft)	Graphic Log	Unit	Samples: Sample ID	Samples: Type	Samples: Rec/Att	Samples: Blows	Description	Well Construction
0								
5								Hydropunch, 2" diameter
10			PGG-38-10	GW Grab				Backfilled with 3/8-inch bentonite chips
15								Total Depth = 13 ft
20								
25								
30								

Address: 5700 3rd Ave S
City, State: Seattle, WA
Tax Parcel ID: 172280-1495
Location (TRS): T24N R4W S20; NE1/4 of SW1/4
Lat/Long: N 204739 ft, E 1270711 ft
Consulting Firm: Pacific Groundwater Group
Logged by: G. Wallace


Drilling Firm: ESN NW
Drilling Method: Direct Push
Ecology ID: NA
DTW: NA ft bmp
MP Elevation: ~12 ft
V. Datum: NAVD 88
Date: 9/8/2008

Figure
Boring Log
PGG-38

Blaser Die Casting
Remedial Investigation
JK0504.03

PgG

[This Page Intentionally Left Blank]

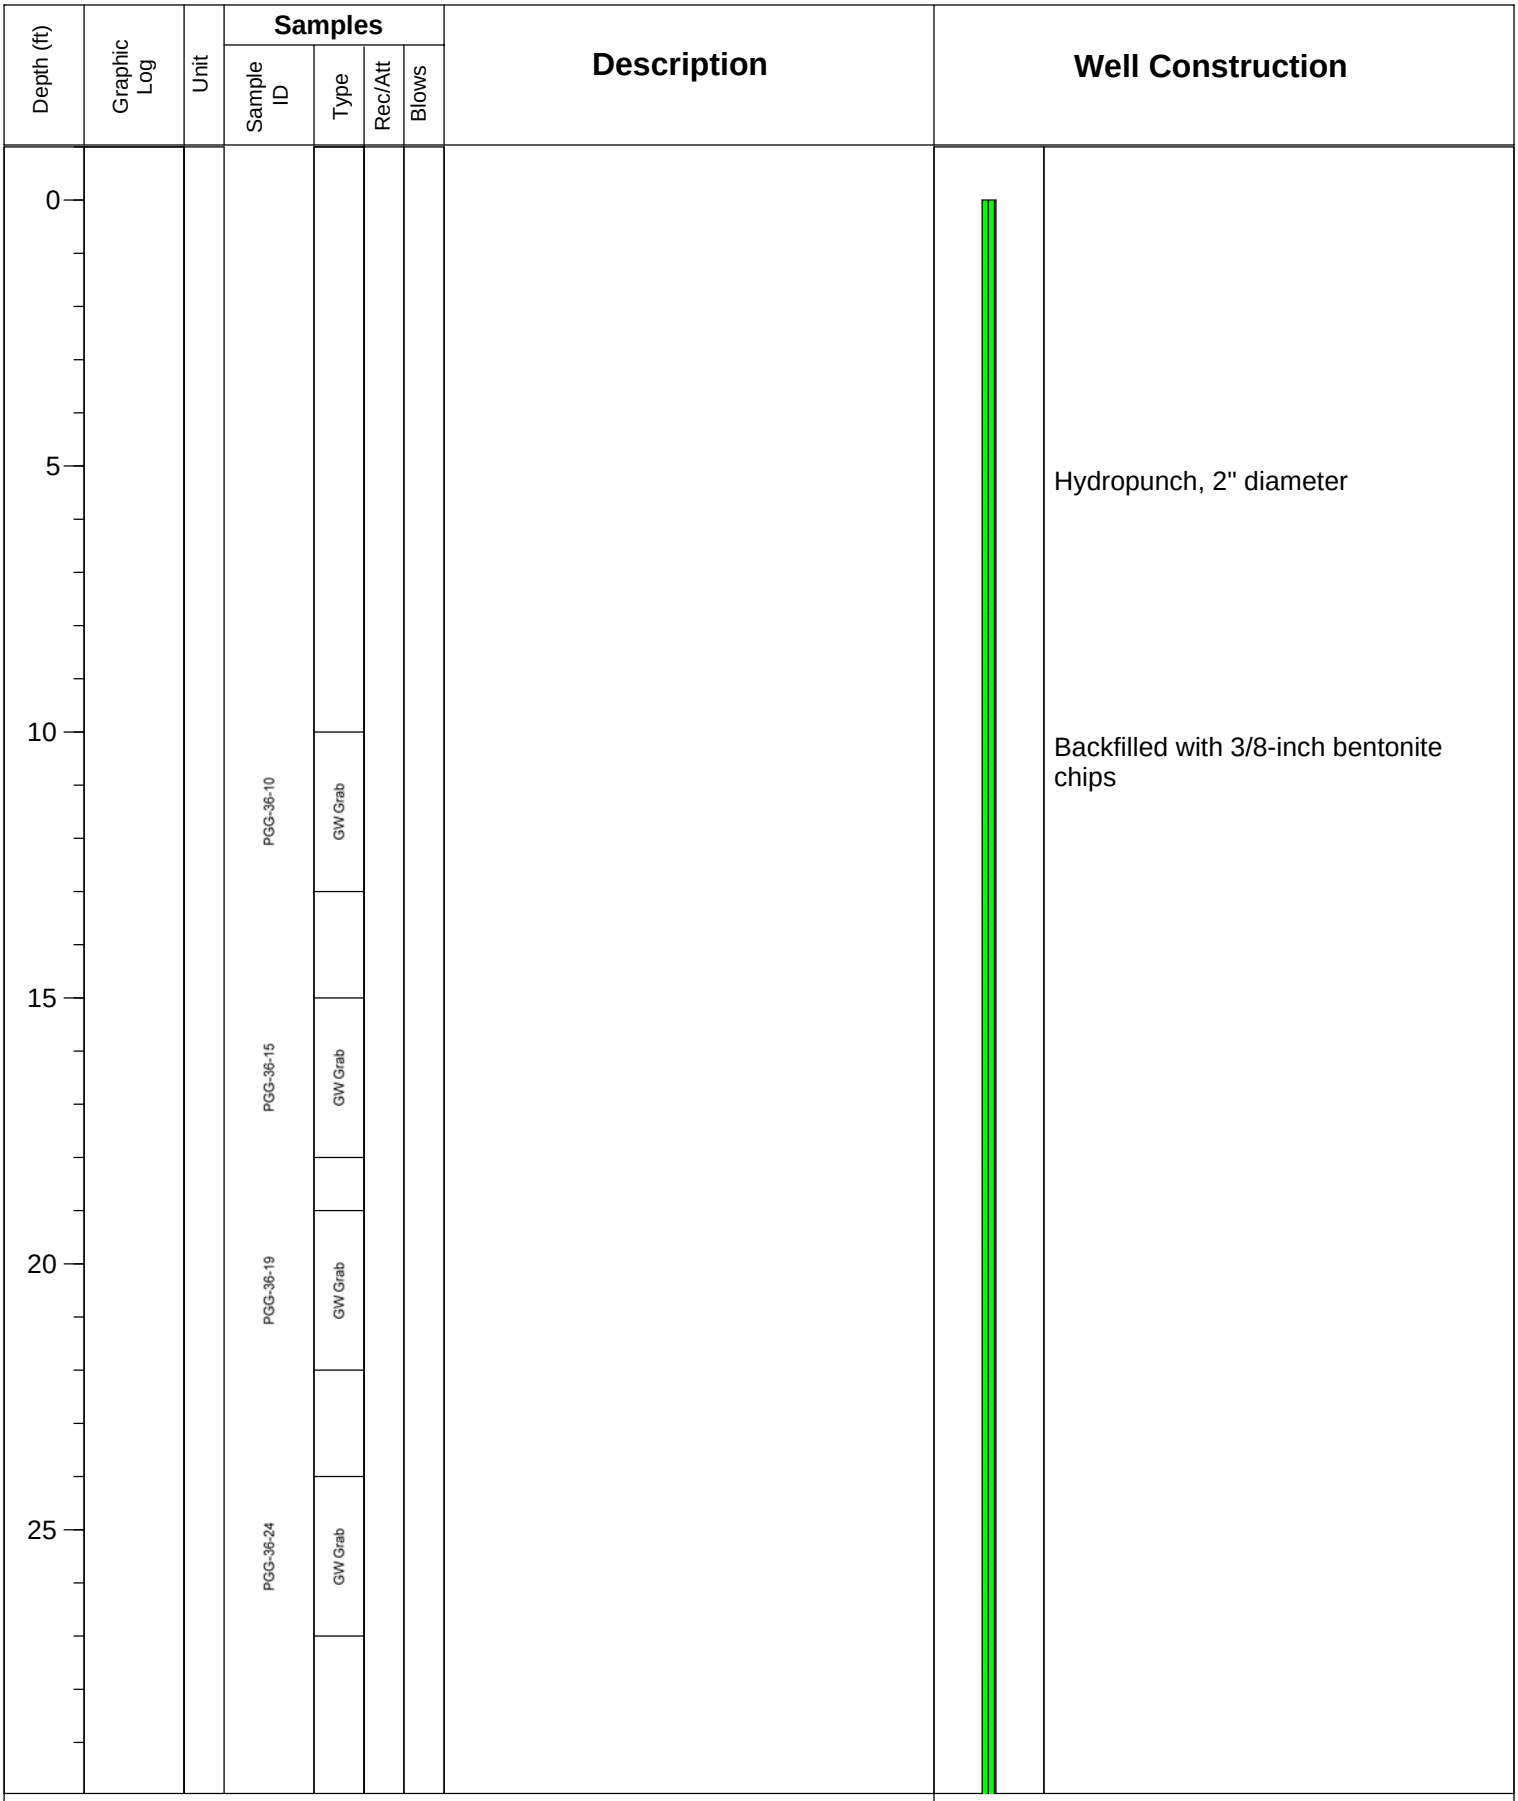

Address: 5700 3rd Ave S
City, State: Seattle, WA
Tax Parcel ID: 172280-1495
Location (TRS): T24N R4W S20; NE1/4 of SW1/4
Lat/Long: N 204770.5 ft, E 1270589 ft
Consulting Firm: Pacific Groundwater Group
Logged by: G. Wallace

Drilling Firm: ESN NW
Drilling Method: Direct Push
Ecology ID: NA
DTW: NA ft bmp
MP Elevation: ~12 ft
V. Datum: NAVD 88
Date: 9/9/2008

Figure
Boring Log
PGG-36

Blaser Die Casting
Remedial Investigation
JK0504.03

PGG

Depth (ft)	Graphic Log	Unit	Samples: Sample ID	Samples: Type	Samples: Rec/Att	Samples: Blows	Description	Well Construction
30			PGG-36-30	GW Grab				
35			PGG-36-34	GW Grab				
			PGG-36-37	GW Grab				
40								Hydropunch, 2" diameter
			PGG-36-42	GW Grab				
45								Backfilled with 3/8-inch bentonite chips
			PGG-36-46	GW Grab				
50			PGG-36-50	GW Grab				
55			PGG-36-54	GW Grab				
			PGG-36-57	GW Grab				
60								

Address: 5700 3rd Ave S
City, State: Seattle, WA
Tax Parcel ID: 172280-1495
Location (TRS): T24N R4W S20; NE1/4 of SW1/4
Lat/Long: N 204770.5 ft, E 1270589 ft
Consulting Firm: Pacific Groundwater Group
Logged by: G. Wallace

Drilling Firm: ESN NW
Drilling Method: Direct Push
Ecology ID: NA
DTW: NA ft bmp
MP Elevation: ~12 ft
V. Datum: NAVD 88
Date: 9/9/2008

Figure
Boring Log
PGG-36

Blaser Die Casting
Remedial Investigation
JK0504.03

PGG

Depth (ft)	Graphic Log	Unit	Samples: Sample ID	Samples: Type	Samples: Rec/Att	Samples: Blows	Description	Well Construction
0								
5								Hydropunch, 2" diameter
10			PGG-39-10	GW Grab				Backfilled with 3/8-inch bentonite chips
15								Total Depth = 13 ft
20								
25								
30								

Address: 5700 3rd Ave S
City, State: Seattle, WA
Tax Parcel ID: 172280-1495
Location (TRS): T24N R4W S20; NE1/4 of SW1/4
Lat/Long: N 204758.7 ft, E 1270851 ft
Consulting Firm: Pacific Groundwater Group
Logged by: G. Wallace


Drilling Firm: ESN NW
Drilling Method: Direct Push
Ecology ID: NA
DTW: NA ft bmp
MP Elevation: ~12 ft
V. Datum: NAVD 88
Date: 9/9/2008

Figure
Boring Log
PGG-39

Blaser Die Casting
Remedial Investigation
JK0504.03

PgG

[This Page Intentionally Left Blank]

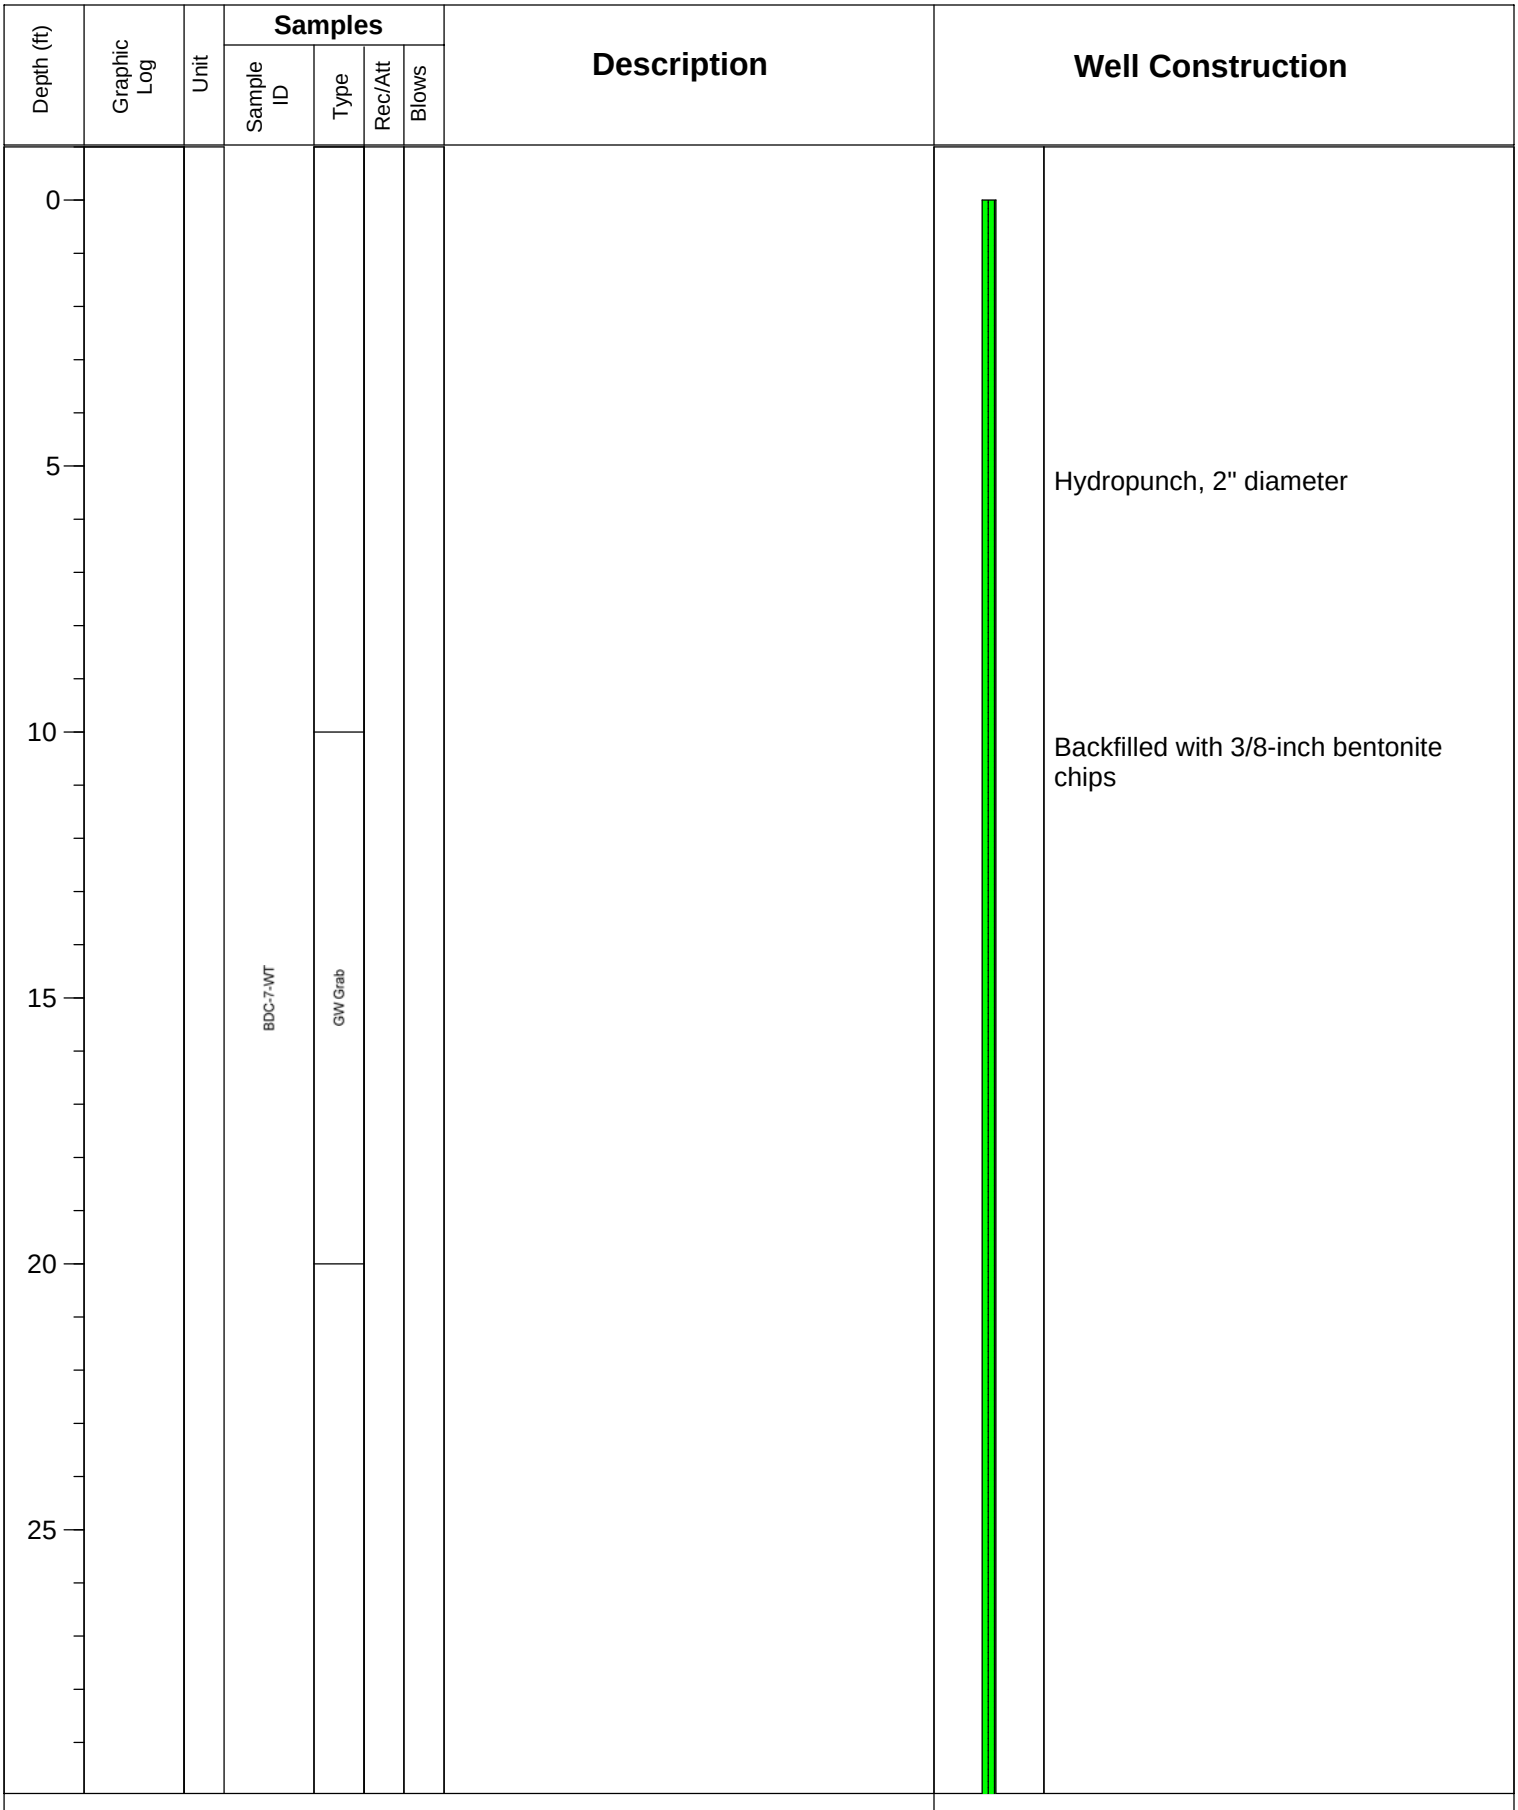

Address: 5700 3rd Ave S
City, State: Seattle, WA
Tax Parcel ID: 172280-1495
Location (TRS): T24N R4W S20; NE1/4 of SW1/4
Lat/Long: N 204730.2 ft, E 1270643.9 ft
Consulting Firm: Pacific Groundwater Group
Logged by: G. Wallace

Drilling Firm: ESN NW
Drilling Method: Direct Push
Ecology ID: NA
DTW: NA ft bmp
MP Elevation: ~15 ft
V. Datum: NAVD 88
Date: 11/16/2009

Figure
Boring Log
BDC-7

Blaser Die Casting
Remedial Investigation
JK0504.03

PgG

Depth (ft)	Graphic Log	Unit	Samples: Sample ID	Samples: Type	Samples: Rec/Att	Samples: Blows	Description	Well Construction
30			BDC-7-40A	GW Grab				
35			BDC-7-40B	GW Grab				
			BDC-7-40C	GW Grab				
40								Hydropunch, 2" diameter
45								Backfilled with 3/8-inch bentonite chips
50			BDC-7-60A	GW Grab				
55			BDC-7-60B	GW Grab				
			BDC-7-60C	GW Grab				
60								Total Depth = 60 ft


Address: 5700 3rd Ave S
City, State: Seattle, WA
Tax Parcel ID: 172280-1495
Location (TRS): T24N R4W S20; NE1/4 of SW1/4
Lat/Long: N 204730.2 ft, E 1270643.9 ft
Consulting Firm: Pacific Groundwater Group
Logged by: G. Wallace

Drilling Firm: ESN NW
Drilling Method: Direct Push
Ecology ID: NA
DTW: NA ft bmp
MP Elevation: ~15 ft
V. Datum: NAVD 88
Date: 11/16/2009

Figure
Boring Log
BDC-7

Blaser Die Casting
Remedial Investigation
JK0504.03

PgG

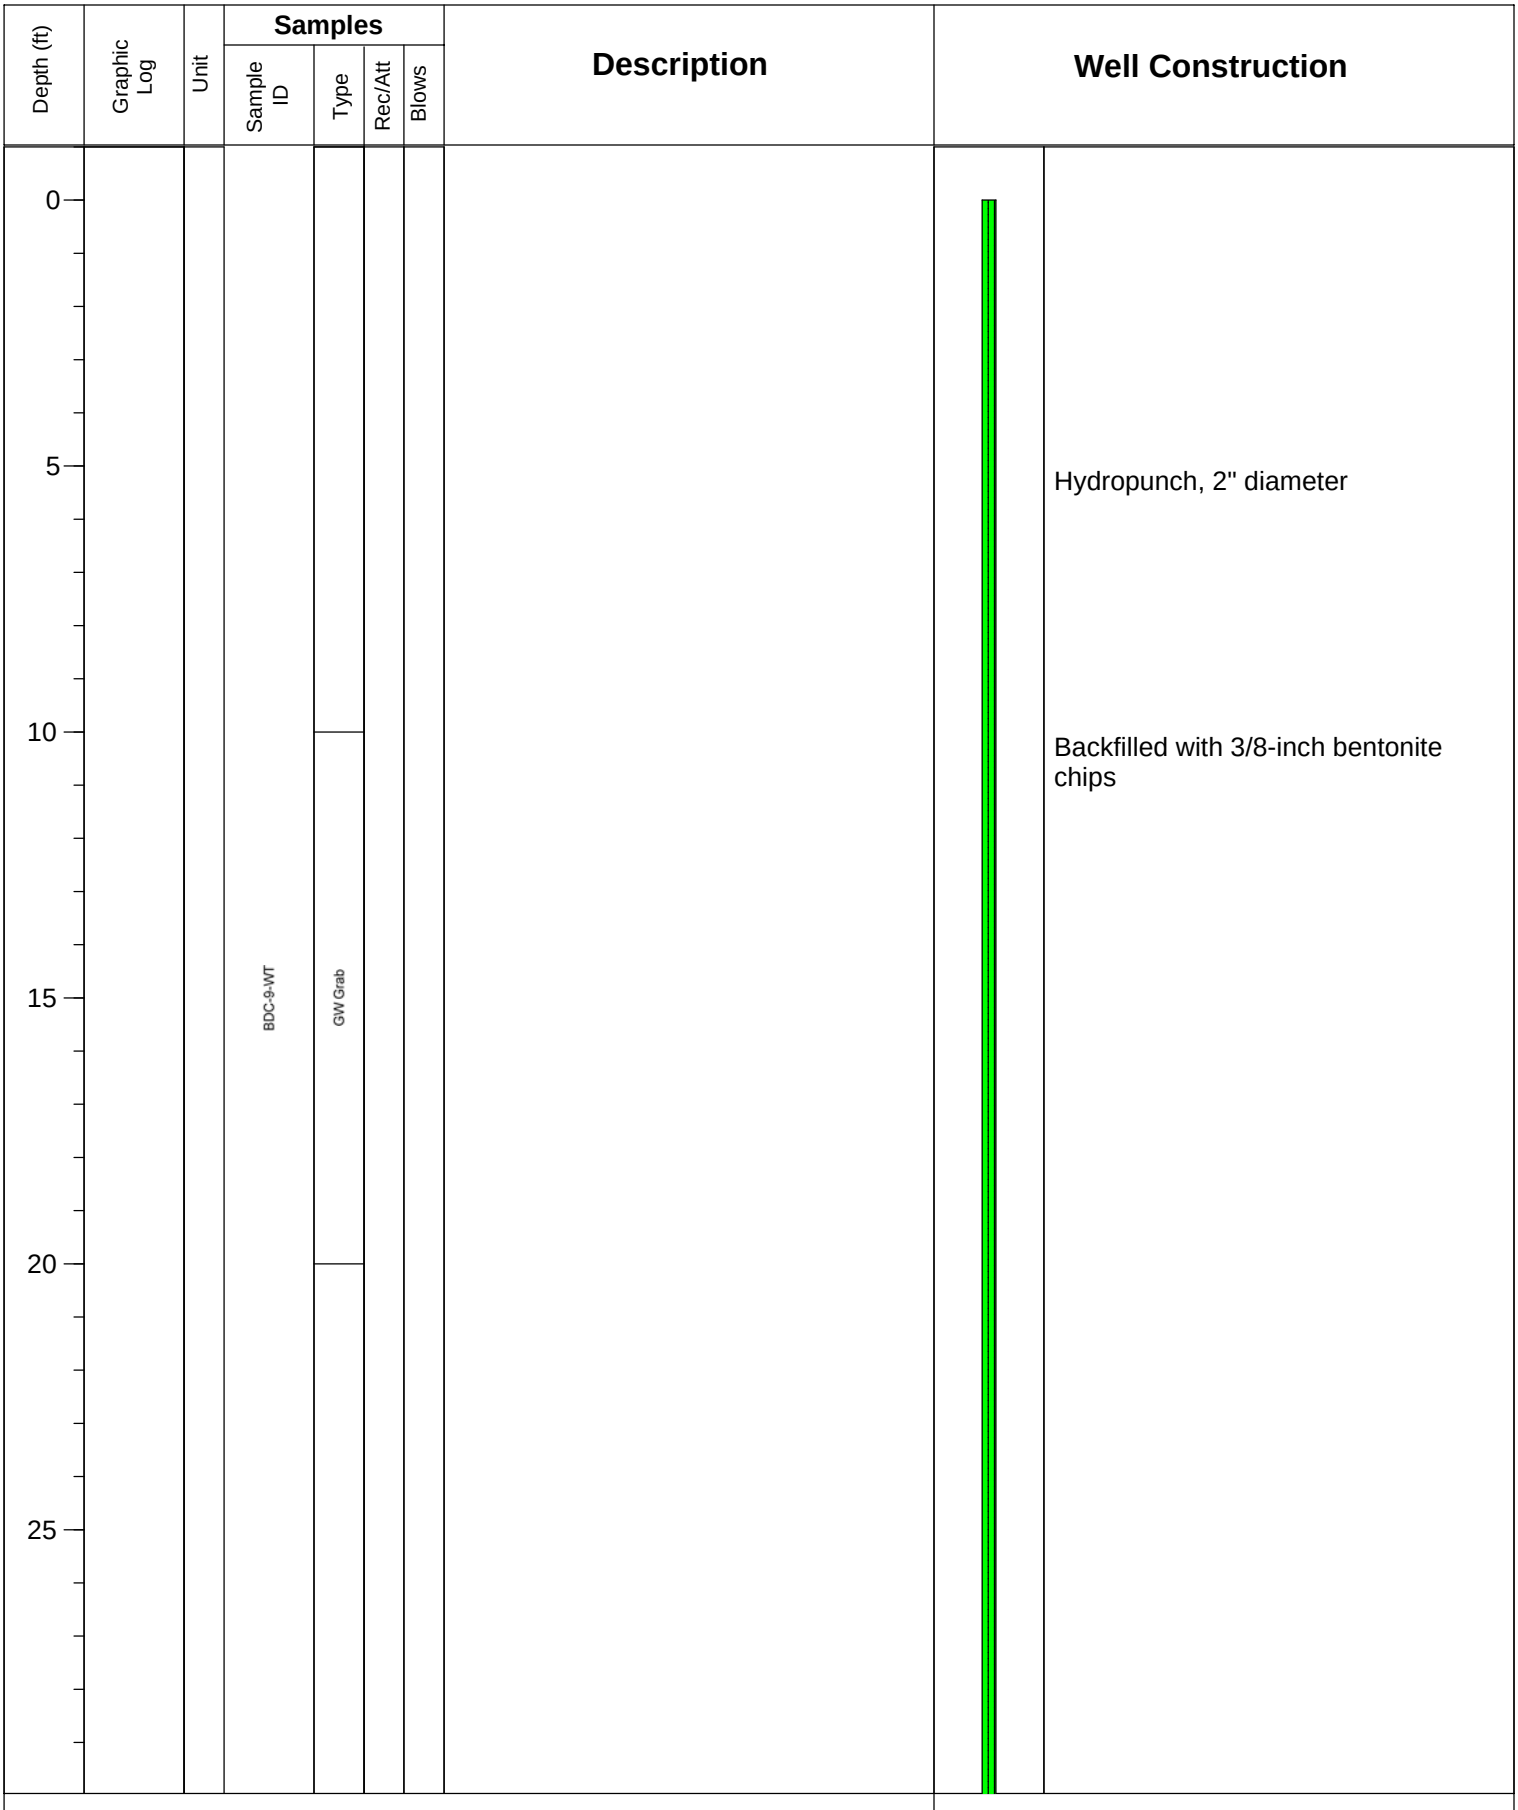

Address: 202-228 S Mead St
City, State: Seattle, WA
Tax Parcel ID: 172280-1750
Location (TRS): T24N R4W S20; NE1/4 of SW1/4
Lat/Long: N 204751.5 ft, E1270563.5 ft
Consulting Firm: Pacific Groundwater Group
Logged by: G. Wallace

Drilling Firm: ESN NW
Drilling Method: Direct Push
Ecology ID: NA
DTW: NA ft bmp
MP Elevation: ~15 ft
V. Datum: NAVD 88
Date: 11/16/2009

Figure
Boring Log
BDC-9

Blaser Die Casting
Remedial Investigation
JK0504.03

PgG

Depth (ft)	Graphic Log	Unit	Samples: Sample ID	Samples: Type	Samples: Rec/Att	Samples: Blows	Description	Well Construction
30			BDC-9-40A	GW Grab				
35			BDC-9-40B	GW Grab				
			BDC-9-40C	GW Grab				
40								Hydropunch, 2" diameter
45								Backfilled with 3/8-inch bentonite chips
50			BDC-9-60A	GW Grab				
55			BDC-9-60B	GW Grab				
			BDC-9-60C	GW Grab				Total Depth = 60 ft
60								

Address: 202-228 S Mead St
City, State: Seattle, WA
Tax Parcel ID: 172280-1750
Location (TRS): T24N R4W S20; NE1/4 of SW1/4
Lat/Long: N 204751.5 ft, E1270563.5 ft
Consulting Firm: Pacific Groundwater Group
Logged by: G. Wallace

Drilling Firm: ESN NW
Drilling Method: Direct Push
Ecology ID: NA
DTW: NA ft bmp
MP Elevation: ~15 ft
V. Datum: NAVD 88
Date: 11/16/2009

Figure
Boring Log
BDC-9

Blaser Die Casting
Remedial Investigation
JK0504.03

PgG

Depth (ft)	Graphic Log	Unit	Samples: Sample ID	Samples: Type	Samples: Rec/Att	Samples: Blows	Description	Well Construction
0								
5								Hydropunch, 2" diameter
10								Backfilled with 3/8-inch bentonite chips
15								
20								
25								

Address: S Mead St
City, State: Seattle, WA
Tax Parcel ID: NA
Location (TRS): T24N R4W S20; NE1/4 of SW1/4
Lat/Long: N 204648 ft, E1270215 ft
Consulting Firm: Pacific Groundwater Group
Logged by: G. Wallace

Drilling Firm: ESN NW
Drilling Method: Direct Push
Ecology ID: NA
DTW: NA ft bmp
MP Elevation: NA
V. Datum: NAVD 88
Date: 4/10/2012

Figure
Boring Log
BDC-12-40

Blaser Die Casting
Remedial Investigation
JK0504.03

PgG

Depth (ft)	Graphic Log	Unit	Samples: Sample ID	Samples: Type	Samples: Rec/Att	Samples: Blows	Description	Well Construction
30								
35			BDC-12-40	GW Grab				
40								Total Depth = 40 ft
45								
50								
55								
60								

Address: S Mead St
City, State: Seattle, WA
Tax Parcel ID: NA
Location (TRS): T24N R4W S20; NE1/4 of SW1/4
Lat/Long: N 204648 ft, E1270215 ft
Consulting Firm: Pacific Groundwater Group
Logged by: G. Wallace

Drilling Firm: ESN NW
Drilling Method: Direct Push
Ecology ID: NA
DTW: NA ft bmp
MP Elevation: NA
V. Datum: NAVD 88
Date: 4/10/2012

Figure
Boring Log
BDC-12-40

Blaser Die Casting
Remedial Investigation
JK0504.03

PgG

Depth (ft)	Graphic Log	Unit	Samples: Sample ID	Samples: Type	Samples: Rec/Att	Samples: Blows	Description	Well Construction
0								
5								Hydropunch, 2" diameter
10								Backfilled with 3/8-inch bentonite chips
15								
20								
25								

Address: 5700 3rd Ave S
City, State: Seattle, WA
Tax Parcel ID: 172280-1495
Location (TRS): T24N R4W S20; NE1/4 of SW1/4
Lat/Long: N 20467 ft, E 1270620 ft
Consulting Firm: Pacific Groundwater Group
Logged by: G. Wallace

Drilling Firm: ESN NW
Drilling Method: Direct Push
Ecology ID: NA
DTW: NA ft bmp
MP Elevation: ~15 ft
V. Datum: NAVD 88
Date: 11/16/2009

Figure
Boring Log
CG-136-60

Blaser Die Casting
Remedial Investigation
JK0504.03

PgG

Depth (ft)	Graphic Log	Unit	Samples: Sample ID	Samples: Type	Samples: Rec/Att	Samples: Blows	Description	Well Construction
30								
35								
40								Hydropunch, 2" diameter
45								Backfilled with 3/8-inch bentonite chips
50			CG-136-60A	GW Grab				
55			CG-136-60B	GW Grab				
60			CG-136-60C	GW Grab				Total Depth = 60 ft

Address: 5700 3rd Ave S
City, State: Seattle, WA
Tax Parcel ID: 172280-1495
Location (TRS): T24N R4W S20; NE1/4 of SW1/4
Lat/Long: N 20467 ft, E 1270620 ft
Consulting Firm: Pacific Groundwater Group
Logged by: G. Wallace

Drilling Firm: ESN NW
Drilling Method: Direct Push
Ecology ID: NA
DTW: NA ft bmp
MP Elevation: ~15 ft
V. Datum: NAVD 88
Date: 11/16/2009

Figure
Boring Log
CG-136-60

Blaser Die Casting
Remedial Investigation
JK0504.03

PgG

Depth (ft)	Graphic Log	Unit	Samples: Sample ID	Samples: Type	Samples: Rec/Att	Samples: Blows	Description	Well Construction
0								
5								Hydropunch, 2" diameter
10								Backfilled with 3/8-inch bentonite chips
15								
20								
25								
30								
35								

Address: 5700 3rd Ave S
City, State: Seattle, WA
Tax Parcel ID: 172280-1495
Location (TRS): T24N R4W S20; NE1/4 of SW1/4
Lat/Long: N 20470 ft, E 1270623 ft
Consulting Firm: Pacific Groundwater Group
Logged by: G. Wallace

Drilling Firm: ESN NW
Drilling Method: Direct Push
Ecology ID: NA
DTW: NA ft bmp
MP Elevation:
V. Datum: NAVD 88
Date: 5/30/2012

Figure
Boring Log
CG-136

Blaser Die Casting
Remedial Investigation
JK0504.03

PgG

Depth (ft)	Graphic Log	Unit	Samples: Sample ID	Samples: Type	Samples: Rec/Att	Samples: Blows	Description	Well Construction
40								Hydropunch, 2" diameter
45								Backfilled with 3/8-inch bentonite chips
50								
55								
60			CG-136-63	GW Grab				
65								
70			CG-136-66	GW Grab				
75			CG-136-73	GW Grab				Total Depth = 76 ft

Address: 5700 3rd Ave S
City, State: Seattle, WA
Tax Parcel ID: 172280-1495
Location (TRS): T24N R4W S20; NE1/4 of SW1/4
Lat/Long: N 20470 ft, E 1270623 ft
Consulting Firm: Pacific Groundwater Group
Logged by: G. Wallace

Drilling Firm: ESN NW
Drilling Method: Direct Push
Ecology ID: NA
DTW: NA ft bmp
MP Elevation:
V. Datum: NAVD 88
Date: 5/30/2012

Figure
Boring Log
CG-136

Blaser Die Casting
Remedial Investigation
JK0504.03

PgG
